

Town of Westford, Massachusetts
12 North Main Street Phase 1 Building Stabilization Project

Addendum Number One
October 28, 2015

The Contract Documents for the Phase 1 Building Stabilization Project- 12 North Main Street issued on October 16, 2015 are replaced in their entirety with the enclosed document entitled Contract Specifications for 12 North Main Street Phase 1 Stabilization Project Graniteville Westford, Massachusetts dated October 28, 2015.

In addition to this new set of contract specifications, a new set of contract drawings has been added to the bid package. This set of contract drawings is titled Phase 1 Building Stabilization 12 North Main Street dated 10/28/2015.

The bid package now consists of the following:

- Contract Specifications 10/28/2015
- Contract Drawings 10/28/2015
- Attachment A - Wage Rates 10/13/2015
- Attachment B - Draft Abatement Work Plan 10/13/2015
- Attachment C - Existing Conditions 10/16/2015

Please confirm receipt of this addendum.

Town Manager's Office
Town of Westford
55 Main Street
Westford, MA 01886
jmangiaratti@westfordma.gov

CONTRACT SPECIFICATIONS FOR

12 NORTH MAIN STREET PHASE 1 STABILIZATION PROJECT GRANITEVILLE WESTFORD, MASSACHUSETTS



Owner:

Town of Westford
55 Main Street
Westford, MA 01886
John S. Mangiaratti, Assistant Town Manager

Architect:

Bargmann Hendrie + Archetype, Inc.
300 A Street
Boston, MA 02210-1710
Tel: 617-350-0450
Fax: 617-350-0215
www.bhplus.com

Structural Engineer:

Structures North Consulting Engineers, Inc.
60 Washington Street, Suite 401
Salem, MA 01970-3517
Tel: 978-745-6817
Fax: 978-745-6067
www.structures-north.com

October 28, 2015

TABLE OF CONTENTS

Section Number

List of Drawings

A001	Cover Sheet
A101	Basement Plan
A102	First Floor Plan
A200	Details
S101	[Structural] Basement Plan
S102	[Structural] First Floor

Bidding And Contract Requirements

Invitation for Bid	00020
Instructions to Bidders	00100
Form of General Bid	00300
Agreement	00500
Construction Performance Bond	00610
Construction Payment Bond	00620
General Conditions	00700
Supplemental General Conditions	00800
Excerpts from Applicable State Law	00850
Advertisement for Bids	001113
Certification of Tax Compliance	
Certificate of Non-Collusion	003003
Reference Forms	003004
Bid Bond	004313
Substitution Request Forms during Bidding	007000 / 007001
Summary	011000
Alternates	012300
Contract Modification Procedures	012500
Bulletin Form	012500a
Payment procedures	012900
Project Management and Coordination	013100
RFI response	013100b
Construction Progress Documentation	013200
Photo Documentation	013220
Submittal Procedures	013300
Submittal Response Template	013300
Quality Requirements	014000
Temporary Facilities and Controls (including Alternate No. 3)	015000
Product Requirements	016000
Substitution Request Form	016100

Execution Requirements	017000
Cutting and Patching	017310
Selective Demolition	017320
Closeout Procedure	017700
Site Clearing	022300
Shoring Bracing and Support	024400
Rough Carpentry	061000

Attachment A – Wage Rates

Attachment B – DRAFT Abatement Work Plan

Attachment C – Existing Conditions (10/16/15)

SECTION 00020

INVITATION FOR BIDS

Sealed bids for Phase 1 Building Stabilization Project - 12 North Main Street will be received at the Office of the Town Manager, Town Hall, 55 Main Street, Westford, MA 01886 until **November 6, 2015 at 2:00 p.m.** at which time the bids will be publicly opened and read:

Specifications and bid forms may be obtained at the Office of the Town Manager Monday through Friday between 8 a.m. and 4 p.m.

Each Bid and filed sub-bid must be accompanied by a bid security consisting of a BID BOND, CASH, or, CERTIFIED CHECK issued by a responsible bank or trust company in the amount of 5% of the bid price.

Pre-Bid Conference and Site Visit will be held at the Highway Facility located at 28 North Main Street, Westford, MA on October 30, 2015 at 10:00a.m. It is imperative that all prospective bidders have a representative in attendance.

A performance bond in an amount equal to 100 percent of the total amount of the contract price with a surety company qualified to do business in the Commonwealth of Massachusetts will be required for the faithful performance of the contract as well as a labor and materials bond in an amount equal to 100 percent of the total contract price.

All bids for this project are subject to applicable public bidding laws of Massachusetts, including G.L. c.149, § 44A through 44H, as amended.

Attention is directed to the minimum wage rates to be paid as determined by the Commissioner of Labor and Workforce Development and the weekly payroll record submittal requirements under the provisions of Massachusetts General Laws, Chapter 149, Section 26 through 27D inclusive.

Attention is further directed to the requirements of G.L. c.149, §44D requiring submission of a Division of Capital Asset Management approved Certificate of Eligibility and Update Statement with all bids.

Selection of the contractor will be based upon bidder qualifications, including evidence of past performance in similar projects, and bid price. The contract will be awarded to the bidder deemed by the awarding authority to be the lowest responsible and eligible bidder.

The bidder agrees that its bid shall be good and may not be withdrawn for a period of 30 days, Saturdays, Sundays and legal holidays excluded, after the opening of the bids.

The Town reserves the right to waive any informalities, to accept or reject, in whole or in part any or all bids, or take whatever other action may be deemed to be in the best interest of the City/Town.

SECTION 00100

INSTRUCTIONS TO BIDDERS

1. Receipt and Opening of Bids

The Town of Westford, Massachusetts, herein called the Owner or Awarding Authority, acting by and through its Board of Selectmen, will receive sealed Bids for the project known as

Phase 1 Building Stabilization Project - 12 North Main Street

This Project is subject to the public bidding statutes, G.L. c. 149, §§44A-44H

General bids similarly addressed to the Town Manager, Westford Town Hall, 55 Main Street, Westford, MA 01886 and endorsed "Bid for Phase 1 Building Stabilization Project - 12 North Main Street" will be received at the Office of the Town Manager until 2:00 p.m. prevailing time, on November 6, 2015, at which time and place said bids will be publicly opened and read aloud.

Any bid may be withdrawn prior to the above scheduled time for the opening of bids or authorized postponement thereof. Any bid received after the time and date specified will not be considered. The bidder agrees that its bid shall be good and may not be withdrawn for a period of 30 days, Saturdays, Sundays, and legal holidays excluded, after the opening of bids.

2. Location and Work to be Done

The Work consists of debris removal, hazardous material abatement, structural reinforcement of historic floor beams, boarding of windows, and stabilization of an historic smoke stack and all work incidental thereto, in accordance with the Specifications and conceptual plans attached hereto.

The location, general characteristics, and principal details of the Work are indicated on plans entitled:

- EXISTING CONDITIONS OF THE FORMER ABBOT WORSTED MILL BUILDING LOCATED AT 12 NORTH MAIN STREET, DATED 10/16/2015
- ABATEMENT WORK PLAN FOR THE ROOFING ABATEMENT PROJECT 12 NORTH MAIN STREET WESTFORD, MASSACHUSETTS, DATED 10/13/2015
- PLANS FOR 12 NORTH MAIN STREET PHASE 1 STABILIZATION PROJECT, DATED 10/28/15

Additional drawings showing details in accordance with which the Work is to be done may be furnished by addendum from time to time during the bidding period by the Owner or its Architect/Engineer, and shall then become a part of the Contract Documents.

The Contractor shall furnish all labor, services, materials, equipment, plant, machinery, apparatus, appliances, tools, supplies, and all other things necessary to do all work required for the completion of each item of the Work and as herein specified.

The Work to be done and paid for under any item shall not be limited to the exact extent mentioned or described but shall include all incidental work necessary or customarily done for the completion of that item.

3. Preparation of Bid

Each bid must be submitted on the prescribed form. All blank spaces for bid prices must be filled in, in ink or typewritten, in both words and figures.

Each bid must be submitted in a sealed envelope bearing on the outside the name of the bidder, his address, and endorsed with the name of the project as specified in Receipt and Opening of Bids, above. If forwarded by mail, the sealed envelope containing the bid must be enclosed in another envelope addressed as specified in Receipt and Opening of Bids, above.

4. Bid Opening Procedure

The following list of requirements shall apply to each filed bid. Bids not meeting all the requirements for timeliness and security will be rejected; bids not meeting signature and addenda requirements will be rejected prior to checking of bid amounts.

Bids shall be filed at the place and before the time specified in Receipt and Opening of Bids, above.

Properly executed bid security shall be placed in a sealed envelope and shall be attached to the outside of the envelope containing the bid.

Bid signatures will be checked.

All addenda will be sent Certified Mail, with return receipt requested, and/or facsimile or e-mail to all prospective bidders.

The total dollar amount of each bid will be read. All those present at the bid opening may examine all bids after the bid opening.

5. Modification

Any bidder may modify his bid by written communication at any time prior to the scheduled closing time for receipt of bids. Any telegraphic communication must be received by the Owner prior to the closing time, and, provided further, the Owner must be satisfied that a written confirmation of the telegraphic modification over the signature of the bidder was mailed prior to the closing time. If written confirmation is not received within two days from the closing time, no consideration will be given to a telegraphic communication.

The communication shall not reveal the bid price but shall provide the addition or subtraction or other modification so that the final prices or terms will not be known by the Owner until the sealed bid is opened.

6. Ability and Experience of Bidder

No award will be made to any bidder who cannot satisfy the Owner that he/she has sufficient ability and experience in this class of work and sufficient capital and plant to enable him to prosecute and complete the work successfully within the time named. The Owner's decision or judgment on these matters will be final, conclusive, and binding.

The Owner may make such investigations as it deems necessary, and the bidder shall furnish to the Owner, under oath if so required, all such information and data for this purpose as the Owner may request.

7. Conditions of Work

Each bidder must familiarize himself/herself fully with the conditions relating to the construction of the project and the employment of labor thereon. Failure to do so will not relieve a successful bidder of his/her obligation to furnish all material and labor necessary to carry out the provisions of his contract. Insofar as possible the Contractor, in carrying out his work, must employ such methods or means as will not cause any interruption of or interference with the work of any other Contractor.

8. Addenda and Interpretations

No interpretation of the meaning of the plans, specifications or other pre-bid documents will be made to any bidder orally. All information given to bidders other than by means of the plans, specifications, or by addenda, as described below, is given informally and shall not be used as the basis of a claim against the Owner.

Every request for such interpretation should be in writing addressed to Jodi Ross, Town Manager, Town Hall 55 Main Street Westford, MA 01886, and to be given consideration must be received at least five days prior to the date fixed for the opening of bids. Any and all such interpretations and any supplemental instructions will be in the form of written addenda to the specifications which, when issued, will be mailed by Certified Mail with return receipt requested to all prospective bidders (at the respective address furnished by them for such purposes), or sent via facsimile or email if time requires. Failure of any bidder to receive any such addendum or interpretation shall not relieve such bidder from any obligation under his bid as submitted. All addenda so issued shall become part of the Contract Documents.

9. Security for Faithful Performance

Simultaneously with his delivery of the executed Contract, the Contractor shall furnish a surety bond or bonds as security for faithful performance of this contract and for the payment of all persons performing labor and materials under this contract as specified in

Section 00700, GENERAL CONDITIONS included herein. The surety on such bond or bonds shall be a surety company qualified to do business under the laws of the Commonwealth and satisfactory to the Owner. The bonds shall remain in force for one year after final acceptance of the work by the Owner, unless the Owner, in writing, releases the Contractor from the obligation sooner.

10. Power of Attorney

Attorneys-in-fact who sign Contract bonds must file with each bond a certified and effectively dated copy of their power of attorney.

11. Laws and Regulations

The bidder's attention is directed to the fact that all applicable State laws, municipal ordinances or bylaws, and the rules and regulations of all authorities having jurisdiction over construction of the project shall apply to the Contract throughout, and they will be deemed to be included in the Contract the same as though written out in full. Attention is directed to Section 00850 and to other applicable sections of the Contract Documents.

12. Liquidated Damages for Failure to Enter into Contract

The successful bidder, upon his failure or refusal to execute and deliver the Contract and bonds required within 10 days after presentation thereof by the Owner, shall forfeit to the Owner, as liquidated damages for such failure or refusal, the security deposited with his/her bid, but the amount forfeited shall not exceed the difference between his/her bid price and the bid price of the next lowest responsible and eligible bidder. In case of death, disability, bona fide clerical or mechanical error of a substantial nature, or other similar unforeseen circumstances affecting the bidder, his/her bid deposit will be returned.

13. Obligation of Bidder

At the time of the opening of bids, each bidder will be presumed to have inspected the site and to have read and to be thoroughly familiar with the Contract Documents (including all addenda). The failure or omission of any bidder to examine any form, instrument, or document shall in no way relieve any bidder from any obligation in respect of his bid.

14. Information Not Guaranteed

All information given in the Contract Documents relating to subsurface and other conditions, natural phenomena, existing pipes, and other structures is from the best sources at present available to the Owner. All such information is furnished only for the information and convenience of bidders and is not guaranteed.

It is agreed and understood that the Owner does not warrant or guarantee that the subsurface or other conditions, natural phenomena, existing pipes, or other structures encountered during construction will be the same as those indicated in the Contract Documents.

If is further agreed and understood that no bidder or Contractor shall use or be entitled to use any of the information made available to him or obtained in any examination made by him in any manner as a basis of or ground for any claim or demand against the Owner or the Architect/Engineer, arising from or by reason of any variance which may exist between the information made available and the actual subsurface or other structures actually encountered during the construction work, except as may otherwise be expressly provided for in the Contract Documents.

15. Bid Security

Each bid and sub-bid must be accompanied by bid security in the form of a certified check, a bid bond, cash, or a treasurer's or cashier's check, payable to the Owner, in the amount of five (5) percent of the value of the bid. Such security of general bidders will be returned to all except the three lowest responsible and eligible bidders within five days, Saturdays, Sundays, and legal holidays excluded, after the opening of bids, and the remaining securities will be returned promptly after the Owner and the accepted bidder have executed the Contract, or if no notice of intent to award has been presented to the selected contractor within 30 days, Saturdays, Sundays and holidays excluded, after the date of the opening of bids, upon demand of the bidder at any time thereafter. Bid security of sub-bidders, except that of the sub-bidders named in the general bids of the three lowest responsible and eligible general bidders and those of the three lowest responsible and eligible sub-bidders for each sub-trade, shall be returned within five (5) days, Saturdays, Sundays and legal holidays excluded. After the opening of general bids, the bid security of the sub-bidders not returned as aforesaid, shall be returned within five (5) days, Saturdays, Sundays and legal holidays excluded, after the execution of the General Contract.

16. Right to Reject Bid

The Owner reserves the right to waive any informalities in bids and to reject any and all bids, should the Owner deem it to be in the public interest to do so.

The Owner may also reject bids which in its sole judgment are either incomplete, conditional, obscure or not responsive or which contain additions not called for, erasures not properly initialed, alterations, or similar irregularities.

17. Time for Completion

The successful general bidder must agree to commence work within ten (10) days of the date of the Notice to Proceed and to fully complete the project within the time limit stated in Section 00300, FORM OF GENERAL BID.

18. Comparison of Bids

Bids will be compared on the basis of prices set forth in the bid forms.

In the event that there is a discrepancy between the lump sum or unit prices written in words and figures, the prices written in words will govern.

19. Award of Contract

The Contract will be awarded to "the lowest responsible and eligible bidder" pursuant to General Laws Chapter 149, Section 44A(2), as amended. Such a bidder shall possess the skill, ability and integrity necessary for the faithful performance of the work, shall be able to furnish labor that can work in harmony with all other elements of labor employed, or to be employed, in the work, and shall otherwise comply with all applicable provisions of law. Contract award shall be subject to availability of an appropriation for funding.

20. Statutes Regulating Competitive Bidding

Any bid which does not comply with the provisions of Massachusetts General Laws Chapter 149, Sections 44A through 44H, as amended, need not be accepted and the Owner may reject every such bid.

21. Wage Rates

Prevailing Wage Rates as determined by the Commissioner of the Department of Labor and Workforce Development under the provision of the Massachusetts General Laws, Chapter 149, Section 26 to 27G, as amended, apply to this project. It is the responsibility of the bidder, before bid opening, to request any additional information on Prevailing Wage Rates for those tradespeople who may be employed for the proposed work under this contract.

State schedules of Prevailing wage rates are included in the Supplemental General Conditions section of the Contract Documents.

22. Contractor Records

The Contractor shall comply with the provisions of Massachusetts General Laws, Chapter 30, Section 39R concerning Contractor records.

23. INSURANCE

The Contractor shall carry and continuously maintain until completion of the Contract, insurance as specified in the General Conditions and in such form as shall protect him performing work covered by this Contract, and the Town of Westford and its employees, agents and officials, from all claims an liability for damages for bodily injury, including accidental death, and for property damage, which may arise from operations under this Contract. The City/Town shall be named as an additional insured. The Contractor covenants and agrees to hold the City/Town and its employees, agents and officials harmless from loss or damage due to claims for bodily injury or death and/or property damage arising from, or in connection with, operations under this Contract.

25. PROJECT MANAGER

In addition to a project Architect/Engineer, the Owner may utilize the services of a project manager, whose duties shall be as set forth in the Agreement for Project Manager Services.

21. Certificate of Eligibility and Update Statement

In accordance with G.L. c.149, §44D, every bid and sub-bid must be accompanied by a copy of a certificate of eligibility issued by the Division of Capital Asset Management showing that the bidder or sub-bidder has the classification and capacity rating to perform the work required. An appropriate update statement must also be provided with each bid. Any bid or sub-bid submitted without an appropriate certificate of eligibility or update statement shall be invalid.

SECTION 00300

FORM OF GENERAL BID

Bid of _____ (hereinafter called "Bidder")*

(____) a corporation, organized and existing under the laws of the state of _____

(____) a partnership

(____) a joint venture

(____) an individual
doing business as _____

To the City/Town of _____, Massachusetts (hereinafter called "Owner").

Gentlemen:

A) The undersigned Bidder, in compliance with your invitation for bids for the project known as _____, having examined the plans and specifications and related documents and the site of the proposed work, and being familiar with all of the conditions surrounding the construction of the proposed project including the availability of materials and labor, hereby proposes to furnish all labor, materials, and supplies, and to construct the project in accordance with the contract documents and the plans and specifications within the time set forth below, and at the prices stated below. These prices are to cover all expenses incurred in performing the work required under the contract documents, of which this bid is a part.

The Bidder hereby agrees to commence work on or before the date to be specified in written "Notice to Proceed" of the Owner, and to substantially complete the project within forty five (45) consecutive calendar days thereafter.

*Specify corporation, partnership or individual as applicable.

B) Bidder acknowledges receipt of and this bid includes the following addenda:

No. _____ Dated: _____

No. _____ Dated: _____

No. _____ Dated: _____

No. _____ Dated: _____

C) The Bidder agrees to perform the work described in the specifications and shown on the plans for the following contract price: \$ _____ .

For Alternate No. 1 Add \$ _____; Subtract \$ _____

For Alternate No. 2 Add \$ _____; Subtract \$ _____

For Alternate No. 3 Add \$ _____; Subtract \$ _____

The undersigned agrees that, if he/she is selected as general contractor, he/she will within five days, Saturdays, Sundays and legal holidays excluded, after presentation thereof by the awarding authority, execute a contract in accordance with the terms of this bid and furnish a performance bond and also a labor and materials or payment bond, each of a surety company qualified to do business under the laws of the commonwealth and satisfactory to the awarding authority and each in the sum of the contract price, the premiums for which are to be paid by the general contractor and are included in the contract price; provided, however, that if there is more than one surety company, the surety companies shall be jointly and severally liable.

The undersigned hereby certifies that he/she is able to furnish labor that can work in harmony with all other elements of labor employed or to be employed on the work; that all employees to be employed at the worksite will have successfully completed a course in construction safety and health approved by the United States Occupational Safety and Health Administration (OSHA) that is at least 10 hours in duration at the time the employee begins work and who shall furnish documentation of successful completion of said course with the first certified payroll report for each employee; and that he/she will comply fully with all laws and regulations applicable to awards made subject to section 44A.

The undersigned further certifies under the penalties of perjury that this bid is in all respects bona fide, fair and made without collusion or fraud with any other person. As used in this subsection the word "person" shall mean any natural person, joint venture, partnership, corporation or other business or legal entity. The undersigned further certifies under penalty of perjury that the said undersigned is not presently debarred from doing public construction work in the commonwealth under the provisions of section twenty-nine F of chapter twenty-nine, or any other applicable debarment provisions of any other chapter of the General Laws or any rule or regulation promulgated thereunder.

The Bidder understands that the Owner reserves the right to reject any or all bids and to waive any informalities in the bidding.

The Bidder agrees that this bid shall be good and may not be withdrawn for a period of 30 days, Saturdays, Sundays and legal holidays excluded, after the opening of bids.

Bid security is attached in the sum of five percent (5%) of the total bid in accordance with the conditions of Section 00100 INSTRUCTIONS TO BIDDERS. The bid security may become the property of the Owner in the event the contract and bonds are not executed within the time set forth above.

The selected Contractor shall furnish a performance bond and a payment bond in an amount at least equal to one hundred percent (100%) of the contract price in accordance with Section 00610 PERFORMANCE BOND, Section 00620 PAYMENT BOND, and as stipulated in Section 00700 GENERAL CONDITIONS and any supplemental general conditions thereto.

The undersigned offers the following information as evidence of his qualifications to perform the work as bid upon according to all the requirements of the plans and specifications.

1. Have been in business under present name for ____ years.
2. The names and addresses of all persons interested in the bid (if made by a partnership or corporation) as principals, are as follows:

(attach supplementary list if necessary)

3. The bidder is requested to state below what work of a similar character to that included in the proposed contract he/she has done, and give references that will enable the Owner to judge his experience, skill and business standing (add supplementary page if necessary).

<u>Completion Date</u>	<u>Project Name</u>	<u>Contract Amount</u>	<u>Design Architect</u>	<u>Reference Name</u>	<u>Telephone No.</u>
----------------------------	-------------------------	----------------------------	-----------------------------	---------------------------	--------------------------

a. _____

b. _____

c. _____

d. _____

e. _____

f. _____

Pursuant to M.G.L. C. 62C, Sec. 49A, I certify hereby in writing, under penalties of perjury, that the within named Bidder/Contractor has complied with all laws of the commonwealth relating to taxes, reporting of employees and contractors, and withholding and remitting of child support.

The undersigned bidder hereby certifies, under pains and penalties of perjury, that the foregoing bid is based upon the payment to laborers to be employed on the project of wages in an amount no less than the applicable prevailing wage rates established for the project by the Massachusetts Department of Labor and Workforce Development. The undersigned bidder agrees to indemnify the Awarding Authority for, from and against any loss, expense, damages, actions or claims, including any expense incurred in connection with any delay or stoppage of the project work arising out of or as a result of (1) the failure of the said bid to be based upon the payment of the said applicable prevailing wage rates or (2) the failure of the bidder, if selected as the contractor, to pay laborers employed on the project the said applicable prevailing wage rates.

Respectfully submitted:

Date: _____

By: _____
(Signature)

(Type Name of Bidder)

(Title)

(Business Address)

(City and State)

(Telephone Number)

SECTION 00500

AGREEMENT

THIS AGREEMENT, made this _____ day of _____, 201_, by and between the party of the first part, the Town of Westford, hereinafter called "OWNER," acting herein through its _____, and the party of the second part, _____ doing business as *(an individual) (a partnership) (a joint venture) (a corporation) located in the *(City) (Town) of _____, County of _____, and State of _____, hereinafter called "CONTRACTOR."

WITNESSETH: That for and in consideration of the payments and agreements hereinafter mentioned, to be made and performed by the OWNER, the CONTRACTOR hereby agrees with the OWNER to commence and complete the project described as follows: _____, hereinafter called the Project, for the sum of _____ Dollars (\$_____) and all extra work in connection therewith, under the terms as stated in the Contract Documents; and at his (its or their) own proper cost and expense to furnish all the materials, supplies, machinery equipment, tools, superintendence, labor, insurance, and other accessories and services necessary to complete the said project in accordance with the conditions and prices stated in Section 00300 FORM OF GENERAL BID, Section 00700 GENERAL CONDITIONS, and Section 00800 SUPPLEMENTAL GENERAL CONDITIONS, the plans, which include all maps, plates, blue prints, and the specifications and Contract Documents as prepared by the Owner.

The CONTRACTOR hereby agrees to commence work under this Contract on or before a date to be specified in written "Notice to Proceed" of the OWNER.

The CONTRACTOR further agrees to substantially complete the project within 45 consecutive calendar days of the date of the notice to proceed.

~~The CONTRACTOR further agrees to pay as liquidated damages the sum of \$ _____ for each consecutive calendar day thereafter as provided in the Liquidated Damages Paragraph of Article 8 of Section 00700 GENERAL CONDITIONS.~~

The CONTRACTOR agrees not to discriminate against or exclude any person from participation herein on grounds of race, religion, color, sex, age or national origin; and that it shall take affirmative actions to ensure that applicants are employed, and that employees are treated during their employment, without regard to race, religion, color, sex, age, handicapped status, or national origin.

The CONTRACTOR agrees not to participate in or cooperate with an international boycott, as defined in Section 999 (b)(3) and (4) of the Internal Revenue Code of 1986, as amended, or engage in conduct declared to be unlawful by Section 2 of Chapter 151E of the Massachusetts General Laws.

The OWNER agrees to pay the CONTRACTOR in current funds for the performance of the contract, subject to additions and deductions, as provided in Section 00700 GENERAL CONDITIONS, and to make payments on account thereof as provided in Article 9 of Section 00700 GENERAL CONDITIONS.

IN WITNESS WHEREOF, the parties to these presents have executed this contract in two (2) counterparts, each of which shall be deemed an original, in the year and day first above mentioned.

AGREED:

TOWN OF WESTFORD, MASSACHUSETTS

(Owner)

By _____

(Name)

(Title)

CONTRACTOR: _____

By _____

(Name)

(Title)

(Address)

(City and State)

Approved as to Form:

By _____
(Owner's Counsel)

In accordance with M.G.L. C.44, Section 31C, this is to certify that an appropriation in the amount of this contract is available therefor and that the _____ has been authorized to execute the contract and approve all requisitions and change orders.

By _____
(Owner's Accountant)

(Name)

CERTIFICATE OF VOTE
(to be filed if Contractor is a Corporation)

I, _____, hereby certify that I am the duly qualified
(Secretary of the Corporation)

and acting Secretary of _____ and I further certify that a meeting of the
(Name of Corporation)
Directors of said Company, duly called and held on _____, at which
(Date of Meeting)

all Directors were present and voting, the following vote was unanimously passed:

VOTED: To authorize and empower

Anyone acting singly, to execute Forms of General Bid, Contracts or Bonds on behalf of the Corporation.

I further certify that the above vote is still in effect and has not been changed or modified in any respect.

By: _____
(Secretary of Corporation)

A True Copy:

Attest: _____
(Notary Public)

My Commission Expires: _____
(Date)

**CERTIFICATIONS REQUIRED BY LAW
FOR PUBLIC CONSTRUCTION CONTRACTS**

You must COMPLETE and SIGN the following certifications. You must also print, at the bottom of this page, the name of the contractor for whom these certifications are submitted.

TAX COMPLIANCE

Pursuant to Chapter 62C of the Massachusetts General Laws, Section 49A(b), I, the undersigned, authorized signatory for the below named contractor, do hereby certify under the pains and penalties of perjury that said contractor has complied with all laws of the Commonwealth of Massachusetts relating to taxes, reporting of employees and contractors, and withholding and remitting child support.

NON-COLLUSION

The undersigned certifies under the penalties of perjury that this bid is in all respects bona fide, fair and made without collusion or fraud with any other person. As used in this subsection the word "person" shall mean any natural person, joint venture, partnership, corporation or other business or legal entity.

PUBLIC CONTRACTOR DEBARMENT

The undersigned certifies under penalty of perjury that the below named contractor is not presently debarred from doing public construction work in the commonwealth under the provisions of section twenty-nine F of chapter twenty-nine, or any other applicable debarment provisions of any other chapter of the General Laws or any rule or regulation promulgated thereunder.

OSHA TRAINING

Pursuant to G.L. c. 30, §39S, the Contractor hereby certifies under penalties of perjury as follows:

- (1) Contractor is able to furnish labor that can work in harmony with all other elements of labor employed or to be employed in the work;
- (2) All employees to be employed at the worksite will have successfully completed a course in construction safety and health approved by the United States Occupational Safety and Health Administration that is at least 10 hours in duration at the time the employee begins work and they shall furnish documentation of successful completion of said course with the first certified payroll report for each employee; and
- (3) All employees to be employed in the work subject to this contract have successfully completed a course in construction safety and health approved by the United States Occupational Safety and Health Administration that is at least 10 hours in duration.

COMPLETE AND SIGN BELOW:

Authorized Person's Signature

Date

Print Name & Title of Signatory

Name of Contractor

SECTION 00610

PERFORMANCE BOND

KNOW ALL MEN BY THESE PRESENTS: That we _____
(Name of Contractor)

a _____ hereinafter called "Principal" and
(Corporation, Partnership, Joint Venture or Individual)

_____ of _____, State of _____
(Surety) (City & State)

_____ hereinafter called the "Surety" and licensed by the State
Division of Insurance to do business under the laws of the Commonwealth of Massachusetts, are
held and firmly bound to the City/Town of _____, Massachusetts, hereinafter called
"Owner", in the penal sum of

_____ Dollars
(\$ _____) in lawful money of the United States, for the payment of which
sum well and truly to be made, we bind ourselves, our heirs, executors, administrators and
successors, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION is such that Whereas, the Principal entered
into a certain contract with the Owner, dated the _____ day of _____,
20__ (the "Construction Contract"), for the construction described as follows: _____
_____.

NOW, THEREFORE, if the Principal shall well, truly and faithfully perform its duties,
all the undertakings, covenants, terms, conditions, and agreements of the Construction Contract
during the original term thereof, and any extensions thereof which may be granted by the Owner,
with or without notice to the Surety, and if he/she shall satisfy all claims and demands incurred
under the Construction Contract, and shall fully indemnify and save harmless the Owner from all
costs and damages which it may suffer by reason of failure to do so, and shall reimburse and
repay the Owner all outlay and expense which the Owner may incur in making good any default,
then this obligation shall be void; otherwise to remain in full force and effect.

PROVIDED, FURTHER, that the Surety's obligation under this Bond shall arise after (1)
the Owner has declared the Principal in default of the Construction Contract or any provision
thereof or (2) has declared that the Principal has failed, or is otherwise unable or unwilling, to
execute the work consistent with, and in conformance to, the Construction Contract (collectively
referred to as a "Contractor Default"). The determination of a Contractor Default shall be made
solely by the Owner. The Owner need not terminate the Construction Contract to declare a
Contractor Default or to invoke its rights under this Bond.

When the Surety's obligation under this Bond arises, the Surety, at its sole expense and at the consent and election of the Owner, shall promptly take one of the following steps: (1) arrange for the Principal to perform and complete the work of the Construction Contract; (2) arrange for a contractor other than the Principal to perform and complete the work of the Construction Contract; (3) reimburse the Owner, in a manner and at such time as the Owner shall decide, for all costs and expenses incurred by the Owner in performing and completing the work of the Construction Contract. Surety will keep Owner reasonably informed of the progress, status and results of any investigation of any claim of the Owner.

If the Surety does not proceed as provided in this Bond with due diligence and all deliberate speed, the Surety shall be deemed to be in default of this Bond, and the Owner shall be entitled to enforce any remedy available to the Owner.

After the Surety's obligation under this Bond arises, the Surety is obligated, to the limit of the amounts of this Bond, for (1) the correction of defective work and completion of the Construction Contract; (2) additional design, professional services, and legal costs, including attorneys' fees, resulting from the Contractor Default or from the default of the Surety under this Bond; (3) any additional work beyond the Construction Contract made necessary by the Contractor Default or default of the Surety under this Bond; (4) indemnification obligation of the Principal, if any, as provided in the Construction Contract; and (5) liquidated damages as provided in the Construction Contract, or if none are so specified, actual and foreseeable consequential damages resulting from the Contractor Default or default of the Surety under this Bond.

Any proceeding, legal or equitable, under this Bond shall be instituted in any court of competent jurisdiction in the Commonwealth of Massachusetts.

The Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of the Construction Contract or to the work to be performed thereunder or the specifications accompanying the same shall in any way affect its obligation on this Bond, and it does hereby waive notice of any such change, extension of time, alteration or addition to the terms of the Construction Contract or to the work or to the specifications.

SECTION 00620

PAYMENT BOND

KNOW ALL MEN BY THESE PRESENTS: That we _____

_____ a _____
(Name of Contractor) (Corporation, Partnership, Joint Venture or Individual)

hereinafter called "Principal" and _____ of _____,
(Surety)

State of _____ hereinafter called the "Surety" and licensed by the State
(City and State)

Division of Insurance to do business under the laws of the Commonwealth of Massachusetts, are held and firmly bound to the City/Town of _____, Massachusetts, hereinafter called "Owner", in the penal sum of _____ Dollars

(\$_____) in lawful money of the United States, for the payment of which sum well and truly to be made, we bind ourselves, our heirs, executors, administrators and successors, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION is such that Whereas, the Principal entered into a certain contract with the Owner, dated the _____ day of _____, 20____, for the construction described as follows:

NOW, THEREFORE, if the Principal shall promptly make payment to all persons, firms, subcontractors, and corporations furnishing materials for or performing labor in the prosecution of the work provided for in such contract, and any authorized extension or modification thereof, including all amounts due for materials, lubricants, oil, gasoline, coal and coke, repairs on machinery, equipment and tools, consumed or used in connection with the construction of such work, and all insurance premiums on said work, and for all labor, performed in such work whether by subcontractor or otherwise, then this obligation shall be void; otherwise to remain in full force and effect.

PROVIDED, FURTHER, that the said Surety, for value received hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of the contract or to the work to be performed thereunder or the specifications accompanying the same shall in any way affect its obligation on this bond, and it does hereby waive notice of any such change, extension of time, alteration or addition to the terms of this contract or to the work or to the specifications.

PROVIDED, FURTHER, that no final settlement between the Owner and the Contractor shall abridge the right of any beneficiary hereunder, whose claim may be unsatisfied.

IN WITNESS WHEREOF, this instrument is executed in ____ () counterparts, each one of which shall be deemed an original, this the _____ day of _____, 20__.

ATTEST:

_____		_____
		Surety
_____	By	_____
		(Attorney-in-Fact)

		(Address-Zip Code)
_____	(SEAL)	
Witness as to Surety		

(Address-Zip Code)		

NOTE: Date of Bond must not be prior to date of Contract. If Contractor is a Partnership, all partners should execute Bond.

SECTION 00700

GENERAL CONDITIONS

Refer to attached AIA A201 (2007 edition)

SECTION 00750

SUPPLEMENTARY CONDITIONS

Refer to attached Supplementary General Conditions to AIA A201.



AIA[®] Document A201[™] – 2007

General Conditions of the Contract for Construction

for the following PROJECT:
(Name and location or address)

THE OWNER:
(Name and address)

THE ARCHITECT:
(Name and address)

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

TABLE OF ARTICLES

- 1 GENERAL PROVISIONS
- 2 OWNER
- 3 CONTRACTOR
- 4 ARCHITECT
- 5 SUBCONTRACTORS
- 6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS
- 7 CHANGES IN THE WORK
- 8 TIME
- 9 PAYMENTS AND COMPLETION
- 10 PROTECTION OF PERSONS AND PROPERTY
- 11 INSURANCE AND BONDS
- 12 UNCOVERING AND CORRECTION OF WORK
- 13 MISCELLANEOUS PROVISIONS
- 14 TERMINATION OR SUSPENSION OF THE CONTRACT
- 15 CLAIMS AND DISPUTES

Init.

AIA Document A201[™] – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

INDEX

(Numbers and Topics in Bold are Section Headings)

Acceptance of Nonconforming Work

9.6.6, 9.9.3, **12.3**

Acceptance of Work

9.6.6, 9.8.2, 9.9.3, 9.10.1, 9.10.3, **12.3**

Access to Work

3.16, 6.2.1, 12.1

Accident Prevention

10

Acts and Omissions

3.2, 3.3.2, 3.12.8, 3.18, 4.2.3, 8.3.1, 9.5.1, 10.2.5, 10.2.8, 13.4.2, 13.7.1, 14.1, 15.2

Addenda

1.1.1, 3.11.1

Additional Costs, Claims for

3.7.4, 3.7.5, 6.1.1, 7.3.7.5, 10.3, 15.1.4

Additional Inspections and Testing

9.4.2, 9.8.3, 12.2.1, **13.5**

Additional Insured

11.1.4

Additional Time, Claims for

3.2.4, 3.7.4, 3.7.5, 3.10.2, 8.3.2, **15.1.5**

Administration of the Contract

3.1.3, **4.2**, 9.4, 9.5

Advertisement or Invitation to Bid

1.1.1

Aesthetic Effect

4.2.13

Allowances

3.8, 7.3.8

All-risk Insurance

11.3.1, 11.3.1.1

Applications for Payment

4.2.5, 7.3.9, 9.2, **9.3**, 9.4, 9.5.1, 9.6.3, 9.7.1, 9.10, 11.1.3

Approvals

2.1.1, 2.2.2, 2.4, 3.1.3, 3.10.2, 3.12.8, 3.12.9, 3.12.10, 4.2.7, 9.3.2, 13.5.1

Arbitration

8.3.1, 11.3.10, 13.1.1, 15.3.2, **15.4**

ARCHITECT

4

Architect, Definition of

4.1.1

Architect, Extent of Authority

2.4.1, 3.12.7, 4.1, 4.2, 5.2, 6.3.1, 7.1.2, 7.3.7, 7.4, 9.2.1, 9.3.1, 9.4, 9.5, 9.6.3, 9.8, 9.10.1, 9.10.3, 12.1, 12.2.1, 13.5.1, 13.5.2, 14.2.2, 14.2.4, 15.1.3, 15.2.1

Architect, Limitations of Authority and Responsibility

2.1.1, 3.12.4, 3.12.8, 3.12.10, 4.1.2, 4.2.1, 4.2.2, 4.2.3, 4.2.6, 4.2.7, 4.2.10, 4.2.12, 4.2.13, 5.2.1, 7.4.1, 9.4.2, 9.5.3, 9.6.4, 15.1.3, 15.2

Architect's Additional Services and Expenses

2.4.1, 11.3.1.1, 12.2.1, 13.5.2, 13.5.3, 14.2.4

Architect's Administration of the Contract

3.1.3, 4.2, 3.7.4, 15.2, 9.4.1, 9.5

Architect's Approvals

2.4.1, 3.1.3, 3.5.1, 3.10.2, 4.2.7

Architect's Authority to Reject Work

3.5.1, 4.2.6, 12.1.2, 12.2.1

Architect's Copyright

1.1.7, 1.5

Architect's Decisions

3.7.4, 4.2.6, 4.2.7, 4.2.11, 4.2.12, 4.2.13, 4.2.14, 6.3.1, 7.3.7, 7.3.9, 8.1.3, 8.3.1, 9.2.1, 9.4.1, 9.5, 9.8.4, 9.9.1, 13.5.2, 15.2, 15.3

Architect's Inspections

3.7.4, 4.2.2, 4.2.9, 9.4.2, 9.8.3, 9.9.2, 9.10.1, 13.5

Architect's Instructions

3.2.4, 3.3.1, 4.2.6, 4.2.7, 13.5.2

Architect's Interpretations

4.2.11, 4.2.12

Architect's Project Representative

4.2.10

Architect's Relationship with Contractor

1.1.2, 1.5, 3.1.3, 3.2.2, 3.2.3, 3.2.4, 3.3.1, 3.4.2, 3.5.1, 3.7.4, 3.7.5, 3.9.2, 3.9.3, 3.10, 3.11, 3.12, 3.16, 3.18, 4.1.2, 4.1.3, 4.2.5.2, 6.2.2, 7, 8.3.1, 9.2, 9.3, 9.4, 9.5, 9.7, 9.8, 9.9, 10.2.6, 10.3, 11.3.7, 12, 13.4.2, 13.5, 15.2

Architect's Relationship with Subcontractors

1.1.2, 4.2.3, 4.2.4, 4.2.6, 9.6.3, 9.6.4, 11.3.7

Architect's Representations

9.4.2, 9.5.1, 9.10.1

Architect's Site Visits

3.7.4, 4.2.2, 4.2.9, 9.4.2, 9.5.1, 9.9.2, 9.10.1, 13.5

Asbestos

10.3.1

Attorneys' Fees

3.18.1, 9.10.2, 10.3.3

Award of Separate Contracts

6.1.1, 6.1.2

Award of Subcontracts and Other Contracts for Portions of the Work

5.2

Basic Definitions

1.1

Bidding Requirements

1.1.1, 5.2.1, 11.4.1

Binding Dispute Resolution

9.7.1, 11.3.9, 11.3.10, 13.1.1, 15.2.5, 15.2.6.1, 15.3.1, 15.3.2, 15.4.1

Boiler and Machinery Insurance

11.3.2

Bonds, Lien

7.3.7.4, 9.10.2, 9.10.3

Bonds, Performance, and Payment

7.3.7.4, 9.6.7, 9.10.3, 11.3.9, **11.4**

Building Permit

3.7.1

Capitalization

1.3

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

2

Certificate of Substantial Completion

9.8.3, 9.8.4, 9.8.5

Certificates for Payment

4.2.1, 4.2.5, 4.2.9, 9.3.3, 9.4, 9.5, 9.6.1, 9.6.6, 9.7.1,

9.10.1, 9.10.3, 14.1.1.3, 14.2.4, 15.1.3

Certificates of Inspection, Testing or Approval

13.5.4

Certificates of Insurance

9.10.2, 11.1.3

Change Orders

1.1.1, 2.4.1, 3.4.2, 3.7.4, 3.8.2.3, 3.11.1, 3.12.8, 4.2.8,

5.2.3, 7.1.2, 7.1.3, 7.2, 7.3.2, 7.3.6, 7.3.9, 7.3.10,

8.3.1, 9.3.1.1, 9.10.3, 10.3.2, 11.3.1.2, 11.3.4, 11.3.9,

12.1.2, 15.1.3

Change Orders, Definition of

7.2.1

CHANGES IN THE WORK

2.2.1, 3.11, 4.2.8, 7, 7.2.1, 7.3.1, 7.4, 7.4.1, 8.3.1,

9.3.1.1, 11.3.9

Claims, Definition of

15.1.1

CLAIMS AND DISPUTES

3.2.4, 6.1.1, 6.3.1, 7.3.9, 9.3.3, 9.10.4, 10.3.3, 15,

15.4

Claims and Timely Assertion of Claims

15.4.1

Claims for Additional Cost

3.2.4, 3.7.4, 6.1.1, 7.3.9, 10.3.2, **15.1.4**

Claims for Additional Time

3.2.4, 3.7.46.1.1, 8.3.2, 10.3.2, **15.1.5**

Concealed or Unknown Conditions, Claims for

3.7.4

Claims for Damages

3.2.4, 3.18, 6.1.1, 8.3.3, 9.5.1, 9.6.7, 10.3.3, 11.1.1,

11.3.5, 11.3.7, 14.1.3, 14.2.4, 15.1.6

Claims Subject to Arbitration

15.3.1, 15.4.1

Cleaning Up

3.15, 6.3

Commencement of the Work, Conditions Relating to

2.2.1, 3.2.2, 3.4.1, 3.7.1, 3.10.1, 3.12.6, 5.2.1, 5.2.3,

6.2.2, 8.1.2, 8.2.2, 8.3.1, 11.1, 11.3.1, 11.3.6, 11.4.1,

15.1.4

Commencement of the Work, Definition of

8.1.2

Communications Facilitating Contract

Administration

3.9.1, **4.2.4**

Completion, Conditions Relating to

3.4.1, 3.11, 3.15, 4.2.2, 4.2.9, 8.2, 9.4.2, 9.8, 9.9.1,

9.10, 12.2, 13.7, 14.1.2

COMPLETION, PAYMENTS AND

9

Completion, Substantial

4.2.9, 8.1.1, 8.1.3, 8.2.3, 9.4.2, 9.8, 9.9.1, 9.10.3,

12.2, 13.7

Compliance with Laws

1.6.1, 3.2.3, 3.6, 3.7, 3.12.10, 3.13, 4.1.1, 9.6.4,

10.2.2, 11.1, 11.3, 13.1, 13.4, 13.5.1, 13.5.2, 13.6,

14.1.1, 14.2.1.3, 15.2.8, 15.4.2, 15.4.3

Concealed or Unknown Conditions

3.7.4, 4.2.8, 8.3.1, 10.3

Conditions of the Contract

1.1.1, 6.1.1, 6.1.4

Consent, Written

3.4.2, 3.7.4, 3.12.8, 3.14.2, 4.1.2, 9.3.2, 9.8.5, 9.9.1,

9.10.2, 9.10.3, 11.3.1, 13.2, 13.4.2, 15.4.4.2

Consolidation or Joinder

15.4.4

CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

1.1.4, 6

Construction Change Directive, Definition of

7.3.1

Construction Change Directives

1.1.1, 3.4.2, 3.12.8, 4.2.8, 7.1.1, 7.1.2, 7.1.3, **7.3,**

9.3.1.1

Construction Schedules, Contractor's

3.10, 3.12.1, 3.12.2, 6.1.3, 15.1.5.2

Contingent Assignment of Subcontracts

5.4, 14.2.2.2

Continuing Contract Performance

15.1.3

Contract, Definition of

1.1.2

CONTRACT, TERMINATION OR

SUSPENSION OF THE

5.4.1.1, 11.3.9, 14

Contract Administration

3.1.3, 4, 9.4, 9.5

Contract Award and Execution, Conditions Relating to

3.7.1, 3.10, 5.2, 6.1, 11.1.3, 11.3.6, 11.4.1

Contract Documents, The

1.1.1

Contract Documents, Copies Furnished and Use of

1.5.2, 2.2.5, 5.3

Contract Documents, Definition of

1.1.1

Contract Sum

3.7.4, 3.8, 5.2.3, 7.2, 7.3, 7.4, **9.1,** 9.4.2, 9.5.1.4,

9.6.7, 9.7, 10.3.2, 11.3.1, 14.2.4, 14.3.2, 15.1.4,

15.2.5

Contract Sum, Definition of

9.1

Contract Time

3.7.4, 3.7.5, 3.10.2, 5.2.3, 7.2.1.3, 7.3.1, 7.3.5, 7.4,

8.1.1, 8.2.1, 8.3.1, 9.5.1, 9.7.1, 10.3.2, 12.1.1, 14.3.2,

15.1.5.1, 15.2.5

Contract Time, Definition of

8.1.1

CONTRACTOR

3

Contractor, Definition of

3.1, 6.1.2

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

Contractor's Construction Schedules

3.10, 3.12.1, 3.12.2, 6.1.3, 15.1.5.2

Contractor's Employees

3.3.2, 3.4.3, 3.8.1, 3.9, 3.18.2, 4.2.3, 4.2.6, 10.2, 10.3, 11.1.1, 11.3.7, 14.1, 14.2.1.1

Contractor's Liability Insurance

11.1

Contractor's Relationship with Separate Contractors and Owner's Forces

3.12.5, 3.14.2, 4.2.4, 6, 11.3.7, 12.1.2, 12.2.4

Contractor's Relationship with Subcontractors

1.2.2, 3.3.2, 3.18.1, 3.18.2, 5, 9.6.2, 9.6.7, 9.10.2, 11.3.1.2, 11.3.7, 11.3.8

Contractor's Relationship with the Architect

1.1.2, 1.5, 3.1.3, 3.2.2, 3.2.3, 3.2.4, 3.3.1, 3.4.2, 3.5.1, 3.7.4, 3.10, 3.11, 3.12, 3.16, 3.18, 4.1.3, 4.2, 5.2, 6.2.2, 7, 8.3.1, 9.2, 9.3, 9.4, 9.5, 9.7, 9.8, 9.9, 10.2.6, 10.3, 11.3.7, 12, 13.5, 15.1.2, 15.2.1

Contractor's Representations

3.2.1, 3.2.2, 3.5.1, 3.12.6, 6.2.2, 8.2.1, 9.3.3, 9.8.2

Contractor's Responsibility for Those Performing the Work

3.3.2, 3.18, 5.3.1, 6.1.3, 6.2, 9.5.1, 10.2.8

Contractor's Review of Contract Documents

3.2

Contractor's Right to Stop the Work

9.7

Contractor's Right to Terminate the Contract

14.1, 15.1.6

Contractor's Submittals

3.10, 3.11, 3.12.4, 4.2.7, 5.2.1, 5.2.3, 9.2, 9.3, 9.8.2, 9.8.3, 9.9.1, 9.10.2, 9.10.3, 11.1.3, 11.4.2

Contractor's Superintendent

3.9, 10.2.6

Contractor's Supervision and Construction Procedures

1.2.2, 3.3, 3.4, 3.12.10, 4.2.2, 4.2.7, 6.1.3, 6.2.4, 7.1.3, 7.3.5, 7.3.7, 8.2, 10, 12, 14, 15.1.3

Contractual Liability Insurance

11.1.1.8, 11.2

Coordination and Correlation

1.2, 3.2.1, 3.3.1, 3.10, 3.12.6, 6.1.3, 6.2.1

Copies Furnished of Drawings and Specifications

1.5, 2.2.5, 3.11

Copyrights

1.5, 3.17

Correction of Work

2.3, 2.4, 3.7.3, 9.4.2, 9.8.2, 9.8.3, 9.9.1, 12.1.2, 12.2

Correlation and Intent of the Contract Documents

1.2

Cost, Definition of

7.3.7

Costs

2.4.1, 3.2.4, 3.7.3, 3.8.2, 3.15.2, 5.4.2, 6.1.1, 6.2.3, 7.3.3.3, 7.3.7, 7.3.8, 7.3.9, 9.10.2, 10.3.2, 10.3.6, 11.3, 12.1.2, 12.2.1, 12.2.4, 13.5, 14

Cutting and Patching

3.14, 6.2.5

Damage to Construction of Owner or Separate Contractors

3.14.2, 6.2.4, 10.2.1.2, 10.2.5, 10.4, 11.1.1, 11.3, 12.2.4

Damage to the Work

3.14.2, 9.9.1, 10.2.1.2, 10.2.5, 10.4.1, 11.3.1, 12.2.4

Damages, Claims for

3.2.4, 3.18, 6.1.1, 8.3.3, 9.5.1, 9.6.7, 10.3.3, 11.1.1, 11.3.5, 11.3.7, 14.1.3, 14.2.4, 15.1.6

Damages for Delay

6.1.1, 8.3.3, 9.5.1.6, 9.7, 10.3.2

Date of Commencement of the Work, Definition of

8.1.2

Date of Substantial Completion, Definition of

8.1.3

Day, Definition of

8.1.4

Decisions of the Architect

3.7.4, 4.2.6, 4.2.7, 4.2.11, 4.2.12, 4.2.13, 15.2, 6.3, 7.3.7, 7.3.9, 8.1.3, 8.3.1, 9.2.1, 9.4, 9.5.1, 9.8.4, 9.9.1, 13.5.2, 14.2.2, 14.2.4, 15.1, 15.2

Decisions to Withhold Certification

9.4.1, 9.5, 9.7, 14.1.1.3

Defective or Nonconforming Work, Acceptance, Rejection and Correction of

2.3.1, 2.4.1, 3.5.1, 4.2.6, 6.2.5, 9.5.1, 9.5.2, 9.6.6, 9.8.2, 9.9.3, 9.10.4, 12.2.1

Defective Work, Definition of

3.5.1

Definitions

1.1, 2.1.1, 3.1.1, 3.5.1, 3.12.1, 3.12.2, 3.12.3, 4.1.1, 15.1.1, 5.1, 6.1.2, 7.2.1, 7.3.1, 8.1, 9.1, 9.8.1

Delays and Extensions of Time

3.2., 3.7.4, 5.2.3, 7.2.1, 7.3.1, 7.4.1, 8.3, 9.5.1, 9.7.1, 10.3.2, 10.4.1, 14.3.2, 15.1.5, 15.2.5

Disputes

6.3.1, 7.3.9, 15.1, 15.2

Documents and Samples at the Site

3.11

Drawings, Definition of

1.1.5

Drawings and Specifications, Use and Ownership of

3.11

Effective Date of Insurance

8.2.2, 11.1.2

Emergencies

10.4, 14.1.1.2, 15.1.4

Employees, Contractor's

3.3.2, 3.4.3, 3.8.1, 3.9, 3.18.2, 4.2.3, 4.2.6, 10.2, 10.3.3, 11.1.1, 11.3.7, 14.1, 14.2.1.1

Equipment, Labor, Materials or

1.1.3, 1.1.6, 3.4, 3.5.1, 3.8.2, 3.8.3, 3.12, 3.13.1, 3.15.1, 4.2.6, 4.2.7, 5.2.1, 6.2.1, 7.3.7, 9.3.2, 9.3.3, 9.5.1.3, 9.10.2, 10.2.1, 10.2.4, 14.2.1.1, 14.2.1.2

Execution and Progress of the Work

1.1.3, 1.2.1, 1.2.2, 2.2.3, 2.2.5, 3.1, 3.3.1, 3.4.1, 3.5.1, 3.7.1, 3.10.1, 3.12, 3.14, 4.2, 6.2.2, 7.1.3, 7.3.5, 8.2, 9.5.1, 9.9.1, 10.2, 10.3, 12.2, 14.2, 14.3.1, 15.1.3

Init.

Extensions of Time
3.2.4, 3.7.4, 5.2.3, 7.2.1, 7.3, 7.4.1, 9.5.1, 9.7.1,
10.3.2, 10.4.1, 14.3, 15.1.5, 15.2.5
Failure of Payment
9.5.1.3, 9.7, 9.10.2, 13.6, 14.1.1.3, 14.2.1.2
Faulty Work
(See Defective or Nonconforming Work)
Final Completion and Final Payment
4.2.1, 4.2.9, 9.8.2, 9.10, 11.1.2, 11.1.3, 11.3.1, 11.3.5,
12.3.1, 14.2.4, 14.4.3
Financial Arrangements, Owner's
2.2.1, 13.2.2, 14.1.1.4
Fire and Extended Coverage Insurance
11.3.1.1

GENERAL PROVISIONS

1

Governing Law

13.1

Guarantees (See Warranty)

Hazardous Materials

10.2.4, 10.3

Identification of Subcontractors and Suppliers
5.2.1

Indemnification

3.17.1, 3.18, 9.10.2, 10.3.3, 10.3.5, 10.3.6, 11.3.1.2,
11.3.7

Information and Services Required of the Owner

2.1.2, 2.2, 3.2.2, 3.12.4, 3.12.10, 6.1.3, 6.1.4, 6.2.5,
9.6.1, 9.6.4, 9.9.2, 9.10.3, 10.3.3, 11.2.1, 11.4, 13.5.1,
13.5.2, 14.1.1.4, 14.1.4, 15.1.3

Initial Decision

15.2

Initial Decision Maker, Definition of

1.1.8

Initial Decision Maker, Decisions

14.2.2, 14.2.4, 15.2.1, 15.2.2, 15.2.3, 15.2.4, 15.2.5

Initial Decision Maker, Extent of Authority

14.2.2, 14.2.4, 15.1.3, 15.2.1, 15.2.2, 15.2.3, 15.2.4,
15.2.5

Injury or Damage to Person or Property

10.2.8, 10.4.1

Inspections

3.1.3, 3.3.3, 3.7.1, 4.2.2, 4.2.6, 4.2.9, 9.4.2, 9.8.3,
9.9.2, 9.10.1, 12.2.1, 13.5

Instructions to Bidders

1.1.1

Instructions to the Contractor

3.2.4, 3.3.1, 3.8.1, 5.2.1, 7, 8.2.2, 12, 13.5.2

Instruments of Service, Definition of

1.1.7

Insurance

3.18.1, 6.1.1, 7.3.7, 9.3.2, 9.8.4, 9.9.1, 9.10.2, 11

Insurance, Boiler and Machinery

11.3.2

Insurance, Contractor's Liability

11.1

Insurance, Effective Date of

8.2.2, 11.1.2

Insurance, Loss of Use

11.3.3

Insurance, Owner's Liability

11.2

Insurance, Property

10.2.5, 11.3

Insurance, Stored Materials

9.3.2, 11.4.1.4

INSURANCE AND BONDS

11

Insurance Companies, Consent to Partial Occupancy

9.9.1, 11.4.1.5

Insurance Companies, Settlement with

11.4.10

Intent of the Contract Documents

1.2.1, 4.2.7, 4.2.12, 4.2.13, 7.4

Interest

13.6

Interpretation

1.2.3, 1.4, 4.1.1, 5.1, 6.1.2, 15.1.1

Interpretations, Written

4.2.11, 4.2.12, 15.1.4

Judgment on Final Award

15.4.2

Labor and Materials, Equipment

1.1.3, 1.1.6, 3.4, 3.5.1, 3.8.2, 3.8.3, 3.12, 3.13, 3.15.1,

4.2.6, 4.2.7, 5.2.1, 6.2.1, 7.3.7, 9.3.2, 9.3.3, 9.5.1.3,

9.10.2, 10.2.1, 10.2.4, 14.2.1.1, 14.2.1.2

Labor Disputes

8.3.1

Laws and Regulations

1.5, 3.2.3, 3.6, 3.7, 3.12.10, 3.13.1, 4.1.1, 9.6.4, 9.9.1,

10.2.2, 11.1.1, 11.3, 13.1.1, 13.4, 13.5.1, 13.5.2,

13.6.1, 14, 15.2.8, 15.4

Liens

2.1.2, 9.3.3, 9.10.2, 9.10.4, 15.2.8

Limitations, Statutes of

12.2.5, 13.7, 15.4.1.1

Limitations of Liability

2.3.1, 3.2.2, 3.5.1, 3.12.10, 3.17.1, 3.18.1, 4.2.6,

4.2.7, 4.2.12, 6.2.2, 9.4.2, 9.6.4, 9.6.7, 10.2.5, 10.3.3,

11.1.2, 11.2.1, 11.3.7, 12.2.5, 13.4.2

Limitations of Time

2.1.2, 2.2, 2.4, 3.2.2, 3.10, 3.11, 3.12.5, 3.15.1, 4.2.7,

5.2, 5.3.1, 5.4.1, 6.2.4, 7.3, 7.4, 8.2, 9.2.1, 9.3.1,

9.3.3, 9.4.1, 9.5, 9.6, 9.7.1, 9.8, 9.9, 9.10, 11.1.3,

11.3.1.5, 11.3.6, 11.3.10, 12.2, 13.5, 13.7, 14, 15

Loss of Use Insurance

11.3.3

Material Suppliers

1.5, 3.12.1, 4.2.4, 4.2.6, 5.2.1, 9.3, 9.4.2, 9.6, 9.10.5

Materials, Hazardous

10.2.4, 10.3

Materials, Labor, Equipment and

1.1.3, 1.1.6, 1.5.1, 3.4.1, 3.5.1, 3.8.2, 3.8.3, 3.12,

3.13.1, 3.15.1, 4.2.6, 4.2.7, 5.2.1, 6.2.1, 7.3.7, 9.3.2,

9.3.3, 9.5.1.3, 9.10.2, 10.2.1.2, 10.2.4, 14.2.1.1,

14.2.1.2

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

Means, Methods, Techniques, Sequences and
Procedures of Construction

3.3.1, 3.12.10, 4.2.2, 4.2.7, 9.4.2

Mechanic's Lien

2.1.2, 15.2.8

Mediation

8.3.1, 10.3.5, 10.3.6, 15.2.1, 15.2.5, 15.2.6, **15.3**,
15.4.1

Minor Changes in the Work

1.1.1, 3.12.8, 4.2.8, 7.1, 7.4

MISCELLANEOUS PROVISIONS

13

Modifications, Definition of

1.1.1

Modifications to the Contract

1.1.1, 1.1.2, 3.11, 4.1.2, 4.2.1, 5.2.3, 7, 8.3.1, 9.7.1,
10.3.2, 11.3.1

Mutual Responsibility

6.2

Nonconforming Work, Acceptance of

9.6.6, 9.9.3, **12.3**

Nonconforming Work, Rejection and Correction of

2.3.1, 2.4.1, 3.5.1, 4.2.6, 6.2.4, 9.5.1, 9.8.2, 9.9.3,
9.10.4, 12.2.1

Notice

2.2.1, 2.3.1, 2.4.1, 3.2.4, 3.3.1, 3.7.2, 3.12.9, 5.2.1,
9.7.1, 9.10, 10.2.2, 11.1.3, 11.4.6, 12.2.2.1, 13.3,
13.5.1, 13.5.2, 14.1, 14.2, 15.2.8, 15.4.1

Notice, Written

2.3.1, 2.4.1, 3.3.1, 3.9.2, 3.12.9, 3.12.10, 5.2.1, 9.7.1,
9.10, 10.2.2, 10.3, 11.1.3, 11.3.6, 12.2.2.1, **13.3**, 14,
15.2.8, 15.4.1

Notice of Claims

3.7.4, 4.5, 10.2.8, **15.1.2**, 15.4

Notice of Testing and Inspections

13.5.1, 13.5.2

Observations, Contractor's

3.2, 3.7.4

Occupancy

2.2.2, 9.6.6, 9.8, 11.3.1.5

Orders, Written

1.1.1, 2.3, 3.9.2, 7, 8.2.2, 11.3.9, 12.1, 12.2.2.1,
13.5.2, 14.3.1

OWNER

2

Owner, Definition of

2.1.1

Owner, Information and Services Required of the

2.1.2, **2.2**, 3.2.2, 3.12.10, 6.1.3, 6.1.4, 6.2.5, 9.3.2,
9.6.1, 9.6.4, 9.9.2, 9.10.3, 10.3.3, 11.2.1, 11.3, 13.5.1,
13.5.2, 14.1.1.4, 14.1.4, 15.1.3

Owner's Authority

1.5, 2.1.1, 2.3.1, 2.4.1, 3.4.2, 3.8.1, 3.12.10, 3.14.2,
4.1.2, 4.1.3, 4.2.4, 4.2.9, 5.2.1, 5.2.4, 5.4.1, 6.1, 6.3.1,
7.2.1, 7.3.1, 8.2.2, 8.3.1, 9.3.1, 9.3.2, 9.5.1, 9.6.4,
9.9.1, 9.10.2, 10.3.2, 11.1.3, 11.3.3, 11.3.10, 12.2.2,
12.3.1, 13.2.2, 14.3, 14.4, 15.2.7

Owner's Financial Capability

2.2.1, 13.2.2, 14.1.1.4

Owner's Liability Insurance

11.2

Owner's Loss of Use Insurance

11.3.3

Owner's Relationship with Subcontractors

1.1.2, 5.2, 5.3, 5.4, 9.6.4, 9.10.2, 14.2.2

Owner's Right to Carry Out the Work

2.4, 14.2.2

Owner's Right to Clean Up

6.3

**Owner's Right to Perform Construction and to
Award Separate Contracts**

6.1

Owner's Right to Stop the Work

2.3

Owner's Right to Suspend the Work

14.3

Owner's Right to Terminate the Contract

14.2

**Ownership and Use of Drawings, Specifications
and Other Instruments of Service**

1.1.1, 1.1.6, 1.1.7, 1.5, 2.2.5, 3.2.2, 3.11.1, 3.17.1,
4.2.12, 5.3.1

Partial Occupancy or Use

9.6.6, 9.9, 11.3.1.5

Patching, Cutting and

3.14, 6.2.5

Patents

3.17

Payment, Applications for

4.2.5, 7.3.9, 9.2.1, **9.3**, 9.4, 9.5, 9.6.3, 9.7.1, 9.8.5,
9.10.1, 14.2.3, 14.2.4, 14.4.3

Payment, Certificates for

4.2.5, 4.2.9, 9.3.3, **9.4**, 9.5, 9.6.1, 9.6.6, 9.7.1, 9.10.1,
9.10.3, 13.7, 14.1.1.3, 14.2.4

Payment, Failure of

9.5.1.3, **9.7**, 9.10.2, 13.6, 14.1.1.3, 14.2.1.2

Payment, Final

4.2.1, 4.2.9, 9.8.2, 9.10, 11.1.2, 11.1.3, 11.4.1, 11.4.5,
12.3.1, 13.7, 14.2.4, 14.4.3

Payment Bond, Performance Bond and

7.3.7.4, 9.6.7, 9.10.3, 11.4.9, 11.4

Payments, Progress

9.3, **9.6**, 9.8.5, 9.10.3, 13.6, 14.2.3, 15.1.3

PAYMENTS AND COMPLETION

9

Payments to Subcontractors

5.4.2, 9.5.1.3, 9.6.2, 9.6.3, 9.6.4, 9.6.7, 11.4.8,
14.2.1.2

PCB

10.3.1

Performance Bond and Payment Bond

7.3.7.4, 9.6.7, 9.10.3, 11.4.9, **11.4**

Permits, Fees, Notices and Compliance with Laws

2.2.2, **3.7**, 3.13, 7.3.7.4, 10.2.2

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

6

**PERSONS AND PROPERTY, PROTECTION OF
10**

Polychlorinated Biphenyl
10.3.1

Product Data, Definition of
3.12.2

Product Data and Samples, Shop Drawings
3.11, 3.12, 4.2.7

Progress and Completion
4.2.2, 8.2, 9.8, 9.9.1, 14.1.4, 15.1.3

Progress Payments
9.3, 9.6, 9.8.5, 9.10.3, 13.6, 14.2.3, 15.1.3

Project, Definition of the
1.1.4

Project Representatives
4.2.10

Property Insurance
10.2.5, 11.3

**PROTECTION OF PERSONS AND PROPERTY
10**

Regulations and Laws
1.5, 3.2.3, 3.6, 3.7, 3.12.10, 3.13, 4.1.1, 9.6.4, 9.9.1,
10.2.2, 11.1, 11.4, 13.1, 13.4, 13.5.1, 13.5.2, 13.6, 14,
15.2.8, 15.4

Rejection of Work
3.5.1, 4.2.6, 12.2.1

Releases and Waivers of Liens
9.10.2

Representations
3.2.1, 3.5.1, 3.12.6, 6.2.2, 8.2.1, 9.3.3, 9.4.2, 9.5.1,
9.8.2, 9.10.1

Representatives
2.1.1, 3.1.1, 3.9, 4.1.1, 4.2.1, 4.2.2, 4.2.10, 5.1.1,
5.1.2, 13.2.1

Responsibility for Those Performing the Work
3.3.2, 3.18, 4.2.3, 5.3.1, 6.1.3, 6.2, 6.3, 9.5.1, 10

Retainage
9.3.1, 9.6.2, 9.8.5, 9.9.1, 9.10.2, 9.10.3

**Review of Contract Documents and Field
Conditions by Contractor**
3.2, 3.12.7, 6.1.3

**Review of Contractor's Submittals by Owner and
Architect**
3.10.1, 3.10.2, 3.11, 3.12, 4.2, 5.2, 6.1.3, 9.2, 9.8.2

**Review of Shop Drawings, Product Data and
Samples by Contractor**
3.12

Rights and Remedies
1.1.2, 2.3, 2.4, 3.5.1, 3.7.4, 3.15.2, 4.2.6, 4.5, 5.3, 5.4,
6.1, 6.3, 7.3.1, 8.3, 9.5.1, 9.7, 10.2.5, 10.3, 12.2.2,
12.2.4, 13.4, 14, 15.4

Royalties, Patents and Copyrights
3.17

Rules and Notices for Arbitration
15.4.1

Safety of Persons and Property
10.2, 10.4

Safety Precautions and Programs

3.3.1, 4.2.2, 4.2.7, 5.3.1, 10.1, 10.2, 10.4

Samples, Definition of
3.12.3

**Samples, Shop Drawings, Product Data and
Samples at the Site, Documents and**
3.11, 3.12, 4.2.7

Schedule of Values
9.2, 9.3.1

Schedules, Construction
1.4.1.2, 3.10, 3.12.1, 3.12.2, 6.1.3, 15.1.5.2

Separate Contracts and Contractors
1.1.4, 3.12.5, 3.14.2, 4.2.4, 4.2.7, 6.8.3.1, 11.4.7,
12.1.2

Shop Drawings, Definition of
3.12.1

Shop Drawings, Product Data and Samples
3.11, 3.12, 4.2.7

Site, Use of
3.13, 6.1.1, 6.2.1

Site Inspections
3.2.2, 3.3.3, 3.7.1, 3.7.4, 4.2, 9.4.2, 9.10.1, 13.5

Site Visits, Architect's
3.7.4, 4.2.2, 4.2.9, 9.4.2, 9.5.1, 9.9.2, 9.10.1, 13.5

Special Inspections and Testing
4.2.6, 12.2.1, 13.5

Specifications, Definition of the
1.1.6

Specifications, The
1.1.1, 1.1.6, 1.2.2, 1.5, 3.11, 3.12.10, 3.17, 4.2.14

Statute of Limitations
13.7, 15.4.1.1

Stopping the Work
2.3, 9.7, 10.3, 14.1

Stored Materials
6.2.1, 9.3.2, 10.2.1.2, 10.2.4, 11.4.1.4

Subcontractor, Definition of
5.1.1

**SUBCONTRACTORS
5**

Subcontractors, Work by
1.2.2, 3.3.2, 3.12.1, 4.2.3, 5.2.3, 5.3, 5.4, 9.3.1.2,
9.6.7

Subcontractual Relations
5.3, 5.4, 9.3.1.2, 9.6, 9.10, 10.2.1, 11.4.7, 11.4.8,
14.1, 14.2.1

Submittals
3.10, 3.11, 3.12, 4.2.7, 5.2.1, 5.2.3, 7.3.7, 9.2, 9.3,
9.8, 9.9.1, 9.10.2, 9.10.3, 11.1.3

Submittal Schedule
3.10.2, 3.12.5, 4.2.7

Subrogation, Waivers of
6.1.1, 11.4.5, 11.3.7

Substantial Completion
4.2.9, 8.1.1, 8.1.3, 8.2.3, 9.4.2, 9.8, 9.9.1, 9.10.3,
12.2, 13.7

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

Substantial Completion, Definition of
9.8.1
 Substitution of Subcontractors
 5.2.3, 5.2.4
 Substitution of Architect
 4.1.3
 Substitutions of Materials
 3.4.2, 3.5.1, 7.3.8
Sub-subcontractor, Definition of
5.1.2
 Subsurface Conditions
 3.7.4
Successors and Assigns
13.2
Superintendent
3.9, 10.2.6
Supervision and Construction Procedures
 1.2.2, **3.3**, 3.4, 3.12.10, 4.2.2, 4.2.7, 6.1.3, 6.2.4,
 7.1.3, 7.3.7, 8.2, 8.3.1, 9.4.2, 10, 12, 14, 15.1.3
 Surety
 5.4.1.2, 9.8.5, 9.10.2, 9.10.3, 14.2.2, 15.2.7
 Surety, Consent of
 9.10.2, 9.10.3
 Surveys
 2.2.3
Suspension by the Owner for Convenience
14.3
 Suspension of the Work
 5.4.2, 14.3
 Suspension or Termination of the Contract
 5.4.1.1, 11.4.9, 14
Taxes
3.6, 3.8.2.1, 7.3.7.4
Termination by the Contractor
14.1, 15.1.6
Termination by the Owner for Cause
 5.4.1.1, **14.2**, 15.1.6
Termination by the Owner for Convenience
14.4
 Termination of the Architect
 4.1.3
 Termination of the Contractor
 14.2.2
TERMINATION OR SUSPENSION OF THE
CONTRACT
14
Tests and Inspections
 3.1.3, 3.3.3, 4.2.2, 4.2.6, 4.2.9, 9.4.2, 9.8.3, 9.9.2,
 9.10.1, 10.3.2, 11.4.1.1, 12.2.1, **13.5**
TIME
8
Time, Delays and Extensions of
 3.2.4, 3.7.4, 5.2.3, 7.2.1, 7.3.1, 7.4.1, **8.3**, 9.5.1, 9.7.1,
 10.3.2, 10.4.1, 14.3.2, 15.1.5, 15.2.5

Time Limits
 2.1.2, 2.2, 2.4, 3.2.2, 3.10, 3.11, 3.12.5, 3.15.1, 4.2,
 4.4, 4.5, 5.2, 5.3, 5.4, 6.2.4, 7.3, 7.4, 8.2, 9.2, 9.3.1,
 9.3.3, 9.4.1, 9.5, 9.6, 9.7, 9.8, 9.9, 9.10, 11.1.3,
 11.4.1.5, 11.4.6, 11.4.10, 12.2, 13.5, 13.7, 14, 15.1.2,
 15.4
Time Limits on Claims
 3.7.4, 10.2.8, **13.7**, 15.1.2
 Title to Work
 9.3.2, 9.3.3
Transmission of Data in Digital Form
1.6
UNCOVERING AND CORRECTION OF WORK
12
Uncovering of Work
12.1
 Unforeseen Conditions, Concealed or Unknown
3.7.4, 8.3.1, 10.3
 Unit Prices
 7.3.3.2, 7.3.4
 Use of Documents
 1.1.1, 1.5, 2.2.5, 3.12.6, 5.3
Use of Site
3.13, 6.1.1, 6.2.1
Values, Schedule of
9.2, 9.3.1
 Waiver of Claims by the Architect
 13.4.2
 Waiver of Claims by the Contractor
 9.10.5, 11.4.7, 13.4.2, 15.1.6
 Waiver of Claims by the Owner
 9.9.3, 9.10.3, 9.10.4, 11.4.3, 11.4.5, 11.4.7, 12.2.2.1,
 13.4.2, 14.2.4, 15.1.6
 Waiver of Consequential Damages
 14.2.4, 15.1.6
 Waiver of Liens
 9.10.2, 9.10.4
Waivers of Subrogation
 6.1.1, 11.4.5, **11.3.7**
Warranty
3.5, 4.2.9, 9.3.3, 9.8.4, 9.9.1, 9.10.4, 12.2.2, 13.7.1
 Weather Delays
 15.1.5.2
Work, Definition of
1.1.3
 Written Consent
 1.5.2, 3.4.2, 3.7.4, 3.12.8, 3.14.2, 4.1.2, 9.3.2, 9.8.5,
 9.9.1, 9.10.2, 9.10.3, 11.4.1, 13.2, 13.4.2, 15.4.4.2
 Written Interpretations
 4.2.11, 4.2.12
Written Notice
 2.3, 2.4, 3.3.1, 3.9, 3.12.9, 3.12.10, 5.2.1, 8.2.2, 9.7,
 9.10, 10.2.2, 10.3, 11.1.3, 11.4.6, 12.2.2, 12.2.4, **13.3**,
 14, 15.4.1
 Written Orders
 1.1.1, 2.3, 3.9, 7, 8.2.2, 11.4.9, 12.1, 12.2, 13.5.2,
 14.3.1, 15.1.2

ARTICLE 1 GENERAL PROVISIONS

§ 1.1 BASIC DEFINITIONS

§ 1.1.1 THE CONTRACT DOCUMENTS

The Contract Documents are enumerated in the Agreement between the Owner and Contractor (hereinafter the Agreement) and consist of the Agreement, Conditions of the Contract (General, Supplementary and other Conditions), Drawings, Specifications, Addenda issued prior to execution of the Contract, other documents listed in the Agreement and Modifications issued after execution of the Contract. A Modification is (1) a written amendment to the Contract signed by both parties, (2) a Change Order, (3) a Construction Change Directive or (4) a written order for a minor change in the Work issued by the Architect. Unless specifically enumerated in the Agreement, the Contract Documents do not include the advertisement or invitation to bid, Instructions to Bidders, sample forms, other information furnished by the Owner in anticipation of receiving bids or proposals, the Contractor's bid or proposal, or portions of Addenda relating to bidding requirements.

§ 1.1.2 THE CONTRACT

The Contract Documents form the Contract for Construction. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations or agreements, either written or oral. The Contract may be amended or modified only by a Modification. The Contract Documents shall not be construed to create a contractual relationship of any kind (1) between the Contractor and the Architect or the Architect's consultants, (2) between the Owner and a Subcontractor or a Sub-subcontractor, (3) between the Owner and the Architect or the Architect's consultants or (4) between any persons or entities other than the Owner and the Contractor. The Architect shall, however, be entitled to performance and enforcement of obligations under the Contract intended to facilitate performance of the Architect's duties.

§ 1.1.3 THE WORK

The term "Work" means the construction and services required by the Contract Documents, whether completed or partially completed, and includes all other labor, materials, equipment and services provided or to be provided by the Contractor to fulfill the Contractor's obligations. The Work may constitute the whole or a part of the Project.

§ 1.1.4 THE PROJECT

The Project is the total construction of which the Work performed under the Contract Documents may be the whole or a part and which may include construction by the Owner and by separate contractors.

§ 1.1.5 THE DRAWINGS

The Drawings are the graphic and pictorial portions of the Contract Documents showing the design, location and dimensions of the Work, generally including plans, elevations, sections, details, schedules and diagrams.

§ 1.1.6 THE SPECIFICATIONS

The Specifications are that portion of the Contract Documents consisting of the written requirements for materials, equipment, systems, standards and workmanship for the Work, and performance of related services.

§ 1.1.7 INSTRUMENTS OF SERVICE

Instruments of Service are representations, in any medium of expression now known or later developed, of the tangible and intangible creative work performed by the Architect and the Architect's consultants under their respective professional services agreements. Instruments of Service may include, without limitation, studies, surveys, models, sketches, drawings, specifications, and other similar materials.

§ 1.1.8 INITIAL DECISION MAKER

The Initial Decision Maker is the person identified in the Agreement to render initial decisions on Claims in accordance with Section 15.2 and certify termination of the Agreement under Section 14.2.2.

§ 1.2 CORRELATION AND INTENT OF THE CONTRACT DOCUMENTS

§ 1.2.1 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary, and what is required by one shall be as binding as if required by all; performance by the Contractor shall be required only to the extent consistent with the Contract Documents and reasonably inferable from them as being necessary to produce the indicated results.

Init.

§ 1.2.2 Organization of the Specifications into divisions, sections and articles, and arrangement of Drawings shall not control the Contractor in dividing the Work among Subcontractors or in establishing the extent of Work to be performed by any trade.

§ 1.2.3 Unless otherwise stated in the Contract Documents, words that have well-known technical or construction industry meanings are used in the Contract Documents in accordance with such recognized meanings.

§ 1.3 CAPITALIZATION

Terms capitalized in these General Conditions include those that are (1) specifically defined, (2) the titles of numbered articles or (3) the titles of other documents published by the American Institute of Architects.

§ 1.4 INTERPRETATION

In the interest of brevity the Contract Documents frequently omit modifying words such as "all" and "any" and articles such as "the" and "an," but the fact that a modifier or an article is absent from one statement and appears in another is not intended to affect the interpretation of either statement.

§ 1.5 OWNERSHIP AND USE OF DRAWINGS, SPECIFICATIONS AND OTHER INSTRUMENTS OF SERVICE

§ 1.5.1 The Architect and the Architect's consultants shall be deemed the authors and owners of their respective Instruments of Service, including the Drawings and Specifications, and will retain all common law, statutory and other reserved rights, including copyrights. The Contractor, Subcontractors, Sub-subcontractors, and material or equipment suppliers shall not own or claim a copyright in the Instruments of Service. Submittal or distribution to meet official regulatory requirements or for other purposes in connection with this Project is not to be construed as publication in derogation of the Architect's or Architect's consultants' reserved rights.

§ 1.5.2 The Contractor, Subcontractors, Sub-subcontractors and material or equipment suppliers are authorized to use and reproduce the Instruments of Service provided to them solely and exclusively for execution of the Work. All copies made under this authorization shall bear the copyright notice, if any, shown on the Instruments of Service. The Contractor, Subcontractors, Sub-subcontractors, and material or equipment suppliers may not use the Instruments of Service on other projects or for additions to this Project outside the scope of the Work without the specific written consent of the Owner, Architect and the Architect's consultants.

§ 1.6 TRANSMISSION OF DATA IN DIGITAL FORM

If the parties intend to transmit Instruments of Service or any other information or documentation in digital form, they shall endeavor to establish necessary protocols governing such transmissions, unless otherwise already provided in the Agreement or the Contract Documents.

ARTICLE 2 OWNER

§ 2.1 GENERAL

§ 2.1.1 The Owner is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Owner shall designate in writing a representative who shall have express authority to bind the Owner with respect to all matters requiring the Owner's approval or authorization. Except as otherwise provided in Section 4.2.1, the Architect does not have such authority. The term "Owner" means the Owner or the Owner's authorized representative.

§ 2.1.2 The Owner shall furnish to the Contractor within fifteen days after receipt of a written request, information necessary and relevant for the Contractor to evaluate, give notice of or enforce mechanic's lien rights. Such information shall include a correct statement of the record legal title to the property on which the Project is located, usually referred to as the site, and the Owner's interest therein.

§ 2.2 INFORMATION AND SERVICES REQUIRED OF THE OWNER

§ 2.2.1 Prior to commencement of the Work, the Contractor may request in writing that the Owner provide reasonable evidence that the Owner has made financial arrangements to fulfill the Owner's obligations under the Contract. Thereafter, the Contractor may only request such evidence if (1) the Owner fails to make payments to the Contractor as the Contract Documents require; (2) a change in the Work materially changes the Contract Sum; or (3) the Contractor identifies in writing a reasonable concern regarding the Owner's ability to make payment when due. The Owner shall furnish such evidence as a condition precedent to commencement or continuation of the Work or the portion of the Work affected by a material change. After the Owner furnishes the evidence, the Owner shall not materially vary such financial arrangements without prior notice to the Contractor.

Init.

§ 2.2.2 Except for permits and fees that are the responsibility of the Contractor under the Contract Documents, including those required under Section 3.7.1, the Owner shall secure and pay for necessary approvals, easements, assessments and charges required for construction, use or occupancy of permanent structures or for permanent changes in existing facilities.

§ 2.2.3 The Owner shall furnish surveys describing physical characteristics, legal limitations and utility locations for the site of the Project, and a legal description of the site. The Contractor shall be entitled to rely on the accuracy of information furnished by the Owner but shall exercise proper precautions relating to the safe performance of the Work.

§ 2.2.4 The Owner shall furnish information or services required of the Owner by the Contract Documents with reasonable promptness. The Owner shall also furnish any other information or services under the Owner's control and relevant to the Contractor's performance of the Work with reasonable promptness after receiving the Contractor's written request for such information or services.

§ 2.2.5 Unless otherwise provided in the Contract Documents, the Owner shall furnish to the Contractor one copy of the Contract Documents for purposes of making reproductions pursuant to Section 1.5.2.

§ 2.3 OWNER'S RIGHT TO STOP THE WORK

If the Contractor fails to correct Work that is not in accordance with the requirements of the Contract Documents as required by Section 12.2 or repeatedly fails to carry out Work in accordance with the Contract Documents, the Owner may issue a written order to the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, the right of the Owner to stop the Work shall not give rise to a duty on the part of the Owner to exercise this right for the benefit of the Contractor or any other person or entity, except to the extent required by Section 6.1.3.

§ 2.4 OWNER'S RIGHT TO CARRY OUT THE WORK

If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a ten-day period after receipt of written notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may, without prejudice to other remedies the Owner may have, correct such deficiencies. In such case an appropriate Change Order shall be issued deducting from payments then or thereafter due the Contractor the reasonable cost of correcting such deficiencies, including Owner's expenses and compensation for the Architect's additional services made necessary by such default, neglect or failure. Such action by the Owner and amounts charged to the Contractor are both subject to prior approval of the Architect. If payments then or thereafter due the Contractor are not sufficient to cover such amounts, the Contractor shall pay the difference to the Owner.

ARTICLE 3 CONTRACTOR

§ 3.1 GENERAL

§ 3.1.1 The Contractor is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Contractor shall be lawfully licensed, if required in the jurisdiction where the Project is located. The Contractor shall designate in writing a representative who shall have express authority to bind the Contractor with respect to all matters under this Contract. The term "Contractor" means the Contractor or the Contractor's authorized representative.

§ 3.1.2 The Contractor shall perform the Work in accordance with the Contract Documents.

§ 3.1.3 The Contractor shall not be relieved of obligations to perform the Work in accordance with the Contract Documents either by activities or duties of the Architect in the Architect's administration of the Contract, or by tests, inspections or approvals required or performed by persons or entities other than the Contractor.

§ 3.2 REVIEW OF CONTRACT DOCUMENTS AND FIELD CONDITIONS BY CONTRACTOR

§ 3.2.1 Execution of the Contract by the Contractor is a representation that the Contractor has visited the site, become generally familiar with local conditions under which the Work is to be performed and correlated personal observations with requirements of the Contract Documents.

Init.

§ 3.2.2 Because the Contract Documents are complementary, the Contractor shall, before starting each portion of the Work, carefully study and compare the various Contract Documents relative to that portion of the Work, as well as the information furnished by the Owner pursuant to Section 2.2.3, shall take field measurements of any existing conditions related to that portion of the Work, and shall observe any conditions at the site affecting it. These obligations are for the purpose of facilitating coordination and construction by the Contractor and are not for the purpose of discovering errors, omissions, or inconsistencies in the Contract Documents; however, the Contractor shall promptly report to the Architect any errors, inconsistencies or omissions discovered by or made known to the Contractor as a request for information in such form as the Architect may require. It is recognized that the Contractor's review is made in the Contractor's capacity as a contractor and not as a licensed design professional, unless otherwise specifically provided in the Contract Documents.

§ 3.2.3 The Contractor is not required to ascertain that the Contract Documents are in accordance with applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, but the Contractor shall promptly report to the Architect any nonconformity discovered by or made known to the Contractor as a request for information in such form as the Architect may require.

§ 3.2.4 If the Contractor believes that additional cost or time is involved because of clarifications or instructions the Architect issues in response to the Contractor's notices or requests for information pursuant to Sections 3.2.2 or 3.2.3, the Contractor shall make Claims as provided in Article 15. If the Contractor fails to perform the obligations of Sections 3.2.2 or 3.2.3, the Contractor shall pay such costs and damages to the Owner as would have been avoided if the Contractor had performed such obligations. If the Contractor performs those obligations, the Contractor shall not be liable to the Owner or Architect for damages resulting from errors, inconsistencies or omissions in the Contract Documents, for differences between field measurements or conditions and the Contract Documents, or for nonconformities of the Contract Documents to applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities.

§ 3.3 SUPERVISION AND CONSTRUCTION PROCEDURES

§ 3.3.1 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for, and have control over, construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work under the Contract, unless the Contract Documents give other specific instructions concerning these matters. If the Contract Documents give specific instructions concerning construction means, methods, techniques, sequences or procedures, the Contractor shall evaluate the jobsite safety thereof and, except as stated below, shall be fully and solely responsible for the jobsite safety of such means, methods, techniques, sequences or procedures. If the Contractor determines that such means, methods, techniques, sequences or procedures may not be safe, the Contractor shall give timely written notice to the Owner and Architect and shall not proceed with that portion of the Work without further written instructions from the Architect. If the Contractor is then instructed to proceed with the required means, methods, techniques, sequences or procedures without acceptance of changes proposed by the Contractor, the Owner shall be solely responsible for any loss or damage arising solely from those Owner-required means, methods, techniques, sequences or procedures.

§ 3.3.2 The Contractor shall be responsible to the Owner for acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons or entities performing portions of the Work for, or on behalf of, the Contractor or any of its Subcontractors.

§ 3.3.3 The Contractor shall be responsible for inspection of portions of Work already performed to determine that such portions are in proper condition to receive subsequent Work.

§ 3.4 LABOR AND MATERIALS

§ 3.4.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for proper execution and completion of the Work, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work.

§ 3.4.2 Except in the case of minor changes in the Work authorized by the Architect in accordance with Sections 3.12.8 or 7.4, the Contractor may make substitutions only with the consent of the Owner, after evaluation by the Architect and in accordance with a Change Order or Construction Change Directive.

§ 3.4.3 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Work. The Contractor shall not permit employment of unfit persons or persons not properly skilled in tasks assigned to them.

§ 3.5 WARRANTY

The Contractor warrants to the Owner and Architect that materials and equipment furnished under the Contract will be of good quality and new unless the Contract Documents require or permit otherwise. The Contractor further warrants that the Work will conform to the requirements of the Contract Documents and will be free from defects, except for those inherent in the quality of the Work the Contract Documents require or permit. Work, materials, or equipment not conforming to these requirements may be considered defective. The Contractor's warranty excludes remedy for damage or defect caused by abuse, alterations to the Work not executed by the Contractor, improper or insufficient maintenance, improper operation, or normal wear and tear and normal usage. If required by the Architect, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment.

§ 3.6 TAXES

The Contractor shall pay sales, consumer, use and similar taxes for the Work provided by the Contractor that are legally enacted when bids are received or negotiations concluded, whether or not yet effective or merely scheduled to go into effect.

§ 3.7 PERMITS, FEES, NOTICES, AND COMPLIANCE WITH LAWS

§ 3.7.1 Unless otherwise provided in the Contract Documents, the Contractor shall secure and pay for the building permit as well as for other permits, fees, licenses, and inspections by government agencies necessary for proper execution and completion of the Work that are customarily secured after execution of the Contract and legally required at the time bids are received or negotiations concluded.

§ 3.7.2 The Contractor shall comply with and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities applicable to performance of the Work.

§ 3.7.3 If the Contractor performs Work knowing it to be contrary to applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, the Contractor shall assume appropriate responsibility for such Work and shall bear the costs attributable to correction.

§ 3.7.4 Concealed or Unknown Conditions. If the Contractor encounters conditions at the site that are (1) subsurface or otherwise concealed physical conditions that differ materially from those indicated in the Contract Documents or (2) unknown physical conditions of an unusual nature that differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, the Contractor shall promptly provide notice to the Owner and the Architect before conditions are disturbed and in no event later than 21 days after first observance of the conditions. The Architect will promptly investigate such conditions and, if the Architect determines that they differ materially and cause an increase or decrease in the Contractor's cost of, or time required for, performance of any part of the Work, will recommend an equitable adjustment in the Contract Sum or Contract Time, or both. If the Architect determines that the conditions at the site are not materially different from those indicated in the Contract Documents and that no change in the terms of the Contract is justified, the Architect shall promptly notify the Owner and Contractor in writing, stating the reasons. If either party disputes the Architect's determination or recommendation, that party may proceed as provided in Article 15.

§ 3.7.5 If, in the course of the Work, the Contractor encounters human remains or recognizes the existence of burial markers, archaeological sites or wetlands not indicated in the Contract Documents, the Contractor shall immediately suspend any operations that would affect them and shall notify the Owner and Architect. Upon receipt of such notice, the Owner shall promptly take any action necessary to obtain governmental authorization required to resume the operations. The Contractor shall continue to suspend such operations until otherwise instructed by the Owner but shall continue with all other operations that do not affect those remains or features. Requests for adjustments in the Contract Sum and Contract Time arising from the existence of such remains or features may be made as provided in Article 15.

§ 3.8 ALLOWANCES

§ 3.8.1 The Contractor shall include in the Contract Sum all allowances stated in the Contract Documents. Items covered by allowances shall be supplied for such amounts and by such persons or entities as the Owner may direct,

Init.

but the Contractor shall not be required to employ persons or entities to whom the Contractor has reasonable objection.

§ 3.8.2 Unless otherwise provided in the Contract Documents,

- .1 allowances shall cover the cost to the Contractor of materials and equipment delivered at the site and all required taxes, less applicable trade discounts;
- .2 Contractor's costs for unloading and handling at the site, labor, installation costs, overhead, profit and other expenses contemplated for stated allowance amounts shall be included in the Contract Sum but not in the allowances; and
- .3 whenever costs are more than or less than allowances, the Contract Sum shall be adjusted accordingly by Change Order. The amount of the Change Order shall reflect (1) the difference between actual costs and the allowances under Section 3.8.2.1 and (2) changes in Contractor's costs under Section 3.8.2.2.

§ 3.8.3 Materials and equipment under an allowance shall be selected by the Owner with reasonable promptness.

§ 3.9 SUPERINTENDENT

§ 3.9.1 The Contractor shall employ a competent superintendent and necessary assistants who shall be in attendance at the Project site during performance of the Work. The superintendent shall represent the Contractor, and communications given to the superintendent shall be as binding as if given to the Contractor.

§ 3.9.2 The Contractor, as soon as practicable after award of the Contract, shall furnish in writing to the Owner through the Architect the name and qualifications of a proposed superintendent. The Architect may reply within 14 days to the Contractor in writing stating (1) whether the Owner or the Architect has reasonable objection to the proposed superintendent or (2) that the Architect requires additional time to review. Failure of the Architect to reply within the 14 day period shall constitute notice of no reasonable objection.

§ 3.9.3 The Contractor shall not employ a proposed superintendent to whom the Owner or Architect has made reasonable and timely objection. The Contractor shall not change the superintendent without the Owner's consent, which shall not unreasonably be withheld or delayed.

§ 3.10 CONTRACTOR'S CONSTRUCTION SCHEDULES

§ 3.10.1 The Contractor, promptly after being awarded the Contract, shall prepare and submit for the Owner's and Architect's information a Contractor's construction schedule for the Work. The schedule shall not exceed time limits current under the Contract Documents, shall be revised at appropriate intervals as required by the conditions of the Work and Project, shall be related to the entire Project to the extent required by the Contract Documents, and shall provide for expeditious and practicable execution of the Work.

§ 3.10.2 The Contractor shall prepare a submittal schedule, promptly after being awarded the Contract and thereafter as necessary to maintain a current submittal schedule, and shall submit the schedule(s) for the Architect's approval. The Architect's approval shall not unreasonably be delayed or withheld. The submittal schedule shall (1) be coordinated with the Contractor's construction schedule, and (2) allow the Architect reasonable time to review submittals. If the Contractor fails to submit a submittal schedule, the Contractor shall not be entitled to any increase in Contract Sum or extension of Contract Time based on the time required for review of submittals.

§ 3.10.3 The Contractor shall perform the Work in general accordance with the most recent schedules submitted to the Owner and Architect.

§ 3.11 DOCUMENTS AND SAMPLES AT THE SITE

The Contractor shall maintain at the site for the Owner one copy of the Drawings, Specifications, Addenda, Change Orders and other Modifications, in good order and marked currently to indicate field changes and selections made during construction, and one copy of approved Shop Drawings, Product Data, Samples and similar required submittals. These shall be available to the Architect and shall be delivered to the Architect for submittal to the Owner upon completion of the Work as a record of the Work as constructed.

Init.

§ 3.12 SHOP DRAWINGS, PRODUCT DATA AND SAMPLES

§ 3.12.1 Shop Drawings are drawings, diagrams, schedules and other data specially prepared for the Work by the Contractor or a Subcontractor, Sub-subcontractor, manufacturer, supplier or distributor to illustrate some portion of the Work.

§ 3.12.2 Product Data are illustrations, standard schedules, performance charts, instructions, brochures, diagrams and other information furnished by the Contractor to illustrate materials or equipment for some portion of the Work.

§ 3.12.3 Samples are physical examples that illustrate materials, equipment or workmanship and establish standards by which the Work will be judged.

§ 3.12.4 Shop Drawings, Product Data, Samples and similar submittals are not Contract Documents. Their purpose is to demonstrate the way by which the Contractor proposes to conform to the information given and the design concept expressed in the Contract Documents for those portions of the Work for which the Contract Documents require submittals. Review by the Architect is subject to the limitations of Section 4.2.7. Informational submittals upon which the Architect is not expected to take responsive action may be so identified in the Contract Documents. Submittals that are not required by the Contract Documents may be returned by the Architect without action.

§ 3.12.5 The Contractor shall review for compliance with the Contract Documents, approve and submit to the Architect Shop Drawings, Product Data, Samples and similar submittals required by the Contract Documents in accordance with the submittal schedule approved by the Architect or, in the absence of an approved submittal schedule, with reasonable promptness and in such sequence as to cause no delay in the Work or in the activities of the Owner or of separate contractors.

§ 3.12.6 By submitting Shop Drawings, Product Data, Samples and similar submittals, the Contractor represents to the Owner and Architect that the Contractor has (1) reviewed and approved them, (2) determined and verified materials, field measurements and field construction criteria related thereto, or will do so and (3) checked and coordinated the information contained within such submittals with the requirements of the Work and of the Contract Documents.

§ 3.12.7 The Contractor shall perform no portion of the Work for which the Contract Documents require submittal and review of Shop Drawings, Product Data, Samples or similar submittals until the respective submittal has been approved by the Architect.

§ 3.12.8 The Work shall be in accordance with approved submittals except that the Contractor shall not be relieved of responsibility for deviations from requirements of the Contract Documents by the Architect's approval of Shop Drawings, Product Data, Samples or similar submittals unless the Contractor has specifically informed the Architect in writing of such deviation at the time of submittal and (1) the Architect has given written approval to the specific deviation as a minor change in the Work, or (2) a Change Order or Construction Change Directive has been issued authorizing the deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Shop Drawings, Product Data, Samples or similar submittals by the Architect's approval thereof.

§ 3.12.9 The Contractor shall direct specific attention, in writing or on resubmitted Shop Drawings, Product Data, Samples or similar submittals, to revisions other than those requested by the Architect on previous submittals. In the absence of such written notice, the Architect's approval of a resubmission shall not apply to such revisions.

§ 3.12.10 The Contractor shall not be required to provide professional services that constitute the practice of architecture or engineering unless such services are specifically required by the Contract Documents for a portion of the Work or unless the Contractor needs to provide such services in order to carry out the Contractor's responsibilities for construction means, methods, techniques, sequences and procedures. The Contractor shall not be required to provide professional services in violation of applicable law. If professional design services or certifications by a design professional related to systems, materials or equipment are specifically required of the Contractor by the Contract Documents, the Owner and the Architect will specify all performance and design criteria that such services must satisfy. The Contractor shall cause such services or certifications to be provided by a properly licensed design professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, Shop Drawings and other submittals prepared by such professional. Shop Drawings and other submittals related to the Work designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to the Architect. The Owner and the Architect shall be entitled

Init.

to rely upon the adequacy, accuracy and completeness of the services, certifications and approvals performed or provided by such design professionals, provided the Owner and Architect have specified to the Contractor all performance and design criteria that such services must satisfy. Pursuant to this Section 3.12.10, the Architect will review, approve or take other appropriate action on submittals only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Contractor shall not be responsible for the adequacy of the performance and design criteria specified in the Contract Documents.

§ 3.13 USE OF SITE

The Contractor shall confine operations at the site to areas permitted by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities and the Contract Documents and shall not unreasonably encumber the site with materials or equipment.

§ 3.14 CUTTING AND PATCHING

§ 3.14.1 The Contractor shall be responsible for cutting, fitting or patching required to complete the Work or to make its parts fit together properly. All areas requiring cutting, fitting and patching shall be restored to the condition existing prior to the cutting, fitting and patching, unless otherwise required by the Contract Documents.

§ 3.14.2 The Contractor shall not damage or endanger a portion of the Work or fully or partially completed construction of the Owner or separate contractors by cutting, patching or otherwise altering such construction, or by excavation. The Contractor shall not cut or otherwise alter such construction by the Owner or a separate contractor except with written consent of the Owner and of such separate contractor; such consent shall not be unreasonably withheld. The Contractor shall not unreasonably withhold from the Owner or a separate contractor the Contractor's consent to cutting or otherwise altering the Work.

§ 3.15 CLEANING UP

§ 3.15.1 The Contractor shall keep the premises and surrounding area free from accumulation of waste materials or rubbish caused by operations under the Contract. At completion of the Work, the Contractor shall remove waste materials, rubbish, the Contractor's tools, construction equipment, machinery and surplus materials from and about the Project.

§ 3.15.2 If the Contractor fails to clean up as provided in the Contract Documents, the Owner may do so and Owner shall be entitled to reimbursement from the Contractor.

§ 3.16 ACCESS TO WORK

The Contractor shall provide the Owner and Architect access to the Work in preparation and progress wherever located.

§ 3.17 ROYALTIES, PATENTS AND COPYRIGHTS

The Contractor shall pay all royalties and license fees. The Contractor shall defend suits or claims for infringement of copyrights and patent rights and shall hold the Owner and Architect harmless from loss on account thereof, but shall not be responsible for such defense or loss when a particular design, process or product of a particular manufacturer or manufacturers is required by the Contract Documents, or where the copyright violations are contained in Drawings, Specifications or other documents prepared by the Owner or Architect. However, if the Contractor has reason to believe that the required design, process or product is an infringement of a copyright or a patent, the Contractor shall be responsible for such loss unless such information is promptly furnished to the Architect.

§ 3.18 INDEMNIFICATION

§ 3.18.1 To the fullest extent permitted by law the Contractor shall indemnify and hold harmless the Owner, Architect, Architect's consultants, and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work, provided that such claim, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself), but only to the extent caused by the negligent acts or omissions of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, regardless of whether or not such claim, damage, loss or expense is caused in part by a party indemnified hereunder. Such obligation shall not be construed to negate, abridge, or reduce

other rights or obligations of indemnity that would otherwise exist as to a party or person described in this Section 3.18.

§ 3.18.2 In claims against any person or entity indemnified under this Section 3.18 by an employee of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, the indemnification obligation under Section 3.18.1 shall not be limited by a limitation on amount or type of damages, compensation or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefit acts or other employee benefit acts.

ARTICLE 4 ARCHITECT

§ 4.1 GENERAL

§ 4.1.1 The Owner shall retain an architect lawfully licensed to practice architecture or an entity lawfully practicing architecture in the jurisdiction where the Project is located. That person or entity is identified as the Architect in the Agreement and is referred to throughout the Contract Documents as if singular in number.

§ 4.1.2 Duties, responsibilities and limitations of authority of the Architect as set forth in the Contract Documents shall not be restricted, modified or extended without written consent of the Owner, Contractor and Architect. Consent shall not be unreasonably withheld.

§ 4.1.3 If the employment of the Architect is terminated, the Owner shall employ a successor architect as to whom the Contractor has no reasonable objection and whose status under the Contract Documents shall be that of the Architect.

§ 4.2 ADMINISTRATION OF THE CONTRACT

§ 4.2.1 The Architect will provide administration of the Contract as described in the Contract Documents and will be an Owner's representative during construction until the date the Architect issues the final Certificate For Payment. The Architect will have authority to act on behalf of the Owner only to the extent provided in the Contract Documents.

§ 4.2.2 The Architect will visit the site at intervals appropriate to the stage of construction, or as otherwise agreed with the Owner, to become generally familiar with the progress and quality of the portion of the Work completed, and to determine in general if the Work observed is being performed in a manner indicating that the Work, when fully completed, will be in accordance with the Contract Documents. However, the Architect will not be required to make exhaustive or continuous on-site inspections to check the quality or quantity of the Work. The Architect will not have control over, charge of, or responsibility for, the construction means, methods, techniques, sequences or procedures, or for the safety precautions and programs in connection with the Work, since these are solely the Contractor's rights and responsibilities under the Contract Documents, except as provided in Section 3.3.1.

§ 4.2.3 On the basis of the site visits, the Architect will keep the Owner reasonably informed about the progress and quality of the portion of the Work completed, and report to the Owner (1) known deviations from the Contract Documents and from the most recent construction schedule submitted by the Contractor, and (2) defects and deficiencies observed in the Work. The Architect will not be responsible for the Contractor's failure to perform the Work in accordance with the requirements of the Contract Documents. The Architect will not have control over or charge of and will not be responsible for acts or omissions of the Contractor, Subcontractors, or their agents or employees, or any other persons or entities performing portions of the Work.

§ 4.2.4 COMMUNICATIONS FACILITATING CONTRACT ADMINISTRATION

Except as otherwise provided in the Contract Documents or when direct communications have been specially authorized, the Owner and Contractor shall endeavor to communicate with each other through the Architect about matters arising out of or relating to the Contract. Communications by and with the Architect's consultants shall be through the Architect. Communications by and with Subcontractors and material suppliers shall be through the Contractor. Communications by and with separate contractors shall be through the Owner.

§ 4.2.5 Based on the Architect's evaluations of the Contractor's Applications for Payment, the Architect will review and certify the amounts due the Contractor and will issue Certificates for Payment in such amounts.

§ 4.2.6 The Architect has authority to reject Work that does not conform to the Contract Documents. Whenever the Architect considers it necessary or advisable, the Architect will have authority to require inspection or testing of the

init.

Work in accordance with Sections 13.5.2 and 13.5.3, whether or not such Work is fabricated, installed or completed. However, neither this authority of the Architect nor a decision made in good faith either to exercise or not to exercise such authority shall give rise to a duty or responsibility of the Architect to the Contractor, Subcontractors, material and equipment suppliers, their agents or employees, or other persons or entities performing portions of the Work.

§ 4.2.7 The Architect will review and approve, or take other appropriate action upon, the Contractor's submittals such as Shop Drawings, Product Data and Samples, but only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Architect's action will be taken in accordance with the submittal schedule approved by the Architect or, in the absence of an approved submittal schedule, with reasonable promptness while allowing sufficient time in the Architect's professional judgment to permit adequate review. Review of such submittals is not conducted for the purpose of determining the accuracy and completeness of other details such as dimensions and quantities, or for substantiating instructions for installation or performance of equipment or systems, all of which remain the responsibility of the Contractor as required by the Contract Documents. The Architect's review of the Contractor's submittals shall not relieve the Contractor of the obligations under Sections 3.3, 3.5 and 3.12. The Architect's review shall not constitute approval of safety precautions or, unless otherwise specifically stated by the Architect, of any construction means, methods, techniques, sequences or procedures. The Architect's approval of a specific item shall not indicate approval of an assembly of which the item is a component.

§ 4.2.8 The Architect will prepare Change Orders and Construction Change Directives, and may authorize minor changes in the Work as provided in Section 7.4. The Architect will investigate and make determinations and recommendations regarding concealed and unknown conditions as provided in Section 3.7.4.

§ 4.2.9 The Architect will conduct inspections to determine the date or dates of Substantial Completion and the date of final completion; issue Certificates of Substantial Completion pursuant to Section 9.8; receive and forward to the Owner, for the Owner's review and records, written warranties and related documents required by the Contract and assembled by the Contractor pursuant to Section 9.10; and issue a final Certificate for Payment pursuant to Section 9.10.

§ 4.2.10 If the Owner and Architect agree, the Architect will provide one or more project representatives to assist in carrying out the Architect's responsibilities at the site. The duties, responsibilities and limitations of authority of such project representatives shall be as set forth in an exhibit to be incorporated in the Contract Documents.

§ 4.2.11 The Architect will interpret and decide matters concerning performance under, and requirements of, the Contract Documents on written request of either the Owner or Contractor. The Architect's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness.

§ 4.2.12 Interpretations and decisions of the Architect will be consistent with the intent of, and reasonably inferable from, the Contract Documents and will be in writing or in the form of drawings. When making such interpretations and decisions, the Architect will endeavor to secure faithful performance by both Owner and Contractor, will not show partiality to either and will not be liable for results of interpretations or decisions rendered in good faith.

§ 4.2.13 The Architect's decisions on matters relating to aesthetic effect will be final if consistent with the intent expressed in the Contract Documents.

§ 4.2.14 The Architect will review and respond to requests for information about the Contract Documents. The Architect's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness. If appropriate, the Architect will prepare and issue supplemental Drawings and Specifications in response to the requests for information.

ARTICLE 5 SUBCONTRACTORS

§ 5.1 DEFINITIONS

§ 5.1.1 A Subcontractor is a person or entity who has a direct contract with the Contractor to perform a portion of the Work at the site. The term "Subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Subcontractor or an authorized representative of the Subcontractor. The term "Subcontractor" does not include a separate contractor or subcontractors of a separate contractor.

§ 5.1.2 A Sub-subcontractor is a person or entity who has a direct or indirect contract with a Subcontractor to perform a portion of the Work at the site. The term "Sub-subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Sub-subcontractor or an authorized representative of the Sub-subcontractor.

§ 5.2 AWARD OF SUBCONTRACTS AND OTHER CONTRACTS FOR PORTIONS OF THE WORK

§ 5.2.1 Unless otherwise stated in the Contract Documents or the bidding requirements, the Contractor, as soon as practicable after award of the Contract, shall furnish in writing to the Owner through the Architect the names of persons or entities (including those who are to furnish materials or equipment fabricated to a special design) proposed for each principal portion of the Work. The Architect may reply within 14 days to the Contractor in writing stating (1) whether the Owner or the Architect has reasonable objection to any such proposed person or entity or (2) that the Architect requires additional time for review. Failure of the Owner or Architect to reply within the 14-day period shall constitute notice of no reasonable objection.

§ 5.2.2 The Contractor shall not contract with a proposed person or entity to whom the Owner or Architect has made reasonable and timely objection. The Contractor shall not be required to contract with anyone to whom the Contractor has made reasonable objection.

§ 5.2.3 If the Owner or Architect has reasonable objection to a person or entity proposed by the Contractor, the Contractor shall propose another to whom the Owner or Architect has no reasonable objection. If the proposed but rejected Subcontractor was reasonably capable of performing the Work, the Contract Sum and Contract Time shall be increased or decreased by the difference, if any, occasioned by such change, and an appropriate Change Order shall be issued before commencement of the substitute Subcontractor's Work. However, no increase in the Contract Sum or Contract Time shall be allowed for such change unless the Contractor has acted promptly and responsively in submitting names as required.

§ 5.2.4 The Contractor shall not substitute a Subcontractor, person or entity previously selected if the Owner or Architect makes reasonable objection to such substitution.

§ 5.3 SUBCONTRACTUAL RELATIONS

By appropriate agreement, written where legally required for validity, the Contractor shall require each Subcontractor, to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor by terms of the Contract Documents, and to assume toward the Contractor all the obligations and responsibilities, including the responsibility for safety of the Subcontractor's Work, which the Contractor, by these Documents, assumes toward the Owner and Architect. Each subcontract agreement shall preserve and protect the rights of the Owner and Architect under the Contract Documents with respect to the Work to be performed by the Subcontractor so that subcontracting thereof will not prejudice such rights, and shall allow to the Subcontractor, unless specifically provided otherwise in the subcontract agreement, the benefit of all rights, remedies and redress against the Contractor that the Contractor, by the Contract Documents, has against the Owner. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with Sub-subcontractors. The Contractor shall make available to each proposed Subcontractor, prior to the execution of the subcontract agreement, copies of the Contract Documents to which the Subcontractor will be bound, and, upon written request of the Subcontractor, identify to the Subcontractor terms and conditions of the proposed subcontract agreement that may be at variance with the Contract Documents. Subcontractors will similarly make copies of applicable portions of such documents available to their respective proposed Sub-subcontractors.

§ 5.4 CONTINGENT ASSIGNMENT OF SUBCONTRACTS

§ 5.4.1 Each subcontract agreement for a portion of the Work is assigned by the Contractor to the Owner, provided that

- .1 assignment is effective only after termination of the Contract by the Owner for cause pursuant to Section 14.2 and only for those subcontract agreements that the Owner accepts by notifying the Subcontractor and Contractor in writing; and
- .2 assignment is subject to the prior rights of the surety, if any, obligated under bond relating to the Contract.

When the Owner accepts the assignment of a subcontract agreement, the Owner assumes the Contractor's rights and obligations under the subcontract.

Init.

§ 5.4.2 Upon such assignment, if the Work has been suspended for more than 30 days, the Subcontractor's compensation shall be equitably adjusted for increases in cost resulting from the suspension.

§ 5.4.3 Upon such assignment to the Owner under this Section 5.4, the Owner may further assign the subcontract to a successor contractor or other entity. If the Owner assigns the subcontract to a successor contractor or other entity, the Owner shall nevertheless remain legally responsible for all of the successor contractor's obligations under the subcontract.

ARTICLE 6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

§ 6.1 OWNER'S RIGHT TO PERFORM CONSTRUCTION AND TO AWARD SEPARATE CONTRACTS

§ 6.1.1 The Owner reserves the right to perform construction or operations related to the Project with the Owner's own forces, and to award separate contracts in connection with other portions of the Project or other construction or operations on the site under Conditions of the Contract identical or substantially similar to these including those portions related to insurance and waiver of subrogation. If the Contractor claims that delay or additional cost is involved because of such action by the Owner, the Contractor shall make such Claim as provided in Article 15.

§ 6.1.2 When separate contracts are awarded for different portions of the Project or other construction or operations on the site, the term "Contractor" in the Contract Documents in each case shall mean the Contractor who executes each separate Owner-Contractor Agreement.

§ 6.1.3 The Owner shall provide for coordination of the activities of the Owner's own forces and of each separate contractor with the Work of the Contractor, who shall cooperate with them. The Contractor shall participate with other separate contractors and the Owner in reviewing their construction schedules. The Contractor shall make any revisions to the construction schedule deemed necessary after a joint review and mutual agreement. The construction schedules shall then constitute the schedules to be used by the Contractor, separate contractors and the Owner until subsequently revised.

§ 6.1.4 Unless otherwise provided in the Contract Documents, when the Owner performs construction or operations related to the Project with the Owner's own forces, the Owner shall be deemed to be subject to the same obligations and to have the same rights that apply to the Contractor under the Conditions of the Contract, including, without excluding others, those stated in Article 3, this Article 6 and Articles 10, 11 and 12.

§ 6.2 MUTUAL RESPONSIBILITY

§ 6.2.1 The Contractor shall afford the Owner and separate contractors reasonable opportunity for introduction and storage of their materials and equipment and performance of their activities, and shall connect and coordinate the Contractor's construction and operations with theirs as required by the Contract Documents.

§ 6.2.2 If part of the Contractor's Work depends for proper execution or results upon construction or operations by the Owner or a separate contractor, the Contractor shall, prior to proceeding with that portion of the Work, promptly report to the Architect apparent discrepancies or defects in such other construction that would render it unsuitable for such proper execution and results. Failure of the Contractor so to report shall constitute an acknowledgment that the Owner's or separate contractor's completed or partially completed construction is fit and proper to receive the Contractor's Work, except as to defects not then reasonably discoverable.

§ 6.2.3 The Contractor shall reimburse the Owner for costs the Owner incurs that are payable to a separate contractor because of the Contractor's delays, improperly timed activities or defective construction. The Owner shall be responsible to the Contractor for costs the Contractor incurs because of a separate contractor's delays, improperly timed activities, damage to the Work or defective construction.

§ 6.2.4 The Contractor shall promptly remedy damage the Contractor wrongfully causes to completed or partially completed construction or to property of the Owner, separate contractors as provided in Section 10.2.5.

§ 6.2.5 The Owner and each separate contractor shall have the same responsibilities for cutting and patching as are described for the Contractor in Section 3.14.

§ 6.3 OWNER'S RIGHT TO CLEAN UP

If a dispute arises among the Contractor, separate contractors and the Owner as to the responsibility under their respective contracts for maintaining the premises and surrounding area free from waste materials and rubbish, the Owner may clean up and the Architect will allocate the cost among those responsible.

ARTICLE 7 CHANGES IN THE WORK

§ 7.1 GENERAL

§ 7.1.1 Changes in the Work may be accomplished after execution of the Contract, and without invalidating the Contract, by Change Order, Construction Change Directive or order for a minor change in the Work, subject to the limitations stated in this Article 7 and elsewhere in the Contract Documents.

§ 7.1.2 A Change Order shall be based upon agreement among the Owner, Contractor and Architect; a Construction Change Directive requires agreement by the Owner and Architect and may or may not be agreed to by the Contractor; an order for a minor change in the Work may be issued by the Architect alone.

§ 7.1.3 Changes in the Work shall be performed under applicable provisions of the Contract Documents, and the Contractor shall proceed promptly, unless otherwise provided in the Change Order, Construction Change Directive or order for a minor change in the Work.

§ 7.2 CHANGE ORDERS

§ 7.2.1 A Change Order is a written instrument prepared by the Architect and signed by the Owner, Contractor and Architect stating their agreement upon all of the following:

- .1 The change in the Work;
- .2 The amount of the adjustment, if any, in the Contract Sum; and
- .3 The extent of the adjustment, if any, in the Contract Time.

§ 7.3 CONSTRUCTION CHANGE DIRECTIVES

§ 7.3.1 A Construction Change Directive is a written order prepared by the Architect and signed by the Owner and Architect, directing a change in the Work prior to agreement on adjustment, if any, in the Contract Sum or Contract Time, or both. The Owner may by Construction Change Directive, without invalidating the Contract, order changes in the Work within the general scope of the Contract consisting of additions, deletions or other revisions, the Contract Sum and Contract Time being adjusted accordingly.

§ 7.3.2 A Construction Change Directive shall be used in the absence of total agreement on the terms of a Change Order.

§ 7.3.3 If the Construction Change Directive provides for an adjustment to the Contract Sum, the adjustment shall be based on one of the following methods:

- .1 Mutual acceptance of a lump sum properly itemized and supported by sufficient substantiating data to permit evaluation;
- .2 Unit prices stated in the Contract Documents or subsequently agreed upon;
- .3 Cost to be determined in a manner agreed upon by the parties and a mutually acceptable fixed or percentage fee; or
- .4 As provided in Section 7.3.7.

§ 7.3.4 If unit prices are stated in the Contract Documents or subsequently agreed upon, and if quantities originally contemplated are materially changed in a proposed Change Order or Construction Change Directive so that application of such unit prices to quantities of Work proposed will cause substantial inequity to the Owner or Contractor, the applicable unit prices shall be equitably adjusted.

§ 7.3.5 Upon receipt of a Construction Change Directive, the Contractor shall promptly proceed with the change in the Work involved and advise the Architect of the Contractor's agreement or disagreement with the method, if any, provided in the Construction Change Directive for determining the proposed adjustment in the Contract Sum or Contract Time.

§ 7.3.6 A Construction Change Directive signed by the Contractor indicates the Contractor's agreement therewith, including adjustment in Contract Sum and Contract Time or the method for determining them. Such agreement shall be effective immediately and shall be recorded as a Change Order.

§ 7.3.7 If the Contractor does not respond promptly or disagrees with the method for adjustment in the Contract Sum, the Architect shall determine the method and the adjustment on the basis of reasonable expenditures and savings of those performing the Work attributable to the change, including, in case of an increase in the Contract Sum, an amount for overhead and profit as set forth in the Agreement, or if no such amount is set forth in the Agreement, a reasonable amount. In such case, and also under Section 7.3.3.3, the Contractor shall keep and present, in such form as the Architect may prescribe, an itemized accounting together with appropriate supporting data. Unless otherwise provided in the Contract Documents, costs for the purposes of this Section 7.3.7 shall be limited to the following:

- .1 Costs of labor, including social security, old age and unemployment insurance, fringe benefits required by agreement or custom, and workers' compensation insurance;
- .2 Costs of materials, supplies and equipment, including cost of transportation, whether incorporated or consumed;
- .3 Rental costs of machinery and equipment, exclusive of hand tools, whether rented from the Contractor or others;
- .4 Costs of premiums for all bonds and insurance, permit fees, and sales, use or similar taxes related to the Work; and
- .5 Additional costs of supervision and field office personnel directly attributable to the change.

§ 7.3.8 The amount of credit to be allowed by the Contractor to the Owner for a deletion or change that results in a net decrease in the Contract Sum shall be actual net cost as confirmed by the Architect. When both additions and credits covering related Work or substitutions are involved in a change, the allowance for overhead and profit shall be figured on the basis of net increase, if any, with respect to that change.

§ 7.3.9 Pending final determination of the total cost of a Construction Change Directive to the Owner, the Contractor may request payment for Work completed under the Construction Change Directive in Applications for Payment. The Architect will make an interim determination for purposes of monthly certification for payment for those costs and certify for payment the amount that the Architect determines, in the Architect's professional judgment, to be reasonably justified. The Architect's interim determination of cost shall adjust the Contract Sum on the same basis as a Change Order, subject to the right of either party to disagree and assert a Claim in accordance with Article 15.

§ 7.3.10 When the Owner and Contractor agree with a determination made by the Architect concerning the adjustments in the Contract Sum and Contract Time, or otherwise reach agreement upon the adjustments, such agreement shall be effective immediately and the Architect will prepare a Change Order. Change Orders may be issued for all or any part of a Construction Change Directive.

§ 7.4 MINOR CHANGES IN THE WORK

The Architect has authority to order minor changes in the Work not involving adjustment in the Contract Sum or extension of the Contract Time and not inconsistent with the intent of the Contract Documents. Such changes will be effected by written order signed by the Architect and shall be binding on the Owner and Contractor.

ARTICLE 8 TIME

§ 8.1 DEFINITIONS

§ 8.1.1 Unless otherwise provided, Contract Time is the period of time, including authorized adjustments, allotted in the Contract Documents for Substantial Completion of the Work.

§ 8.1.2 The date of commencement of the Work is the date established in the Agreement.

§ 8.1.3 The date of Substantial Completion is the date certified by the Architect in accordance with Section 9.8.

§ 8.1.4 The term "day" as used in the Contract Documents shall mean calendar day unless otherwise specifically defined.

§ 8.2 PROGRESS AND COMPLETION

§ 8.2.1 Time limits stated in the Contract Documents are of the essence of the Contract. By executing the Agreement the Contractor confirms that the Contract Time is a reasonable period for performing the Work.

§ 8.2.2 The Contractor shall not knowingly, except by agreement or instruction of the Owner in writing, prematurely commence operations on the site or elsewhere prior to the effective date of insurance required by Article 11 to be

furnished by the Contractor and Owner. The date of commencement of the Work shall not be changed by the effective date of such insurance.

§ 8.2.3 The Contractor shall proceed expeditiously with adequate forces and shall achieve Substantial Completion within the Contract Time.

§ 8.3 DELAYS AND EXTENSIONS OF TIME

§ 8.3.1 If the Contractor is delayed at any time in the commencement or progress of the Work by an act or neglect of the Owner or Architect, or of an employee of either, or of a separate contractor employed by the Owner; or by changes ordered in the Work; or by labor disputes, fire, unusual delay in deliveries, unavoidable casualties or other causes beyond the Contractor's control; or by delay authorized by the Owner pending mediation and arbitration; or by other causes that the Architect determines may justify delay, then the Contract Time shall be extended by Change Order for such reasonable time as the Architect may determine.

§ 8.3.2 Claims relating to time shall be made in accordance with applicable provisions of Article 15.

§ 8.3.3 This Section 8.3 does not preclude recovery of damages for delay by either party under other provisions of the Contract Documents.

ARTICLE 9 PAYMENTS AND COMPLETION

§ 9.1 CONTRACT SUM

The Contract Sum is stated in the Agreement and, including authorized adjustments, is the total amount payable by the Owner to the Contractor for performance of the Work under the Contract Documents.

§ 9.2 SCHEDULE OF VALUES

Where the Contract is based on a stipulated sum or Guaranteed Maximum Price, the Contractor shall submit to the Architect, before the first Application for Payment, a schedule of values allocating the entire Contract Sum to the various portions of the Work and prepared in such form and supported by such data to substantiate its accuracy as the Architect may require. This schedule, unless objected to by the Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 9.3 APPLICATIONS FOR PAYMENT

§ 9.3.1 At least ten days before the date established for each progress payment, the Contractor shall submit to the Architect an itemized Application for Payment prepared in accordance with the schedule of values, if required under Section 9.2., for completed portions of the Work. Such application shall be notarized, if required, and supported by such data substantiating the Contractor's right to payment as the Owner or Architect may require, such as copies of requisitions from Subcontractors and material suppliers, and shall reflect retainage if provided for in the Contract Documents.

§ 9.3.1.1 As provided in Section 7.3.9, such applications may include requests for payment on account of changes in the Work that have been properly authorized by Construction Change Directives, or by interim determinations of the Architect, but not yet included in Change Orders.

§ 9.3.1.2 Applications for Payment shall not include requests for payment for portions of the Work for which the Contractor does not intend to pay a Subcontractor or material supplier, unless such Work has been performed by others whom the Contractor intends to pay.

§ 9.3.2 Unless otherwise provided in the Contract Documents, payments shall be made on account of materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work. If approved in advance by the Owner, payment may similarly be made for materials and equipment suitably stored off the site at a location agreed upon in writing. Payment for materials and equipment stored on or off the site shall be conditioned upon compliance by the Contractor with procedures satisfactory to the Owner to establish the Owner's title to such materials and equipment or otherwise protect the Owner's interest, and shall include the costs of applicable insurance, storage and transportation to the site for such materials and equipment stored off the site.

§ 9.3.3 The Contractor warrants that title to all Work covered by an Application for Payment will pass to the Owner no later than the time of payment. The Contractor further warrants that upon submittal of an Application for Payment all Work for which Certificates for Payment have been previously issued and payments received from the

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

Owner shall, to the best of the Contractor's knowledge, information and belief, be free and clear of liens, claims, security interests or encumbrances in favor of the Contractor, Subcontractors, material suppliers, or other persons or entities making a claim by reason of having provided labor, materials and equipment relating to the Work.

§ 9.4 CERTIFICATES FOR PAYMENT

§ 9.4.1 The Architect will, within seven days after receipt of the Contractor's Application for Payment, either issue to the Owner a Certificate for Payment, with a copy to the Contractor, for such amount as the Architect determines is properly due, or notify the Contractor and Owner in writing of the Architect's reasons for withholding certification in whole or in part as provided in Section 9.5.1.

§ 9.4.2 The issuance of a Certificate for Payment will constitute a representation by the Architect to the Owner, based on the Architect's evaluation of the Work and the data comprising the Application for Payment, that, to the best of the Architect's knowledge, information and belief, the Work has progressed to the point indicated and that the quality of the Work is in accordance with the Contract Documents. The foregoing representations are subject to an evaluation of the Work for conformance with the Contract Documents upon Substantial Completion, to results of subsequent tests and inspections, to correction of minor deviations from the Contract Documents prior to completion and to specific qualifications expressed by the Architect. The issuance of a Certificate for Payment will further constitute a representation that the Contractor is entitled to payment in the amount certified. However, the issuance of a Certificate for Payment will not be a representation that the Architect has (1) made exhaustive or continuous on-site inspections to check the quality or quantity of the Work, (2) reviewed construction means, methods, techniques, sequences or procedures, (3) reviewed copies of requisitions received from Subcontractors and material suppliers and other data requested by the Owner to substantiate the Contractor's right to payment, or (4) made examination to ascertain how or for what purpose the Contractor has used money previously paid on account of the Contract Sum.

§ 9.5 DECISIONS TO WITHHOLD CERTIFICATION

§ 9.5.1 The Architect may withhold a Certificate for Payment in whole or in part, to the extent reasonably necessary to protect the Owner, if in the Architect's opinion the representations to the Owner required by Section 9.4.2 cannot be made. If the Architect is unable to certify payment in the amount of the Application, the Architect will notify the Contractor and Owner as provided in Section 9.4.1. If the Contractor and Architect cannot agree on a revised amount, the Architect will promptly issue a Certificate for Payment for the amount for which the Architect is able to make such representations to the Owner. The Architect may also withhold a Certificate for Payment or, because of subsequently discovered evidence, may nullify the whole or a part of a Certificate for Payment previously issued, to such extent as may be necessary in the Architect's opinion to protect the Owner from loss for which the Contractor is responsible, including loss resulting from acts and omissions described in Section 3.3.2, because of

- .1 defective Work not remedied;
- .2 third party claims filed or reasonable evidence indicating probable filing of such claims unless security acceptable to the Owner is provided by the Contractor;
- .3 failure of the Contractor to make payments properly to Subcontractors or for labor, materials or equipment;
- .4 reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Sum;
- .5 damage to the Owner or a separate contractor;
- .6 reasonable evidence that the Work will not be completed within the Contract Time, and that the unpaid balance would not be adequate to cover actual or liquidated damages for the anticipated delay;
- or
- .7 repeated failure to carry out the Work in accordance with the Contract Documents.

§ 9.5.2 When the above reasons for withholding certification are removed, certification will be made for amounts previously withheld.

§ 9.5.3 If the Architect withholds certification for payment under Section 9.5.1.3, the Owner may, at its sole option, issue joint checks to the Contractor and to any Subcontractor or material or equipment suppliers to whom the Contractor failed to make payment for Work properly performed or material or equipment suitably delivered. If the Owner makes payments by joint check, the Owner shall notify the Architect and the Architect will reflect such payment on the next Certificate for Payment.

§ 9.6 PROGRESS PAYMENTS

§ 9.6.1 After the Architect has issued a Certificate for Payment, the Owner shall make payment in the manner and within the time provided in the Contract Documents, and shall so notify the Architect.

Init.

§ 9.6.2 The Contractor shall pay each Subcontractor no later than seven days after receipt of payment from the Owner the amount to which the Subcontractor is entitled, reflecting percentages actually retained from payments to the Contractor on account of the Subcontractor's portion of the Work. The Contractor shall, by appropriate agreement with each Subcontractor, require each Subcontractor to make payments to Sub-subcontractors in a similar manner.

§ 9.6.3 The Architect will, on request, furnish to a Subcontractor, if practicable, information regarding percentages of completion or amounts applied for by the Contractor and action taken thereon by the Architect and Owner on account of portions of the Work done by such Subcontractor.

§ 9.6.4 The Owner has the right to request written evidence from the Contractor that the Contractor has properly paid Subcontractors and material and equipment suppliers amounts paid by the Owner to the Contractor for subcontracted Work. If the Contractor fails to furnish such evidence within seven days, the Owner shall have the right to contact Subcontractors to ascertain whether they have been properly paid. Neither the Owner nor Architect shall have an obligation to pay or to see to the payment of money to a Subcontractor, except as may otherwise be required by law.

§ 9.6.5 Contractor payments to material and equipment suppliers shall be treated in a manner similar to that provided in Sections 9.6.2, 9.6.3 and 9.6.4.

§ 9.6.6 A Certificate for Payment, a progress payment, or partial or entire use or occupancy of the Project by the Owner shall not constitute acceptance of Work not in accordance with the Contract Documents.

§ 9.6.7 Unless the Contractor provides the Owner with a payment bond in the full penal sum of the Contract Sum, payments received by the Contractor for Work properly performed by Subcontractors and suppliers shall be held by the Contractor for those Subcontractors or suppliers who performed Work or furnished materials, or both, under contract with the Contractor for which payment was made by the Owner. Nothing contained herein shall require money to be placed in a separate account and not commingled with money of the Contractor, shall create any fiduciary liability or tort liability on the part of the Contractor for breach of trust or shall entitle any person or entity to an award of punitive damages against the Contractor for breach of the requirements of this provision.

§ 9.7 FAILURE OF PAYMENT

If the Architect does not issue a Certificate for Payment, through no fault of the Contractor, within seven days after receipt of the Contractor's Application for Payment, or if the Owner does not pay the Contractor within seven days after the date established in the Contract Documents the amount certified by the Architect or awarded by binding dispute resolution, then the Contractor may, upon seven additional days' written notice to the Owner and Architect, stop the Work until payment of the amount owing has been received. The Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shut-down, delay and start-up, plus interest as provided for in the Contract Documents.

§ 9.8 SUBSTANTIAL COMPLETION

§ 9.8.1 Substantial Completion is the stage in the progress of the Work when the Work or designated portion thereof is sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work for its intended use.

§ 9.8.2 When the Contractor considers that the Work, or a portion thereof which the Owner agrees to accept separately, is substantially complete, the Contractor shall prepare and submit to the Architect a comprehensive list of items to be completed or corrected prior to final payment. Failure to include an item on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents.

§ 9.8.3 Upon receipt of the Contractor's list, the Architect will make an inspection to determine whether the Work or designated portion thereof is substantially complete. If the Architect's inspection discloses any item, whether or not included on the Contractor's list, which is not sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work or designated portion thereof for its intended use, the Contractor shall, before issuance of the Certificate of Substantial Completion, complete or correct such item upon notification by the Architect. In such case, the Contractor shall then submit a request for another inspection by the Architect to determine Substantial Completion.

Init.

§ 9.8.4 When the Work or designated portion thereof is substantially complete, the Architect will prepare a Certificate of Substantial Completion that shall establish the date of Substantial Completion, shall establish responsibilities of the Owner and Contractor for security, maintenance, heat, utilities, damage to the Work and insurance, and shall fix the time within which the Contractor shall finish all items on the list accompanying the Certificate. Warranties required by the Contract Documents shall commence on the date of Substantial Completion of the Work or designated portion thereof unless otherwise provided in the Certificate of Substantial Completion.

§ 9.8.5 The Certificate of Substantial Completion shall be submitted to the Owner and Contractor for their written acceptance of responsibilities assigned to them in such Certificate. Upon such acceptance and consent of surety, if any, the Owner shall make payment of retainage applying to such Work or designated portion thereof. Such payment shall be adjusted for Work that is incomplete or not in accordance with the requirements of the Contract Documents.

§ 9.9 PARTIAL OCCUPANCY OR USE

§ 9.9.1 The Owner may occupy or use any completed or partially completed portion of the Work at any stage when such portion is designated by separate agreement with the Contractor, provided such occupancy or use is consented to by the insurer as required under Section 11.3.1.5 and authorized by public authorities having jurisdiction over the Project. Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner and Contractor have accepted in writing the responsibilities assigned to each of them for payments, retainage, if any, security, maintenance, heat, utilities, damage to the Work and insurance, and have agreed in writing concerning the period for correction of the Work and commencement of warranties required by the Contract Documents. When the Contractor considers a portion substantially complete, the Contractor shall prepare and submit a list to the Architect as provided under Section 9.8.2. Consent of the Contractor to partial occupancy or use shall not be unreasonably withheld. The stage of the progress of the Work shall be determined by written agreement between the Owner and Contractor or, if no agreement is reached, by decision of the Architect.

§ 9.9.2 Immediately prior to such partial occupancy or use, the Owner, Contractor and Architect shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

§ 9.9.3 Unless otherwise agreed upon, partial occupancy or use of a portion or portions of the Work shall not constitute acceptance of Work not complying with the requirements of the Contract Documents.

§ 9.10 FINAL COMPLETION AND FINAL PAYMENT

§ 9.10.1 Upon receipt of the Contractor's written notice that the Work is ready for final inspection and acceptance and upon receipt of a final Application for Payment, the Architect will promptly make such inspection and, when the Architect finds the Work acceptable under the Contract Documents and the Contract fully performed, the Architect will promptly issue a final Certificate for Payment stating that to the best of the Architect's knowledge, information and belief, and on the basis of the Architect's on-site visits and inspections, the Work has been completed in accordance with terms and conditions of the Contract Documents and that the entire balance found to be due the Contractor and noted in the final Certificate is due and payable. The Architect's final Certificate for Payment will constitute a further representation that conditions listed in Section 9.10.2 as precedent to the Contractor's being entitled to final payment have been fulfilled.

§ 9.10.2 Neither final payment nor any remaining retained percentage shall become due until the Contractor submits to the Architect (1) an affidavit that payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or the Owner's property might be responsible or encumbered (less amounts withheld by Owner) have been paid or otherwise satisfied, (2) a certificate evidencing that insurance required by the Contract Documents to remain in force after final payment is currently in effect and will not be canceled or allowed to expire until at least 30 days' prior written notice has been given to the Owner, (3) a written statement that the Contractor knows of no substantial reason that the insurance will not be renewable to cover the period required by the Contract Documents, (4) consent of surety, if any, to final payment and (5), if required by the Owner, other data establishing payment or satisfaction of obligations, such as receipts, releases and waivers of liens, claims, security interests or encumbrances arising out of the Contract, to the extent and in such form as may be designated by the Owner. If a Subcontractor refuses to furnish a release or waiver required by the Owner, the Contractor may furnish a bond satisfactory to the Owner to indemnify the Owner against such lien. If such lien remains unsatisfied after payments are made, the Contractor shall refund to the Owner all money that the Owner may be compelled to pay in discharging such lien, including all costs and reasonable attorneys' fees.

§ 9.10.3 If, after Substantial Completion of the Work, final completion thereof is materially delayed through no fault of the Contractor or by issuance of Change Orders affecting final completion, and the Architect so confirms, the Owner shall, upon application by the Contractor and certification by the Architect, and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed and accepted. If the remaining balance for Work not fully completed or corrected is less than retainage stipulated in the Contract Documents, and if bonds have been furnished, the written consent of surety to payment of the balance due for that portion of the Work fully completed and accepted shall be submitted by the Contractor to the Architect prior to certification of such payment. Such payment shall be made under terms and conditions governing final payment, except that it shall not constitute a waiver of claims.

§ 9.10.4 The making of final payment shall constitute a waiver of Claims by the Owner except those arising from

- .1 liens, Claims, security interests or encumbrances arising out of the Contract and unsettled;
- .2 failure of the Work to comply with the requirements of the Contract Documents; or
- .3 terms of special warranties required by the Contract Documents.

§ 9.10.5 Acceptance of final payment by the Contractor, a Subcontractor or material supplier shall constitute a waiver of claims by that payee except those previously made in writing and identified by that payee as unsettled at the time of final Application for Payment.

ARTICLE 10 PROTECTION OF PERSONS AND PROPERTY

§ 10.1 SAFETY PRECAUTIONS AND PROGRAMS

The Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the performance of the Contract.

§ 10.2 SAFETY OF PERSONS AND PROPERTY

§ 10.2.1 The Contractor shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, injury or loss to

- .1 employees on the Work and other persons who may be affected thereby;
- .2 the Work and materials and equipment to be incorporated therein, whether in storage on or off the site, under care, custody or control of the Contractor or the Contractor's Subcontractors or Sub-subcontractors; and
- .3 other property at the site or adjacent thereto, such as trees, shrubs, lawns, walks, pavements, roadways, structures and utilities not designated for removal, relocation or replacement in the course of construction.

§ 10.2.2 The Contractor shall comply with and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities bearing on safety of persons or property or their protection from damage, injury or loss.

§ 10.2.3 The Contractor shall erect and maintain, as required by existing conditions and performance of the Contract, reasonable safeguards for safety and protection, including posting danger signs and other warnings against hazards, promulgating safety regulations and notifying owners and users of adjacent sites and utilities.

§ 10.2.4 When use or storage of explosives or other hazardous materials or equipment or unusual methods are necessary for execution of the Work, the Contractor shall exercise utmost care and carry on such activities under supervision of properly qualified personnel.

§ 10.2.5 The Contractor shall promptly remedy damage and loss (other than damage or loss insured under property insurance required by the Contract Document(s) to property referred to in Sections 10.2.1.2 and 10.2.1.3 caused in whole or in part by the Contractor, a Subcontractor, a Sub-subcontractor, or anyone directly or indirectly employed by any of them, or by anyone for whose acts they may be liable and for which the Contractor is responsible under Sections 10.2.1.2 and 10.2.1.3, except damage or loss attributable to acts or omissions of the Owner or Architect or anyone directly or indirectly employed by either of them, or by anyone for whose acts either of them may be liable, and not attributable to the fault or negligence of the Contractor. The foregoing obligations of the Contractor are in addition to the Contractor's obligations under Section 3.18.

§ 10.2.6 The Contractor shall designate a responsible member of the Contractor's organization at the site whose duty shall be the prevention of accidents. This person shall be the Contractor's superintendent unless otherwise designated by the Contractor in writing to the Owner and Architect.

§ 10.2.7 The Contractor shall not permit any part of the construction or site to be loaded so as to cause damage or create an unsafe condition.

§ 10.2.8 INJURY OR DAMAGE TO PERSON OR PROPERTY

If either party suffers injury or damage to person or property because of an act or omission of the other party, or of others for whose acts such party is legally responsible, written notice of such injury or damage, whether or not insured, shall be given to the other party within a reasonable time not exceeding 21 days after discovery. The notice shall provide sufficient detail to enable the other party to investigate the matter.

§ 10.3 HAZARDOUS MATERIALS

§ 10.3.1 The Contractor is responsible for compliance with any requirements included in the Contract Documents regarding hazardous materials. If the Contractor encounters a hazardous material or substance not addressed in the Contract Documents and if reasonable precautions will be inadequate to prevent foreseeable bodily injury or death to persons resulting from a material or substance, including but not limited to asbestos or polychlorinated biphenyl (PCB), encountered on the site by the Contractor, the Contractor shall, upon recognizing the condition, immediately stop Work in the affected area and report the condition to the Owner and Architect in writing.

§ 10.3.2 Upon receipt of the Contractor's written notice, the Owner shall obtain the services of a licensed laboratory to verify the presence or absence of the material or substance reported by the Contractor and, in the event such material or substance is found to be present, to cause it to be rendered harmless. Unless otherwise required by the Contract Documents, the Owner shall furnish in writing to the Contractor and Architect the names and qualifications of persons or entities who are to perform tests verifying the presence or absence of such material or substance or who are to perform the task of removal or safe containment of such material or substance. The Contractor and the Architect will promptly reply to the Owner in writing stating whether or not either has reasonable objection to the persons or entities proposed by the Owner. If either the Contractor or Architect has an objection to a person or entity proposed by the Owner, the Owner shall propose another to whom the Contractor and the Architect have no reasonable objection. When the material or substance has been rendered harmless, Work in the affected area shall resume upon written agreement of the Owner and Contractor. By Change Order, the Contract Time shall be extended appropriately and the Contract Sum shall be increased in the amount of the Contractor's reasonable additional costs of shut-down, delay and start-up.

§ 10.3.3 To the fullest extent permitted by law, the Owner shall indemnify and hold harmless the Contractor, Subcontractors, Architect, Architect's consultants and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work in the affected area if in fact the material or substance presents the risk of bodily injury or death as described in Section 10.3.1 and has not been rendered harmless, provided that such claim, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself), except to the extent that such damage, loss or expense is due to the fault or negligence of the party seeking indemnity.

§ 10.3.4 The Owner shall not be responsible under this Section 10.3 for materials or substances the Contractor brings to the site unless such materials or substances are required by the Contract Documents. The Owner shall be responsible for materials or substances required by the Contract Documents, except to the extent of the Contractor's fault or negligence in the use and handling of such materials or substances.

§ 10.3.5 The Contractor shall indemnify the Owner for the cost and expense the Owner incurs (1) for remediation of a material or substance the Contractor brings to the site and negligently handles, or (2) where the Contractor fails to perform its obligations under Section 10.3.1, except to the extent that the cost and expense are due to the Owner's fault or negligence.

§ 10.3.6 If, without negligence on the part of the Contractor, the Contractor is held liable by a government agency for the cost of remediation of a hazardous material or substance solely by reason of performing Work as required by the Contract Documents, the Owner shall indemnify the Contractor for all cost and expense thereby incurred.

Init.

§ 10.4 EMERGENCIES

In an emergency affecting safety of persons or property, the Contractor shall act, at the Contractor's discretion, to prevent threatened damage, injury or loss. Additional compensation or extension of time claimed by the Contractor on account of an emergency shall be determined as provided in Article 15 and Article 7.

ARTICLE 11 INSURANCE AND BONDS

§ 11.1 CONTRACTOR'S LIABILITY INSURANCE

§ 11.1.1 The Contractor shall purchase from and maintain in a company or companies lawfully authorized to do business in the jurisdiction in which the Project is located such insurance as will protect the Contractor from claims set forth below which may arise out of or result from the Contractor's operations and completed operations under the Contract and for which the Contractor may be legally liable, whether such operations be by the Contractor or by a Subcontractor or by anyone directly or indirectly employed by any of them, or by anyone for whose acts any of them may be liable:

- .1 Claims under workers' compensation, disability benefit and other similar employee benefit acts that are applicable to the Work to be performed;
- .2 Claims for damages because of bodily injury, occupational sickness or disease, or death of the Contractor's employees;
- .3 Claims for damages because of bodily injury, sickness or disease, or death of any person other than the Contractor's employees;
- .4 Claims for damages insured by usual personal injury liability coverage;
- .5 Claims for damages, other than to the Work itself, because of injury to or destruction of tangible property, including loss of use resulting therefrom;
- .6 Claims for damages because of bodily injury, death of a person or property damage arising out of ownership, maintenance or use of a motor vehicle;
- .7 Claims for bodily injury or property damage arising out of completed operations; and
- .8 Claims involving contractual liability insurance applicable to the Contractor's obligations under Section 3.18.

§ 11.1.2 The insurance required by Section 11.1.1 shall be written for not less than limits of liability specified in the Contract Documents or required by law, whichever coverage is greater. Coverages, whether written on an occurrence or claims-made basis, shall be maintained without interruption from the date of commencement of the Work until the date of final payment and termination of any coverage required to be maintained after final payment, and, with respect to the Contractor's completed operations coverage, until the expiration of the period for correction of Work or for such other period for maintenance of completed operations coverage as specified in the Contract Documents.

§ 11.1.3 Certificates of insurance acceptable to the Owner shall be filed with the Owner prior to commencement of the Work and thereafter upon renewal or replacement of each required policy of insurance. These certificates and the insurance policies required by this Section 11.1 shall contain a provision that coverages afforded under the policies will not be canceled or allowed to expire until at least 30 days' prior written notice has been given to the Owner. An additional certificate evidencing continuation of liability coverage, including coverage for completed operations, shall be submitted with the final Application for Payment as required by Section 9.10.2 and thereafter upon renewal or replacement of such coverage until the expiration of the time required by Section 11.1.2. Information concerning reduction of coverage on account of revised limits or claims paid under the General Aggregate, or both, shall be furnished by the Contractor with reasonable promptness.

§ 11.1.4 The Contractor shall cause the commercial liability coverage required by the Contract Documents to include (1) the Owner, the Architect and the Architect's Consultants as additional insureds for claims caused in whole or in part by the Contractor's negligent acts or omissions during the Contractor's operations; and (2) the Owner as an additional insured for claims caused in whole or in part by the Contractor's negligent acts or omissions during the Contractor's completed operations.

§ 11.2 OWNER'S LIABILITY INSURANCE

The Owner shall be responsible for purchasing and maintaining the Owner's usual liability insurance.

§ 11.3 PROPERTY INSURANCE

§ 11.3.1 Unless otherwise provided, the Owner shall purchase and maintain, in a company or companies lawfully authorized to do business in the jurisdiction in which the Project is located, property insurance written on a builder's

Init.

risk "all-risk" or equivalent policy form in the amount of the initial Contract Sum, plus value of subsequent Contract Modifications and cost of materials supplied or installed by others, comprising total value for the entire Project at the site on a replacement cost basis without optional deductibles. Such property insurance shall be maintained, unless otherwise provided in the Contract Documents or otherwise agreed in writing by all persons and entities who are beneficiaries of such insurance, until final payment has been made as provided in Section 9.10 or until no person or entity other than the Owner has an insurable interest in the property required by this Section 11.3 to be covered, whichever is later. This insurance shall include interests of the Owner, the Contractor, Subcontractors and Sub-subcontractors in the Project.

§ 11.3.1.1 Property insurance shall be on an "all-risk" or equivalent policy form and shall include, without limitation, insurance against the perils of fire (with extended coverage) and physical loss or damage including, without duplication of coverage, theft, vandalism, malicious mischief, collapse, earthquake, flood, windstorm, falsework, testing and startup, temporary buildings and debris removal including demolition occasioned by enforcement of any applicable legal requirements, and shall cover reasonable compensation for Architect's and Contractor's services and expenses required as a result of such insured loss.

§ 11.3.1.2 If the Owner does not intend to purchase such property insurance required by the Contract and with all of the coverages in the amount described above, the Owner shall so inform the Contractor in writing prior to commencement of the Work. The Contractor may then effect insurance that will protect the interests of the Contractor, Subcontractors and Sub-subcontractors in the Work, and by appropriate Change Order the cost thereof shall be charged to the Owner. If the Contractor is damaged by the failure or neglect of the Owner to purchase or maintain insurance as described above, without so notifying the Contractor in writing, then the Owner shall bear all reasonable costs properly attributable thereto.

§ 11.3.1.3 If the property insurance requires deductibles, the Owner shall pay costs not covered because of such deductibles.

§ 11.3.1.4 This property insurance shall cover portions of the Work stored off the site, and also portions of the Work in transit.

§ 11.3.1.5 Partial occupancy or use in accordance with Section 9.9 shall not commence until the insurance company or companies providing property insurance have consented to such partial occupancy or use by endorsement or otherwise. The Owner and the Contractor shall take reasonable steps to obtain consent of the insurance company or companies and shall, without mutual written consent, take no action with respect to partial occupancy or use that would cause cancellation, lapse or reduction of insurance.

§ 11.3.2 BOILER AND MACHINERY INSURANCE

The Owner shall purchase and maintain boiler and machinery insurance required by the Contract Documents or by law, which shall specifically cover such insured objects during installation and until final acceptance by the Owner; this insurance shall include interests of the Owner, Contractor, Subcontractors and Sub-subcontractors in the Work, and the Owner and Contractor shall be named insureds.

§ 11.3.3 LOSS OF USE INSURANCE

The Owner, at the Owner's option, may purchase and maintain such insurance as will insure the Owner against loss of use of the Owner's property due to fire or other hazards, however caused. The Owner waives all rights of action against the Contractor for loss of use of the Owner's property, including consequential losses due to fire or other hazards however caused.

§ 11.3.4 If the Contractor requests in writing that insurance for risks other than those described herein or other special causes of loss be included in the property insurance policy, the Owner shall, if possible, include such insurance, and the cost thereof shall be charged to the Contractor by appropriate Change Order.

§ 11.3.5 If during the Project construction period the Owner insures properties, real or personal or both, at or adjacent to the site by property insurance under policies separate from those insuring the Project, or if after final payment property insurance is to be provided on the completed Project through a policy or policies other than those insuring the Project during the construction period, the Owner shall waive all rights in accordance with the terms of Section 11.3.7 for damages caused by fire or other causes of loss covered by this separate property insurance. All separate policies shall provide this waiver of subrogation by endorsement or otherwise.

Init.

§ 11.3.6 Before an exposure to loss may occur, the Owner shall file with the Contractor a copy of each policy that includes insurance coverages required by this Section 11.3. Each policy shall contain all generally applicable conditions, definitions, exclusions and endorsements related to this Project. Each policy shall contain a provision that the policy will not be canceled or allowed to expire, and that its limits will not be reduced, until at least 30 days' prior written notice has been given to the Contractor.

§ 11.3.7 WAIVERS OF SUBROGATION

The Owner and Contractor waive all rights against (1) each other and any of their subcontractors, sub-subcontractors, agents and employees, each of the other, and (2) the Architect, Architect's consultants, separate contractors described in Article 6, if any, and any of their subcontractors, sub-subcontractors, agents and employees, for damages caused by fire or other causes of loss to the extent covered by property insurance obtained pursuant to this Section 11.3 or other property insurance applicable to the Work, except such rights as they have to proceeds of such insurance held by the Owner as fiduciary. The Owner or Contractor, as appropriate, shall require of the Architect, Architect's consultants, separate contractors described in Article 6, if any, and the subcontractors, sub-subcontractors, agents and employees of any of them, by appropriate agreements, written where legally required for validity, similar waivers each in favor of other parties enumerated herein. The policies shall provide such waivers of subrogation by endorsement or otherwise. A waiver of subrogation shall be effective as to a person or entity even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, did not pay the insurance premium directly or indirectly, and whether or not the person or entity had an insurable interest in the property damaged.

§ 11.3.8 A loss insured under the Owner's property insurance shall be adjusted by the Owner as fiduciary and made payable to the Owner as fiduciary for the insureds, as their interests may appear, subject to requirements of any applicable mortgagee clause and of Section 11.3.10. The Contractor shall pay Subcontractors their just shares of insurance proceeds received by the Contractor, and by appropriate agreements, written where legally required for validity, shall require Subcontractors to make payments to their Sub-subcontractors in similar manner.

§ 11.3.9 If required in writing by a party in interest, the Owner as fiduciary shall, upon occurrence of an insured loss, give bond for proper performance of the Owner's duties. The cost of required bonds shall be charged against proceeds received as fiduciary. The Owner shall deposit in a separate account proceeds so received, which the Owner shall distribute in accordance with such agreement as the parties in interest may reach, or as determined in accordance with the method of binding dispute resolution selected in the Agreement between the Owner and Contractor. If after such loss no other special agreement is made and unless the Owner terminates the Contract for convenience, replacement of damaged property shall be performed by the Contractor after notification of a Change in the Work in accordance with Article 7.

§ 11.3.10 The Owner as fiduciary shall have power to adjust and settle a loss with insurers unless one of the parties in interest shall object in writing within five days after occurrence of loss to the Owner's exercise of this power; if such objection is made, the dispute shall be resolved in the manner selected by the Owner and Contractor as the method of binding dispute resolution in the Agreement. If the Owner and Contractor have selected arbitration as the method of binding dispute resolution, the Owner as fiduciary shall make settlement with insurers or, in the case of a dispute over distribution of insurance proceeds, in accordance with the directions of the arbitrators.

§ 11.4 PERFORMANCE BOND AND PAYMENT BOND

§ 11.4.1 The Owner shall have the right to require the Contractor to furnish bonds covering faithful performance of the Contract and payment of obligations arising thereunder as stipulated in bidding requirements or specifically required in the Contract Documents on the date of execution of the Contract.

§ 11.4.2 Upon the request of any person or entity appearing to be a potential beneficiary of bonds covering payment of obligations arising under the Contract, the Contractor shall promptly furnish a copy of the bonds or shall authorize a copy to be furnished.

ARTICLE 12 UNCOVERING AND CORRECTION OF WORK

§ 12.1 UNCOVERING OF WORK

§ 12.1.1 If a portion of the Work is covered contrary to the Architect's request or to requirements specifically expressed in the Contract Documents, it must, if requested in writing by the Architect, be uncovered for the Architect's examination and be replaced at the Contractor's expense without change in the Contract Time.

Init.

§ 12.1.2 If a portion of the Work has been covered that the Architect has not specifically requested to examine prior to its being covered, the Architect may request to see such Work and it shall be uncovered by the Contractor. If such Work is in accordance with the Contract Documents, costs of uncovering and replacement shall, by appropriate Change Order, be at the Owner's expense. If such Work is not in accordance with the Contract Documents, such costs and the cost of correction shall be at the Contractor's expense unless the condition was caused by the Owner or a separate contractor in which event the Owner shall be responsible for payment of such costs.

§ 12.2 CORRECTION OF WORK

§ 12.2.1 BEFORE OR AFTER SUBSTANTIAL COMPLETION

The Contractor shall promptly correct Work rejected by the Architect or failing to conform to the requirements of the Contract Documents, whether discovered before or after Substantial Completion and whether or not fabricated, installed or completed. Costs of correcting such rejected Work, including additional testing and inspections, the cost of uncovering and replacement, and compensation for the Architect's services and expenses made necessary thereby, shall be at the Contractor's expense.

§ 12.2.2 AFTER SUBSTANTIAL COMPLETION

§ 12.2.2.1 In addition to the Contractor's obligations under Section 3.5, if, within one year after the date of Substantial Completion of the Work or designated portion thereof or after the date for commencement of warranties established under Section 9.9.1, or by terms of an applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, the Contractor shall correct it promptly after receipt of written notice from the Owner to do so unless the Owner has previously given the Contractor a written acceptance of such condition. The Owner shall give such notice promptly after discovery of the condition. During the one-year period for correction of Work, if the Owner fails to notify the Contractor and give the Contractor an opportunity to make the correction, the Owner waives the rights to require correction by the Contractor and to make a claim for breach of warranty. If the Contractor fails to correct nonconforming Work within a reasonable time during that period after receipt of notice from the Owner or Architect, the Owner may correct it in accordance with Section 2.4.

§ 12.2.2.2 The one-year period for correction of Work shall be extended with respect to portions of Work first performed after Substantial Completion by the period of time between Substantial Completion and the actual completion of that portion of the Work.

§ 12.2.2.3 The one-year period for correction of Work shall not be extended by corrective Work performed by the Contractor pursuant to this Section 12.2.

§ 12.2.3 The Contractor shall remove from the site portions of the Work that are not in accordance with the requirements of the Contract Documents and are neither corrected by the Contractor nor accepted by the Owner.

§ 12.2.4 The Contractor shall bear the cost of correcting destroyed or damaged construction, whether completed or partially completed, of the Owner or separate contractors caused by the Contractor's correction or removal of Work that is not in accordance with the requirements of the Contract Documents.

§ 12.2.5 Nothing contained in this Section 12.2 shall be construed to establish a period of limitation with respect to other obligations the Contractor has under the Contract Documents. Establishment of the one-year period for correction of Work as described in Section 12.2.2 relates only to the specific obligation of the Contractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Contractor's liability with respect to the Contractor's obligations other than specifically to correct the Work.

§ 12.3 ACCEPTANCE OF NONCONFORMING WORK

If the Owner prefers to accept Work that is not in accordance with the requirements of the Contract Documents, the Owner may do so instead of requiring its removal and correction, in which case the Contract Sum will be reduced as appropriate and equitable. Such adjustment shall be effected whether or not final payment has been made.

ARTICLE 13 MISCELLANEOUS PROVISIONS

§ 13.1 GOVERNING LAW

The Contract shall be governed by the law of the place where the Project is located except that, if the parties have selected arbitration as the method of binding dispute resolution, the Federal Arbitration Act shall govern Section 15.4.

§ 13.2 SUCCESSORS AND ASSIGNS

§ 13.2.1 The Owner and Contractor respectively bind themselves, their partners, successors, assigns and legal representatives to covenants, agreements and obligations contained in the Contract Documents. Except as provided in Section 13.2.2, neither party to the Contract shall assign the Contract as a whole without written consent of the other. If either party attempts to make such an assignment without such consent, that party shall nevertheless remain legally responsible for all obligations under the Contract.

§ 13.2.2 The Owner may, without consent of the Contractor, assign the Contract to a lender providing construction financing for the Project, if the lender assumes the Owner's rights and obligations under the Contract Documents. The Contractor shall execute all consents reasonably required to facilitate such assignment.

§ 13.3 WRITTEN NOTICE

Written notice shall be deemed to have been duly served if delivered in person to the individual, to a member of the firm or entity, or to an officer of the corporation for which it was intended; or if delivered at, or sent by registered or certified mail or by courier service providing proof of delivery to, the last business address known to the party giving notice.

§ 13.4 RIGHTS AND REMEDIES

§ 13.4.1 Duties and obligations imposed by the Contract Documents and rights and remedies available thereunder shall be in addition to and not a limitation of duties, obligations, rights and remedies otherwise imposed or available by law.

§ 13.4.2 No action or failure to act by the Owner, Architect or Contractor shall constitute a waiver of a right or duty afforded them under the Contract, nor shall such action or failure to act constitute approval of or acquiescence in a breach there under, except as may be specifically agreed in writing.

§ 13.5 TESTS AND INSPECTIONS

§ 13.5.1 Tests, inspections and approvals of portions of the Work shall be made as required by the Contract Documents and by applicable laws, statutes, ordinances, codes, rules and regulations or lawful orders of public authorities. Unless otherwise provided, the Contractor shall make arrangements for such tests, inspections and approvals with an independent testing laboratory or entity acceptable to the Owner, or with the appropriate public authority, and shall bear all related costs of tests, inspections and approvals. The Contractor shall give the Architect timely notice of when and where tests and inspections are to be made so that the Architect may be present for such procedures. The Owner shall bear costs of (1) tests, inspections or approvals that do not become requirements until after bids are received or negotiations concluded, and (2) tests, inspections or approvals where building codes or applicable laws or regulations prohibit the Owner from delegating their cost to the Contractor.

§ 13.5.2 If the Architect, Owner or public authorities having jurisdiction determine that portions of the Work require additional testing, inspection or approval not included under Section 13.5.1, the Architect will, upon written authorization from the Owner, instruct the Contractor to make arrangements for such additional testing, inspection or approval by an entity acceptable to the Owner, and the Contractor shall give timely notice to the Architect of when and where tests and inspections are to be made so that the Architect may be present for such procedures. Such costs, except as provided in Section 13.5.3, shall be at the Owner's expense.

§ 13.5.3 If such procedures for testing, inspection or approval under Sections 13.5.1 and 13.5.2 reveal failure of the portions of the Work to comply with requirements established by the Contract Documents, all costs made necessary by such failure including those of repeated procedures and compensation for the Architect's services and expenses shall be at the Contractor's expense.

§ 13.5.4 Required certificates of testing, inspection or approval shall, unless otherwise required by the Contract Documents, be secured by the Contractor and promptly delivered to the Architect.

Init.

§ 13.5.5 If the Architect is to observe tests, inspections or approvals required by the Contract Documents, the Architect will do so promptly and, where practicable, at the normal place of testing.

§ 13.5.6 Tests or inspections conducted pursuant to the Contract Documents shall be made promptly to avoid unreasonable delay in the Work.

§ 13.6 INTEREST

Payments due and unpaid under the Contract Documents shall bear interest from the date payment is due at such rate as the parties may agree upon in writing or, in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.

§ 13.7 TIME LIMITS ON CLAIMS

The Owner and Contractor shall commence all claims and causes of action, whether in contract, tort, breach of warranty or otherwise, against the other arising out of or related to the Contract in accordance with the requirements of the final dispute resolution method selected in the Agreement within the time period specified by applicable law, but in any case not more than 10 years after the date of Substantial Completion of the Work. The Owner and Contractor waive all claims and causes of action not commenced in accordance with this Section 13.7.

ARTICLE 14 TERMINATION OR SUSPENSION OF THE CONTRACT

§ 14.1 TERMINATION BY THE CONTRACTOR

§ 14.1.1 The Contractor may terminate the Contract if the Work is stopped for a period of 30 consecutive days through no act or fault of the Contractor or a Subcontractor, Sub-subcontractor or their agents or employees or any other persons or entities performing portions of the Work under direct or indirect contract with the Contractor, for any of the following reasons:

- .1 Issuance of an order of a court or other public authority having jurisdiction that requires all Work to be stopped;
- .2 An act of government, such as a declaration of national emergency that requires all Work to be stopped;
- .3 Because the Architect has not issued a Certificate for Payment and has not notified the Contractor of the reason for withholding certification as provided in Section 9.4.1, or because the Owner has not made payment on a Certificate for Payment within the time stated in the Contract Documents; or
- .4 The Owner has failed to furnish to the Contractor promptly, upon the Contractor's request, reasonable evidence as required by Section 2.2.1.

§ 14.1.2 The Contractor may terminate the Contract if, through no act or fault of the Contractor or a Subcontractor, Sub-subcontractor or their agents or employees or any other persons or entities performing portions of the Work under direct or indirect contract with the Contractor, repeated suspensions, delays or interruptions of the entire Work by the Owner as described in Section 14.3 constitute in the aggregate more than 100 percent of the total number of days scheduled for completion, or 120 days in any 365-day period, whichever is less.

§ 14.1.3 If one of the reasons described in Section 14.1.1 or 14.1.2 exists, the Contractor may, upon seven days' written notice to the Owner and Architect, terminate the Contract and recover from the Owner payment for Work executed, including reasonable overhead and profit, costs incurred by reason of such termination, and damages.

§ 14.1.4 If the Work is stopped for a period of 60 consecutive days through no act or fault of the Contractor or a Subcontractor or their agents or employees or any other persons performing portions of the Work under contract with the Contractor because the Owner has repeatedly failed to fulfill the Owner's obligations under the Contract Documents with respect to matters important to the progress of the Work, the Contractor may, upon seven additional days' written notice to the Owner and the Architect, terminate the Contract and recover from the Owner as provided in Section 14.1.3.

§ 14.2 TERMINATION BY THE OWNER FOR CAUSE

§ 14.2.1 The Owner may terminate the Contract if the Contractor

- .1 repeatedly refuses or fails to supply enough properly skilled workers or proper materials;
- .2 fails to make payment to Subcontractors for materials or labor in accordance with the respective agreements between the Contractor and the Subcontractors;
- .3 repeatedly disregards applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of a public authority; or
- .4 otherwise is guilty of substantial breach of a provision of the Contract Documents.

Init.

§ 14.2.2 When any of the above reasons exist, the Owner, upon certification by the Initial Decision Maker that sufficient cause exists to justify such action, may without prejudice to any other rights or remedies of the Owner and after giving the Contractor and the Contractor's surety, if any, seven days' written notice, terminate employment of the Contractor and may, subject to any prior rights of the surety:

- .1 Exclude the Contractor from the site and take possession of all materials, equipment, tools, and construction equipment and machinery thereon owned by the Contractor;
- .2 Accept assignment of subcontracts pursuant to Section 5.4; and
- .3 Finish the Work by whatever reasonable method the Owner may deem expedient. Upon written request of the Contractor, the Owner shall furnish to the Contractor a detailed accounting of the costs incurred by the Owner in finishing the Work.

§ 14.2.3 When the Owner terminates the Contract for one of the reasons stated in Section 14.2.1, the Contractor shall not be entitled to receive further payment until the Work is finished.

§ 14.2.4 If the unpaid balance of the Contract Sum exceeds costs of finishing the Work, including compensation for the Architect's services and expenses made necessary thereby, and other damages incurred by the Owner and not expressly waived, such excess shall be paid to the Contractor. If such costs and damages exceed the unpaid balance, the Contractor shall pay the difference to the Owner. The amount to be paid to the Contractor or Owner, as the case may be, shall be certified by the Initial Decision Maker, upon application, and this obligation for payment shall survive termination of the Contract.

§ 14.3 SUSPENSION BY THE OWNER FOR CONVENIENCE

§ 14.3.1 The Owner may, without cause, order the Contractor in writing to suspend, delay or interrupt the Work in whole or in part for such period of time as the Owner may determine.

§ 14.3.2 The Contract Sum and Contract Time shall be adjusted for increases in the cost and time caused by suspension, delay or interruption as described in Section 14.3.1. Adjustment of the Contract Sum shall include profit. No adjustment shall be made to the extent

- .1 that performance is, was or would have been so suspended, delayed or interrupted by another cause for which the Contractor is responsible; or
- .2 that an equitable adjustment is made or denied under another provision of the Contract.

§ 14.4 TERMINATION BY THE OWNER FOR CONVENIENCE

§ 14.4.1 The Owner may, at any time, terminate the Contract for the Owner's convenience and without cause.

§ 14.4.2 Upon receipt of written notice from the Owner of such termination for the Owner's convenience, the Contractor shall

- .1 cease operations as directed by the Owner in the notice;
- .2 take actions necessary, or that the Owner may direct, for the protection and preservation of the Work; and
- .3 except for Work directed to be performed prior to the effective date of termination stated in the notice, terminate all existing subcontracts and purchase orders and enter into no further subcontracts and purchase orders.

§ 14.4.3 In case of such termination for the Owner's convenience, the Contractor shall be entitled to receive payment for Work executed, and costs incurred by reason of such termination, along with reasonable overhead and profit on the Work not executed.

ARTICLE 15 CLAIMS AND DISPUTES

§ 15.1 CLAIMS

§ 15.1.1 DEFINITION

A Claim is a demand or assertion by one of the parties seeking, as a matter of right, payment of money, or other relief with respect to the terms of the Contract. The term "Claim" also includes other disputes and matters in question between the Owner and Contractor arising out of or relating to the Contract. The responsibility to substantiate Claims shall rest with the party making the Claim.

§ 15.1.2 NOTICE OF CLAIMS

Claims by either the Owner or Contractor must be initiated by written notice to the other party and to the Initial Decision Maker with a copy sent to the Architect, if the Architect is not serving as the Initial Decision Maker.

Init.

AIA Document A201™ – 2007. Copyright © 1888, 1911, 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1966, 1970, 1976, 1987, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. Purchasers are not permitted to reproduce this document. To report copyright violations of AIA Contract Documents, e-mail The American Institute of Architects' legal counsel, copyright@aia.org.

Claims by either party must be initiated within 21 days after occurrence of the event giving rise to such Claim or within 21 days after the claimant first recognizes the condition giving rise to the Claim, whichever is later.

§ 15.1.3 CONTINUING CONTRACT PERFORMANCE

Pending final resolution of a Claim, except as otherwise agreed in writing or as provided in Section 9.7 and Article 14, the Contractor shall proceed diligently with performance of the Contract and the Owner shall continue to make payments in accordance with the Contract Documents. The Architect will prepare Change Orders and issue Certificates for Payment in accordance with the decisions of the Initial Decision Maker.

§ 15.1.4 CLAIMS FOR ADDITIONAL COST

If the Contractor wishes to make a Claim for an increase in the Contract Sum, written notice as provided herein shall be given before proceeding to execute the Work. Prior notice is not required for Claims relating to an emergency endangering life or property arising under Section 10.4.

§ 15.1.5 CLAIMS FOR ADDITIONAL TIME

§ 15.1.5.1 If the Contractor wishes to make a Claim for an increase in the Contract Time, written notice as provided herein shall be given. The Contractor's Claim shall include an estimate of cost and of probable effect of delay on progress of the Work. In the case of a continuing delay, only one Claim is necessary.

§ 15.1.5.2 If adverse weather conditions are the basis for a Claim for additional time, such Claim shall be documented by data substantiating that weather conditions were abnormal for the period of time, could not have been reasonably anticipated and had an adverse effect on the scheduled construction.

§ 15.1.6 CLAIMS FOR CONSEQUENTIAL DAMAGES

The Contractor and Owner waive Claims against each other for consequential damages arising out of or relating to this Contract. This mutual waiver includes

- .1 damages incurred by the Owner for rental expenses, for losses of use, income, profit, financing, business and reputation, and for loss of management or employee productivity or of the services of such persons; and
- .2 damages incurred by the Contractor for principal office expenses including the compensation of personnel stationed there, for losses of financing, business and reputation, and for loss of profit except anticipated profit arising directly from the Work.

This mutual waiver is applicable, without limitation, to all consequential damages due to either party's termination in accordance with Article 14. Nothing contained in this Section 15.1.6 shall be deemed to preclude an award of liquidated damages, when applicable, in accordance with the requirements of the Contract Documents.

§ 15.2 INITIAL DECISION

§ 15.2.1 Claims, excluding those arising under Sections 10.3, 10.4, 11.3.9, and 11.3.10, shall be referred to the Initial Decision Maker for initial decision. The Architect will serve as the Initial Decision Maker, unless otherwise indicated in the Agreement. Except for those Claims excluded by this Section 15.2.1, an initial decision shall be required as a condition precedent to mediation of any Claim arising prior to the date final payment is due, unless 30 days have passed after the Claim has been referred to the Initial Decision Maker with no decision having been rendered. Unless the Initial Decision Maker and all affected parties agree, the Initial Decision Maker will not decide disputes between the Contractor and persons or entities other than the Owner.

§ 15.2.2 The Initial Decision Maker will review Claims and within ten days of the receipt of a Claim take one or more of the following actions: (1) request additional supporting data from the claimant or a response with supporting data from the other party, (2) reject the Claim in whole or in part, (3) approve the Claim, (4) suggest a compromise, or (5) advise the parties that the Initial Decision Maker is unable to resolve the Claim if the Initial Decision Maker lacks sufficient information to evaluate the merits of the Claim or if the Initial Decision Maker concludes that, in the Initial Decision Maker's sole discretion, it would be inappropriate for the Initial Decision Maker to resolve the Claim.

§ 15.2.3 In evaluating Claims, the Initial Decision Maker may, but shall not be obligated to, consult with or seek information from either party or from persons with special knowledge or expertise who may assist the Initial Decision Maker in rendering a decision. The Initial Decision Maker may request the Owner to authorize retention of such persons at the Owner's expense.

Init.

§ 15.2.4 If the Initial Decision Maker requests a party to provide a response to a Claim or to furnish additional supporting data, such party shall respond, within ten days after receipt of such request, and shall either (1) provide a response on the requested supporting data, (2) advise the Initial Decision Maker when the response or supporting data will be furnished or (3) advise the Initial Decision Maker that no supporting data will be furnished. Upon receipt of the response or supporting data, if any, the Initial Decision Maker will either reject or approve the Claim in whole or in part.

§ 15.2.5 The Initial Decision Maker will render an initial decision approving or rejecting the Claim, or indicating that the Initial Decision Maker is unable to resolve the Claim. This initial decision shall (1) be in writing; (2) state the reasons therefor; and (3) notify the parties and the Architect, if the Architect is not serving as the Initial Decision Maker, of any change in the Contract Sum or Contract Time or both. The initial decision shall be final and binding on the parties but subject to mediation and, if the parties fail to resolve their dispute through mediation, to binding dispute resolution.

§ 15.2.6 Either party may file for mediation of an initial decision at any time, subject to the terms of Section 15.2.6.1.

§ 15.2.6.1 Either party may, within 30 days from the date of an initial decision, demand in writing that the other party file for mediation within 60 days of the initial decision. If such a demand is made and the party receiving the demand fails to file for mediation within the time required, then both parties waive their rights to mediate or pursue binding dispute resolution proceedings with respect to the initial decision.

§ 15.2.7 In the event of a Claim against the Contractor, the Owner may, but is not obligated to, notify the surety, if any, of the nature and amount of the Claim. If the Claim relates to a possibility of a Contractor's default, the Owner may, but is not obligated to, notify the surety and request the surety's assistance in resolving the controversy.

§ 15.2.8 If a Claim relates to or is the subject of a mechanic's lien, the party asserting such Claim may proceed in accordance with applicable law to comply with the lien notice or filing deadlines.

§ 15.3 MEDIATION

§ 15.3.1 Claims, disputes, or other matters in controversy arising out of or related to the Contract except those waived as provided for in Sections 9.10.4, 9.10.5, and 15.1.6 shall be subject to mediation as a condition precedent to binding dispute resolution.

§ 15.3.2 The parties shall endeavor to resolve their Claims by mediation which, unless the parties mutually agree otherwise, shall be administered by the American Arbitration Association in accordance with its Construction Industry Mediation Procedures in effect on the date of the Agreement. A request for mediation shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the mediation. The request may be made concurrently with the filing of binding dispute resolution proceedings but, in such event, mediation shall proceed in advance of binding dispute resolution proceedings, which shall be stayed pending mediation for a period of 60 days from the date of filing, unless stayed for a longer period by agreement of the parties or court order. If an arbitration is stayed pursuant to this Section 15.3.2, the parties may nonetheless proceed to the selection of the arbitrator(s) and agree upon a schedule for later proceedings.

§ 15.3.3 The parties shall share the mediator's fee and any filing fees equally. The mediation shall be held in the place where the Project is located, unless another location is mutually agreed upon. Agreements reached in mediation shall be enforceable as settlement agreements in any court having jurisdiction thereof.

§ 15.4 ARBITRATION

§ 15.4.1 If the parties have selected arbitration as the method for binding dispute resolution in the Agreement, any Claim subject to, but not resolved by, mediation shall be subject to arbitration which, unless the parties mutually agree otherwise, shall be administered by the American Arbitration Association in accordance with its Construction Industry Arbitration Rules in effect on the date of the Agreement. A demand for arbitration shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the arbitration. The party filing a notice of demand for arbitration must assert in the demand all Claims then known to that party on which arbitration is permitted to be demanded.

Init.

§ 15.4.1.1 A demand for arbitration shall be made no earlier than concurrently with the filing of a request for mediation, but in no event shall it be made after the date when the institution of legal or equitable proceedings based on the Claim would be barred by the applicable statute of limitations. For statute of limitations purposes, receipt of a written demand for arbitration by the person or entity administering the arbitration shall constitute the institution of legal or equitable proceedings based on the Claim.

§ 15.4.2 The award rendered by the arbitrator or arbitrators shall be final, and judgment may be entered upon it in accordance with applicable law in any court having jurisdiction thereof.

§ 15.4.3 The foregoing agreement to arbitrate and other agreements to arbitrate with an additional person or entity duly consented to by parties to the Agreement shall be specifically enforceable under applicable law in any court having jurisdiction thereof.

§ 15.4.4 CONSOLIDATION OR JOINDER

§ 15.4.4.1 Either party, at its sole discretion, may consolidate an arbitration conducted under this Agreement with any other arbitration to which it is a party provided that (1) the arbitration agreement governing the other arbitration permits consolidation, (2) the arbitrations to be consolidated substantially involve common questions of law or fact, and (3) the arbitrations employ materially similar procedural rules and methods for selecting arbitrator(s).

§ 15.4.4.2 Either party, at its sole discretion, may include by joinder persons or entities substantially involved in a common question of law or fact whose presence is required if complete relief is to be accorded in arbitration, provided that the party sought to be joined consents in writing to such joinder. Consent to arbitration involving an additional person or entity shall not constitute consent to arbitration of any claim, dispute or other matter in question not described in the written consent.

§ 15.4.4.3 The Owner and Contractor grant to any person or entity made a party to an arbitration conducted under this Section 15.4, whether by joinder or consolidation, the same rights of joinder and consolidation as the Owner and Contractor under this Agreement.

Sample

SUPPLEMENTARY CONDITIONS

Amending the General Conditions of the Contract for Construction
AIA Document A201 (2007 edition)

I. SUPPLEMENTARY CONDITIONS

The following addendum supplements, modifies, deletes and/or adds to the General Conditions. Where any Article, Paragraph or subparagraph in the General Conditions is supplemented by one of the following paragraphs, the provisions of such Article, Paragraph, or Subparagraph shall remain in effect and the supplemental provisions shall be considered as added thereto. Where any Article, Paragraph, or subparagraph in the General Conditions is amended, voided or superseded by any of the following paragraphs, the provisions of such Article, Paragraph or subparagraph not so amended, voided, or superseded shall remain in effect.

II. MODIFICATIONS TO VARIOUS ARTICLES OF THE AIA CONDITIONS

ARTICLE 1 GENERAL PROVISIONS

- 1.1.1 In the first sentence, delete “are enumerated in the Agreement between the Owner and Contractor (hereinafter the Agreement) and” after “The Contract Documents”.

Insert “between the Owner and Contractor (hereinafter the Agreement)” after “consist of the Agreement”.

In the last sentence:

Delete “Unless specifically enumerated in the Agreement”.

Delete “not” after “Contract Documents do”.

Delete “other” after “sample forms,”.

Delete “or” after “or proposal,” and insert “and”.

Delete “bidding requirements” after “relating to” and insert “those documents.”

- 1.1.8 Delete “Claims” and insert “claims”.

Delete “and certify termination of the Agreement under Section 14.2.2.”.

1.2.1 Add to the end of the sub-section:

All Work mentioned or indicated in the Contract Documents shall be performed by the Contractor as part of this Contract unless it is specifically indicated in the Contract Documents that such Work is to be done by others. Should the Drawings or the Specifications disagree in themselves or with each other, the Contractor shall provide the better quality or greater quantity of Work unless otherwise directed by written addendum to the Contract.

1.2.2 Add to the end of the sentence:

, except that the performance of filed sub-trade work shall comply with the provisions of chapter 149 of the General Laws of the Commonwealth of Massachusetts. The Contractor and all Subcontractors shall refer to all of the Drawings, including those showing primarily the Work of the mechanical, electrical and other specialized trades, and to all of the Sections of the Specifications, and shall perform all Work reasonably inferable therefrom as being necessary to produce the indicated results.

1.2.4 Add the following new sub-sections 1.2.4 to 1.2.11 as follows:

-1.2.11

§ 1.2.4 All indications or notations which apply to one of a number of similar situations, materials or processes shall be deemed to apply to all such situations, materials or processes wherever they appear in the Work, except where a contrary result is clearly indicated by the Contract Documents.

§ 1.2.5 Where codes, standards, requirements and publications of public and private bodies are referred to in the Specifications, references shall be understood to be to the latest revision prior to the date of receiving bids, except where otherwise indicated.

§ 1.2.6 Where no explicit quality or standards for materials or workmanship are established for Work, such Work is to be of good quality for the intended use and consistent with the quality of the surrounding Work and of the construction of the Project generally.

§ 1.2.7 All manufactured articles, materials, and equipment shall be applied, installed, connected, erected, used, cleaned, and conditioned in accordance with the manufacturer's written or printed directions and instructions unless otherwise indicated in the Contract Documents.

§ 1.2.8 The Mechanical, Electrical and Fire Protection Drawings are diagrammatic only, and are not intended to show the alignment, physical locations or configurations of such Work. Such Work shall be installed without additional cost to the Owner to clear all obstructions, permit proper clearances for the Work of other trades, and present an orderly appearance where exposed. Prior to

beginning such Work, the Contractor shall prepare coordination drawings showing the exact alignment, physical location and configuration of the Mechanical, Electrical and Fire Protection installations and demonstrating to the Contractor's satisfaction that the installations will comply with the preceding sentence. A copy of the drawings shall be submitted to the Architect, and the Contractor shall revise and resubmit the drawings if so directed by the Architect.

§ 1.2.9 Exact locations of fixtures and outlets shall be obtained from the Architect as provided in subparagraph 3.2.5 before the Work is roughed in; Work installed without such information from the Architect shall be relocated at the Contractor's expense.

§ 1.2.10 Test boring or soil test information included with the Contract Documents or otherwise made available to the Contractor was obtained by the Owner for use by the Architects in the design of the Project or Work. The Owner does not hold out such information to the Contractor as a completely accurate indication of subsurface conditions, and no claim for extra cost or extension of time resulting from a reliance by the Contractor on such information shall be allowed except as provided in subparagraph 3.7.4.

§ 1.2.11 Where the Work is to fit with existing conditions or work to be performed by others, the Contractor shall fully and completely join the Work with such conditions or work, unless otherwise specified. Owner provided drawings showing existing conditions or construction are based on available documents and are not guaranteed to show actual existing conditions.

1.5.1 Delete 1.5.1 and replace as follows:

§ 1.5.1 All Drawings, Specifications and copies thereof furnished by the Owner are and shall remain the Owner's property. They are to be used only with respect to this Project and are not to be used on any other project without the prior written consent of the Owner. With the exception of one contract set for each party to the Contract, such documents are to be returned or suitably accounted for to the Owner at the completion of the Work. Submission or distribution to meet official regulatory requirements or for other purposes in connection with the Project is not to be construed as publication in derogation of any reserved rights.

ARTICLE 2 OWNER

2.1.2 Delete sub-section 2.1.2.

2.2.1 Delete the last three sentences.

2.2.3 In the first sentence insert “available” after “shall furnish”.

Delete the last sentence and replace as follows:

The Owner makes no warranty as to the accuracy or completeness of such information, and the Contractor shall exercise proper precautions relating to the safe performance of the Work.

2.2.4 Delete the last sentence.

2.2.5 Add to the end of the sub-section as follows:

All additional copies will be furnished upon request at the cost of reproduction.

2.3 Delete from the last sentence “, except to the extent required by Section 6.1.3” and add as follows:

The Contractor shall resume the Work after such stoppage promptly upon written notice to do so from the Owner. The Contractor shall remain responsible for maintaining the progress of the Work and shall not be entitled to any increase in the Contract Sum or Contract Time. The Contractor shall be responsible for all costs incurred by the Owner attributable to such an order to stop the Work.

2.4 In the second sentence:

Delete “Change Order” and replace with “Construction Change Directive”.

Insert “and Owner’s Project Manager’s” after “for the Architect’s”.

Delete the third sentence.

Add to the end of the section as follows:

The rights of the Owner hereunder are in addition to any other rights set forth in the Contract Documents or available at law or in equity.

ARTICLE 3 CONTRACTOR

3.2.1 Delete “generally” after “the site, become”.

Add to the end of the sub-section as follows:

The Contractor shall not be entitled to any change in the Contract Time or Contract Sum on account of its failure, or that of any Subcontractor, to comply with the foregoing requirements.

3.2.2 Delete the beginning of the second sentence as follows:

These obligations are for the purpose of facilitating coordination and construction by the Contractor and are not for the purpose of discovering errors, omissions, or inconsistencies in the Contract Documents; however,

Delete the last sentence and replace as follows:

If the Contractor performs any construction activity that it knows or should know involves a recognized error, inconsistency or omission in the Contract Documents without such notice to the Architect, the Contractor shall assume appropriate responsibility for such performance and shall bear responsibility for the costs of any required correction.

3.2.3 Delete “not” after “Contractor is”.

Delete “, but” after “public authorities” and create new sentence beginning with “The Contractor shall promptly”.

3.2.4 Delete “claims” after “the Contractor shall make” and insert “a claim”.

Delete the last sentence.

3.2.5 Add new sub-section 3.2.5 as follows:

§ 3.2.5 Any claim by the Contractor or Subcontractors that, in submitting their respective bids, they did not include all items as shown in the Contract Documents will be given no consideration for an adjustment of any kind. If any item is specified in a Section which would not normally furnish this item it shall be the responsibility of the Contractor to coordinate the situation with the Subcontractor, and if the item under consideration is not to be provided by the Subcontractor it shall be the responsibility of the Contractor to provide the work in question, without any additional cost to the Owner.

3.3.1 Add to the end of the first sentence as follows:

which shall not be less than such state of skill and attention generally rendered by the contracting profession for projects similar to the Project in scope, difficulty and location. The Contractor shall adequately staff the Project to properly and thoroughly manage, schedule and supervise all construction activities.

Delete the last sentence.

3.3.2 Add the last sentence as follows:

This obligation shall also extend to the presence on the Site of suppliers of materials or equipment, their employees, contractors, and agents engaged in the Work.

3.4.3 Add to the end of the second sentence as follows:

, and the Contractor shall ensure that all workers to be employed on the Project have successfully completed a course in construction safety and health approved by the United States Occupational Safety and Health Administration (OSHA) of at least 10 hours. The Contractor shall be responsible for maintaining all safety precautions at and around the Project site. On the Owner's request, the Contractor shall permanently remove from the Project site any employee of the Contractor or any Subcontractor who fails to comply with the requirements of the Contract Documents or whose presence or behavior is deemed by the Owner to be adverse to the success of the Project or the Owner's interests.

3.5 Add to the end of the first sentence as follows:

and, promptly after written notification of non-conformance, shall be repaired or replaced by the Contractor with Work conforming to such requirements.

Delete the second to last sentence.

3.5.2 Add new sub-sections 3.5.2 to 3.5.8 as follows:

-3.5.8

§ 3.5.2 The Contractor shall be responsible for determining that all materials furnished for the Work meet all requirements of the Contract Documents. The Architect may require the Contractor to produce reasonable evidence that a material meets such requirements, such as certified reports of past tests by qualified testing laboratories, reports of studies by qualified experts, or other evidence which, in the opinion of the Architect, would lead to a reasonable certainty that any material used, or proposed to be used, in the Work meets the requirements of the Contract Documents. All such data shall be furnished at the Contractor's expense. This provision shall not require the Contractor to pay for periodic testing of different batches of the same material, unless such testing is specifically required by the Contract Documents to be performed at the Contractor's expense.

§ 3.5.3 If the Contractor proposes to use a material which, while suitable for the intended use, deviates in any way from the detailed requirements of the Contract Documents, the Contractor shall inform the Architect in writing of the nature of such deviations at the time the material is submitted for approval and request approval of the deviation.

The Architect shall judge the design and appearance of proposed substitutes, and may refuse to approve any substitute which, in the Architect's opinion, would be out of character or otherwise inconsistent with the character or quality of design of the Project.

§ 3.5.4 In informing the Architect of deviations or substitutions, the Contractor shall provide, upon request, evidence leading to a reasonable certainty that the proposed substitution or deviation will provide a quality of result at least equal to that otherwise attainable in accordance with the Contract Documents. If, in the opinion of the Architect, the evidence presented by the Contractor does not provide a sufficient basis for such reasonable certainty, the Architect may reject such substitution or deviation without further investigation.

§ 3.5.5 Any additional cost, or any loss or damage arising from the substitution of any material or any method for those originally specified shall be borne by the Contractor, notwithstanding approval or acceptance of such substitution by the Owner or the Architect, unless such substitution was made at the written request or direction of the Owner or the Architect.

§ 3.5.6 The warranty provided in this paragraph 3.5 shall be in addition to and not in limitation of any other warranty required by the Contract Documents or otherwise prescribed by law.

§ 3.5.7 The Contractor shall procure and deliver to the Architect, no later than the date claimed by the Contractor as the date of Substantial Completion, all special warranties required by the Contract Documents. Delivery by the Contractor shall constitute the Contractor's guarantee to the Owner that the warranty will be performed in accordance with its terms and conditions.

§ 3.5.8 The Contractor shall guarantee all Work for a period of one year after Date of Substantial Completion, or by the terms of any special guarantee required by the Contract Documents. The Contractor shall, upon written notice from the Owner, promptly correct defective Work or Work not in accordance with the Contract Documents.

3.6.1 Add new sub-section 3.6.1 as follows:

§ 3.6.1 The project is exempt from the Massachusetts Sales Tax to the extent permitted by G.L. c.64H, §6(f). The exemption number will be provided by the Awarding Authority to the Contractor.

3.7.2 Add to the end of the sub-section as follows:

If any of the Work is required to be inspected or approved by any public authority, the Contractor shall cause such inspection or approval to be performed

and shall comply with any instructions or corrections ordered by the public authority.

3.7.3 Delete “knowing it” after “performs Work” and replace with “it knows or should know”.

3.7.4 Delete sub-section 3.7.4 and replace as follows:

§ 3.7.4 Concealed or Unknown Conditions. Claims for concealed or unknown conditions shall be governed by Chapter 30, Section 39N of the General Laws of the Commonwealth of Massachusetts, as amended.

3.7.5 Delete second and last sentences.

3.8 Delete section 3.8 in its entirety.

3.9.1 In the first sentence:

Insert “, in accordance with the Contract Documents,” after “shall employ”.

Insert “at all times” after “the Project site”.

3.9.4 Add new sub-sections 3.9.4 and 3.9.5 as follows:

-3.9.5

§ 3.9.4 The Contractor shall coordinate and supervise the Work performed by Subcontractors to the end that the Work is carried out without conflict between trades and so that no trade, at any time, causes delay to the general progress of the Work. The Contractor and all Subcontractors shall at all times afford each trade, any separate contractor, or the Owner, every reasonable opportunity for the installation of Work and the storage of materials.

§ 3.9.5 The Contractor shall arrange for and attend job meetings with the Architect and such other persons as the Architect may from time to time wish to have present. The Contractor shall be represented by a principal, project manager, general superintendent or other authorized main office representative, as well as by the Contractor's own superintendent. An authorized representative of any Subcontractor or Sub-subcontractor shall attend such meetings if the representative's presence is requested by the Architect. Such representatives shall be empowered to make binding commitments on all matters to be discussed at such meetings, including costs, payments, change orders, time schedules and manpower. Any notices required under the Contract may be served on such representatives.

3.10.1 In the first sentence delete “promptly” after “The Contractor” and replace with “within twenty (20) days”.

In the second sentence, insert “or as requested by the Architect” after “conditions of the Work and Project”.

Add to the end of the sub-section as follows:

The construction schedule shall be in such form and contain such information as the Architect and Owner require. The construction schedule shall be resource loaded for the Contractor and all subcontractors, with each resource identified by name, description, unit of measure, and calendar assignment. For each class of work included in the Contractor’s schedule of values, the construction schedule shall show the percentage of completion to be obtained and the total dollar value of the work to be completed as of the first of each month until Substantial Completion. All calculations shall be on the basis of work in place, but not including the value of materials delivered but not in place.

3.10.3 Add to the end of the sub-section as follows:

The Contractor’s compliance with the construction schedule is a material obligation of the Contract.

3.10.4 Add new sub-sections 3.10.4, 3.10.5, and 3.10.6 as follows:

-3.10.6

§ 3.10.4 The Contractor shall monitor the progress of the Work for conformance with the requirements of the construction schedule and shall promptly advise the Owner of any delays or potential delays. The construction schedule shall be updated every month (or more frequently if requested by the Owner) to reflect actual conditions (such updates are sometimes referred to in these General Conditions as "progress reports"). In the event any progress report indicates delays in achievement of any milestone date set forth in such schedule, the Contractor shall propose in written form an affirmative plan (the "Recovery Schedule") to correct the delay, including overtime and/or additional labor, if necessary, which Recovery Schedule shall indicate the date by which the progress of the Work will comply with the construction schedule, and shall be subject to the approval of the Owner and the Architect. In no event shall any progress report or Recovery Schedule constitute an adjustment in the construction schedule, Contract Time or any milestone date unless any such adjustment is agreed to by the Owner and authorized pursuant to a Change Order.

§ 3.10.5 In the event (i) that the performance of the Work, as of a milestone date, has not progressed or reached the level of completion required by the construction schedule, and (ii) the progress of the Work is not brought back into compliance with the construction schedule on the date proposed by the Recovery Schedule, or the Contractor otherwise fails to comply with the Recovery Schedule, the Owner shall have the right to order the Contractor to take corrective measures to expedite the progress of the Work, including, without limitation, (1) supplying additional manpower, equipment, and facilities, (2) working additional shifts or overtime,

(3) working additional days, and (4) other similar measures (hereinafter referred to collectively as "Corrective Measures"). Such Corrective Measures shall continue until the progress of the Work complies with the stage of completion required by the Contract Documents.

§ 3.10.6 The Contractor shall not be entitled to an adjustment in the Contract Sum in connection with Corrective Measures required by the Owner under or pursuant to Section 3.10.5. The Owner may exercise the rights furnished the Owner under or pursuant to Section 3.10.5 as frequently as reasonably necessary to ensure that the Contractor's performance of the Work complies with the milestone dates set forth in the construction schedule.

3.12.6 Add to the end of the sub-section as follows:

By approving and submitting Shop Drawings, Product Data, Samples, and similar submittals the Contractor thereby represents that the Contractor has determined and verified all dimensions, quantities, field dimensions, relations to existing work, coordination with work to be installed later, coordination with information on previously accepted Shop Drawings, Product Data, Samples, or similar submittals and verification of compliance with all the requirements of the Contract Documents. The accuracy of all such information is the responsibility of the Contractor. In reviewing Shop Drawings, Product Data, Samples, and similar submittals the Architect shall be entitled to rely upon the Contractor's representation that such information is correct and accurate.

3.12.10 Add to the end of the last sentence as follows:

, except as provided in Section 3.2.

3.12.11 Add new subsection 3.12.11 as follows:

§ 3.12.11 When professional certification of materials, systems or equipment is required by the Contract Documents, the Owner shall be entitled to rely upon such certifications, and neither the Owner nor the Architect shall be expected to make an independent examination with respect to the performance of such materials, systems or equipment.

3.13 Add to the end of the section as follows:

The right of possession of the premises and the improvements made thereon by the Contractor shall remain at all times with the Owner. The Contractor's right to entry and use thereof arises solely from the permission granted by the Owner under the Contract Documents. The Owner shall not be liable to the Contractor, the Subcontractors, their employees, or anyone else with respect to the conditions of the premises, except only for a condition caused directly and solely by the negligence of the Owner.

3.15.1 Add “site” to the end of the second sentence.

3.15.2 Add to the end of the sentence as follows:

, and may deduct all costs thereof from any payment due the Contractor.

3.16 Insert “, Owner’s representatives” after “provide the Owner”.

3.18.1 Delete the first sentence and replace as follows:

To the fullest extent permitted by law the Contractor shall indemnify and hold harmless the Owner, Architect, Architect’s consultants, and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys’ fees, arising out of or resulting from performance of the Work, including claims, damage, loss or expense attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property, including the Work, caused in whole or in part by the negligent or wrongful acts or omissions of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, regardless of whether or not such claim, damage, loss or expense is caused in part by a party indemnified hereunder. Such obligation shall not be construed to negate, abridge, or reduce other rights or obligations, including those of indemnity, which would otherwise exist as to a party or person described in this section.

ARTICLE 4 ARCHITECT

4.1.2 In the first sentence delete “, Contractor” after “consent of the Owner”.

In the second sentence insert “of the Owner” after “Consent”.

4.1.3 Delete sub-section 4.1.3.

4.2.3 In the first sentence delete “reasonably” after “will keep the Owner”.

4.2.10 Delete sub-section 4.2.10.

4.2.11 Add to the end of the sub-section as follows:

The parties agree that the Architect’s duties under this subparagraph shall be governed by Chapter 30, Section 39P of the General Laws of the Commonwealth of Massachusetts, as amended.

4.2.12 Delete the second sentence.

ARTICLE 5 SUBCONTRACTORS

5.2.1 Delete the last sentence.

5.2.2 In the second sentence insert “and legally permissible” after “has made reasonable”.

5.2.3 Delete the last two sentences and replace as follows:

No increase in the Contract Sum or Contract Time shall be allowed for such change.

5.2.4 Add to the end of the sub-section as follows:

The applicable provisions of Chapter 149, Section 44F of the General Laws of the Commonwealth of Massachusetts shall apply to filed sub-bid subcontractors.

5.4.1 In sub-heading .1 delete “Section 14.2” and replace with “Article 14”.

Add new sub-heading .3 as follows:

.3 The Owner may further assign the subcontract to a successor contractor or other entity.

Delete last sentence of sub-section.

5.4.2 Delete sub-sections 5.4.2 and 5.4.3.

-5.4.3

ARTICLE 6 CONSTRUCTION BY OWNER OR SEPARATE CONTRACTORS

6.1.1 At the end of the first sentence delete “including those portions related to insurance and waiver of subrogation”.

In the second sentence delete “Claim” after “shall make such” and replace with “claim”.

6.1.4 Delete sub-section 6.1.4 and replace as follows:

§ 6.1.4 The Owner reserves the right to enter any part of the Project site at any time to inspect the Work or to perform other work with its own forces or separate contractors, or to address any emergency situation. Such access is not to be construed to mean partial occupancy by the Owner and no claim for increase in the Contract Time or Sum will be considered unless such Owner’s contractors have delayed or damaged the Contractor’s Work. The Contractor shall permit the Owner to place and install as much furniture, equipment and other material during the progress of the Work as is possible before completion of the various parts of

the Work and agrees that such placing and installation of equipment shall not in any way evidence the completion or acceptance of the Work or any portion of it.

6.2.3 Delete the last sentence.

6.2.5 Delete sub-section 6.2.5.

ARTICLE 7 CHANGES IN THE WORK

7.2.3 Add new sub-section 7.2.3 as follows:

§ 7.2.3 Upon request of the Owner or the Architect, the Contractor shall without cost to the Owner submit to the Architect, in such form as the Architect may require, an accurate written estimate of the cost of any proposed extra Work or change. The estimate shall indicate the quantity and unit cost of each item of material, and the number of hours of work and hourly rate for each class of labor, as well as a description and the amounts of all other costs chargeable under the terms of this Article. Unit labor costs for the installation of each item of material shall be shown if required by the Architect. The Contractor shall promptly revise and resubmit each estimate if the Architect determines that it is not in compliance with the requirements of this Article, or that it contains errors of fact or mathematical errors. If required by the Architect, in order to establish the exact cost of new Work added or of previously required Work omitted, the Contractor shall obtain and furnish to the Architect bona fide proposals from recognized suppliers for furnishing any material included in such Work. Such estimates shall be furnished promptly so as to occasion no delay in the Work, and shall be furnished at the Contractor's expense. The Contractor shall state in the estimate any extension of time required for the completion of the Work if the change or extra work is ordered.

7.3.3 Delete the first sentence of the sub-section and replace as follows:

If the Construction Change Directive provides for an adjustment to the Contract Sum, and if the Contract Documents include a unit price for the work that is the subject of such directive, such unit price shall be the basis of the adjustment to the Contract Sum, unless the Owner, in its sole discretion, chooses another method. If, however, the Contract Documents do not include a unit price for such work, the adjustment shall be based on one of the following methods, as selected by the Owner:

In sub-heading .2 delete “stated in the Contract Documents or” after “Unit prices”.

7.3.4 Delete sub-section 7.3.4 and replace as follows:

§ 7.3.4 If unit prices are stated in the Contract Documents or subsequently agreed upon, and if quantities originally contemplated are materially changed in a

proposed Change Order or Construction Change Directive so that, in the opinion of the Architect, application of such unit prices to quantities of Work proposed will cause substantial inequity to the Owner, the applicable unit prices shall be equitably adjusted.

7.3.5 In the first sentence add after “the Work involved and” as follows:

, within five (5) calendar days from receipt of the Construction Change Directive,”

Insert “by written notice” after “advise the Architect”.

Add to the end of the sub-section as follows:

Failure to so advise the Architect within such 5-day period (1) shall be interpreted as Contractor’s agreement with the proposed method of adjustment; (2) shall constitute an irrevocable waiver of any right of the Contractor to submit a claim on account of the method of adjustment; and (3) shall cause the Construction Change Directive to be deemed and constitute a Change Order.

7.3.6 In the second sentence delete “recorded as” after “immediately shall be” and replace with “deemed and shall constitute”.

7.3.7 Delete first sentence and replace as follows:

If the proposed method of adjustment in the Contract Sum is based on unit prices that are stated in the Contract Documents, such unit prices shall be the basis of any adjustment to the Contract Sum, unless the Owner has chosen another method pursuant to subparagraph 7.3.3. If the proposed method of adjustment is not based on such unit prices and the Contractor objects to the proposed method of adjustment, the Contractor must notify the Architect of such objection in writing within five (5) calendar days from Contractor’s receipt of the Construction Change Directive. Failure to so object will irrevocably waive any such objections and claims on account of such method of adjustment, and the Construction Change Directive shall be deemed and shall constitute a Change Order. If the Contractor does so object, the adjustment to the Contract Sum shall be determined by the Architect on the basis of reasonable expenditures and savings of those performing the Work attributable to the change, including, in case of an increase in the Contract Sum, a reasonable allowance for overhead and profit.

In sub-heading .4 insert “and” after “and insurance,” and delete “, and sales, use or similar taxes related to the Work” after “permit fees”.

Delete sub-heading .5 and replaces as follows:

.5 A reasonable allowance for overhead and profit.

7.3.9 Delete the end of the first sentence starting after “Directive to the Owner,” and replace as follows:

amounts for such changes in the Work shall not be included in Applications for Payment. Such amounts shall only be included in an Application for Payment after the adjustment for the Construction Change Directive has been included in a Change Order signed by the Owner and the Contractor.

ARTICLE 8 TIME

8.2.2 In the first sentence delete “, except by agreement or instruction of the Owner in writing, prematurely”.

8.2.4 Add new sub-sections 8.2.4 and 8.2.5 as follows:

-8.2.5

§ 8.2.4 Unless specifically required by law, no payment under this Contract shall be due until the construction schedule, required by Section 3.10, and conforming to the requirements of the General Requirements has been accepted by the Architect.

§ 8.2.5 If the Architect in reviewing any Application for Payment determines that the amount of completed Work in place as certified by the Architect is less than 90% of the Work in place required by the Contractor’s construction schedule or schedule of values provided for in Section 9.2, or that there have been delays to critical paths and the Contract completion date will not be met, or that, in the Owner’s sole discretion, there is reasonable concern that the Work will not be Substantially Complete by the date required in the Contract Documents, the Contractor shall be required to submit a recovery schedule with a written description of the steps the Contractor intends to take to put the Project back on schedule. At the Owner’s option, the Contractor shall take some or all of the following actions at no additional cost to the Owner:

- .1 Increase the number of workers on the site, in such quantities and trades as will substantially eliminate the backlog of work;
- .2 Increase the number of working hours per shift, shifts per day, working days per week, amount of construction equipment, or any combination of the foregoing, sufficiently to substantially eliminate backlog of work; or
- .3 Reschedule activities so that the completion dates initially scheduled will be met.

8.3.1 Insert “(except weather)” after “casualties or other causes”.

Delete “pending mediation and arbitration” after “delay authorized by Owner”.

Add to the end of the sub-section as follows:

, and this shall be the Contractor's sole remedy for such delay. Under no circumstances will the Contractor be entitled to an increase in the Contract Sum, or to any other damages, on account of or in connection with any delay, regardless of the cause of such delay, and Contractor agrees not to make any claim for such damages, including, but not limited, claims for damages on account of having to perform out-of-sequence work, claims for damages on account of loss of production, and claims for damages on account of hindrances or interference with the work.

8.3.3 Delete sub-section 8.3.3.

8.3.4 Add new sections 8.3.4 and 8.3.5 as follows:

-8.3.5

§ 8.3.4 No extension of time shall be granted because of seasonal or abnormal variations in temperature, humidity or precipitation, which conditions shall be wholly at the risk of the Contractor, whether occurring within the time originally scheduled for completion or within the period of any extension granted. There shall be no increase in the Contract Sum on account of any additional costs of operations or conditions resulting therefrom.

§ 8.3.5 The Contractor hereby agrees that the Contractor shall have no claim for damages of any kind against the Owner or the Architect on account of any delay in the commencement of the Work and/or any hindrance, delay or suspension of any portion of the Work, whether such delay is caused by the Owner, the Architect, or otherwise, except as and to the extent expressly provided in G.L. c. 30, §39N. The Contractor acknowledges that the Contractor's sole remedy for any such delay and/or suspension will be an extension of time as provided in this Article.

8.4 Add new section 8.4 as follows:

§ 8.4 LIQUIDATED DAMAGES

§ 8.4.1 It is expressly understood and agreed, by and between the Contractor and Owner, that the time for the completion of the Work described herein is a reasonable time for the completion of same, taking into consideration the average climatic range and usual industrial and/or residential conditions prevailing in this locality. If the said Contractor shall neglect, fail or refuse to complete the Work within the times herein specified, or any proper extension thereof granted by the Owner, then the Contractor does hereby agree, as a part consideration for the awarding of this Contract, to pay to the Owner \$1,000.00, not as a penalty but as liquidated damages for such breach of contract, for each and every calendar day that the Contractor shall be in default after the time stipulated for completing the Work. The said amount is fixed and agreed upon by and between the Contractor and the Owner because of the impracticability and difficulty of fixing and ascertaining the actual damages the Owner would in such event sustain, and said

amount is agreed to be the amount of damages which the Owner would sustain and said amount shall be deducted by the Owner from periodic payments.

ARTICLE 9 SCHEDULE OF VALUES

9.2 Add to the end of the section as follows:

, and shall be revised if later found by the Architect to be inaccurate. In addition, the Contractor shall submit to the Architect, at least 14 days before the first Application for Payment, a Cash Flow Schedule that shows the percentage completion to be obtained and the total dollar value of Work to be completed as of the first of each month until Substantial Completion. All calculations in the Cash Flow Schedule shall be on the basis of Work in place and shall exclude the value of materials delivered but not in place.

9.2.1 Add new sub-section 9.2.1 as follows:

§ 9.2.1 The Cash Flow Schedule shall be based on an orderly progression of the Work allowing adequate time for each operation (including adequate time for submission and review of submittals) and leading to a reasonable certainty of Substantial Completion by the date established in the Agreement. The Cash Flow Schedule will be reviewed by the Architect for compliance with the requirements of the Contract Documents. Unless specifically required by law, no payment under this Contract shall be due until the Cash Flow Schedule has been reviewed and approved by the Architect. The Architect's review of the Cash Flow Schedule shall not impose any duty on the Architect or the Owner with respect to the timing, planning, scheduling or execution of the Work. In particular if the Contractor proposes a Cash Flow Schedule indicating a date of Substantial Completion which is earlier than the Contract Time the Contractor shall not be entitled to additional payment or compensation of any kind if for any reason the full Contract Time is required to achieve Substantial Completion of the Work.

9.3.1.1 Delete sub-section 9.3.1.1.

9.3.2 Add to the end of the sub-section as follows:

The Owner may deduct the amount of such costs from payments due the Contractor.

9.4.1 Insert at the beginning of the first sentence as follows:

Subject to the Contractor's compliance with Section 9.3 and the provisions of Section 9.6,

9.5.1 Add new sub-headings .8, .9, .10, .11, and .12 as follows:

.8 failure of the Contractor or mechanical or electrical trade subcontractors to comply with requirements of the General Requirements for maintaining record drawings. The Contractor shall check record drawings each month. Written confirmation that the record drawings are current will be required by the Architect before approval of the Contractor's monthly payment requisition;

.9 failure of the Contractor to provide required warranties under Section 9.3, claims for direct payment, or reasonable evidence indicating probable filing of such claims;

.10 costs incurred by the Owner under Section 10.2.5;

.11 failure of the Contractor to submit prerequisite documentation required by the General Requirements; or

.12 liquidated damages due the Owner pursuant to Section 8.4.

9.5.3 Delete sub-section 9.5.3.

9.6.4 Delete "If the Contractor fails to furnish such evidence within seven days," from the beginning of the second sentence.

9.6.5 Delete sub-section 9.6.5.

9.6.7 Delete sub-section 9.6.7.

9.6.8 Add new sub-section 9.6.8 as follows:

§ 9.6.8 Notwithstanding the provisions of Section 9.6 all progress payments shall be made in accordance with Chapter 30, Sections 39F, 39G and 39K (as appropriate) of the General Laws of the Commonwealth of Massachusetts, as amended.

9.7 Delete section 9.7.

9.8.1 Add to the end of the sub-section as follows:

In addition, Substantial Completion for the entire Project shall be achieved only when: (1) the Owner has beneficial occupancy and use of the entire Project for all its intended uses; (2) all Project systems included in the Work are operational and acceptable to the Owner; (3) all governmental inspections for the Project have been successfully completed, all governmental approvals and related paperwork have been delivered to the Owner, and final and unconditional certificates of occupancy for the entire Project have been delivered to the Owner, (4) the only remaining Work to be performed is minor in nature and the remaining Work may reasonably be performed without having a material adverse effect on or materially interfering with the Owner's occupancy and use of the Project and (5) all

prerequisites to Substantial Completion defined in the Contract Documents have been completed.

9.8.2 Add to the end of the first sentence as follows:

together with the estimated value of completing or correcting such items (the “Punchlist”) and (2) the permits and certificates referenced in Section 13.5. The Architect shall have the right to modify and supplement the Punchlist, including the estimated value of completion or correction.

9.8.5 Delete sub-section 9.8.5 and replace as follows:

§ 9.8.5 The Certificate of Substantial Completion shall be submitted to the Owner and Contractor by the Architect. The certificate shall state the date of substantial completion, shall state any consequent responsibilities of the Contractor and the Owner in accordance with the Contract Documents. The Contractor shall complete and correct any incomplete and defective work within forty-five (45) calendar days from the date of Substantial Completion

9.8.6 Add new sub-section 9.8.6 as follows:

§ 9.8.6 Services provided by the Architect to conduct more than three (3) inspections of completed Work and any inspections beyond sixty (60) days after the date of substantial completion of any portion of the Work as stated in the Agreement shall be paid by the Contractor to the Owner. The Owner may deduct the cost of such services and inspections from payments due the Contractor.

9.9.1 Delete the end of the first sentence starting after “Work at any stage”.

Delete the second sentence and replace as follows:

Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner has accepted in writing the responsibilities assigned to it and the Contractor for payments, retainage, if any, security, maintenance, heat, utilities, damage to the Work and insurance.

Delete the second to last sentence.

9.10.1 Add to the end of the sub-section as follows:

By Final Completion, the Contractor shall have completed its performance of all Punchlist items, completed all balancing of mechanical and other applicable systems and all seasonal system adjustments that are reasonably necessary to proper functioning of the completed Project, delivered to the Owner all operations and maintenance manuals and completed related training for such manuals, and delivered to the Owner all required warranties and guarantees.

9.10.3 Delete sub-sections 9.10.3 and 9.10.4.
-9.10.4

9.10.5 Insert “for payment for Work performed and of all other claims of which the payee knew or should have known at the time of final payment,” after “claims that payee”

9.10.6 Add new sub-section 9.10.6 as follows:

§ 9.10.6 Notwithstanding anything in the Contract Documents to the contrary, final payment shall be made in accordance with the requirements of G.L.c.30, §39K (building projects) or §39G (public works projects), as amended.

ARTICLE 10 PROTECTION OF PERSONS AND PROPERTY

10.2.1 Add new sub-heading .4 as follows:

.4 work or property of the Owner, its tenants, or other parties at or near the Project site with the Owner's permission.

10.2.5 At the beginning and end of the first sentence:

Delete “and” after “10.2.1.2”.

Insert “and 10.2.1.4” after “10.2.1.3”.

Delete the remainder of the first sentence as follows:

, except damage or loss attributable to acts or omissions of the Owner or Architect or anyone directly or indirectly employed by either of them, or by anyone for whose acts either of them may be liable, and not attributable to the fault or negligence of the Contractor.

Add to the end of the sub-section as follows:

Where the damage or loss presents an immediate danger to the public, the Owner, in its sole discretion and at the Contractor's expense, may promptly remedy such damage or loss without prior notice to the Contractor.

10.2.9 Add new sub-sections 10.2.9, 10.2.10, 10.2.11, 10.2.12, and 10.2.13 as follows:
-10.2.13

§ 10.2.9 The Contractor shall provide and maintain in good operating condition suitable and adequate fire protection equipment and services, and shall comply with all reasonable recommendations regarding fire protection made by the representatives of the fire insurance company carrying insurance on the Work or by the local fire chief or fire marshal. The area within the site limits shall be kept

orderly and clean, and all combustible rubbish shall be promptly removed from the site.

§ 10.2.10 The Contractor shall at all times protect excavations, trenches, buildings and materials from rain water, groundwater, backup or leakage of sewers, drains and other piping, and from water of any other origin and shall remove promptly any accumulation of water. The Contractor shall provide and operate all pumps, piping and other equipment necessary to this end.

§ 10.2.11 The Contractor shall remove snow and ice which might result in damage or delay.

§ 10.2.12 During the progress of the Work and at all times prior to the date of Substantial Completion or occupancy of the Work by the Owner, whichever is earlier, the Contractor shall provide temporary heat, ventilation, and enclosure, adequate to permit the Work to proceed in a timely fashion, and to prevent damage to completed Work or Work in progress, or to materials stored on the premises. The use of the permanent heating and/or ventilation systems for temporary heat and/or ventilation shall be subject to the prior written approval of the Owner and Architect.

§ 10.2.13 [G.L. c.149, §44F(1)] The Contractor shall install weather protection and furnish adequate heat in the protected area from November 1 to March 31.

10.3.1 Delete the second sentence and replace as follows:

The Contractor shall not cause or permit any introduction onto, under, or near the Owner's property of any hazardous materials or substances as defined by any applicable law, and shall not cause or permit any release, discharge, transportation, storage, or disposal of such materials or substances onto, under, or near the Owner's property or areas near the Owner's property. If the Contractor encounters or recognizes on the site any material known or reasonably believed to be hazardous, including but not limited to asbestos or polychlorinated biphenyl (PCB), the Contractor shall immediately stop Work in the area affected and report the condition to the Owner and Architect in writing. The Contractor and the Owner shall cooperate in implementing measures to remove or contain said material and the Contractor shall comply with all directions of the Architect in the implementation of such removal or containment.

10.3.2 Delete sub-sections 10.3.2, 10.3.3, and 10.3.4.

10.3.5 Delete the remainder of the sentence starting after "obligations under" and replace as follows:

Article 10 or for any violation of applicable law related to the Contractor's noncompliance with the provisions of this Article 10.

10.3.6 Delete sub-section 10.3.6.

10.3.7 Add new sub-section 10.3.7 as follows:

§ 10.3.7 The parties anticipate that certain hazardous substances and/or materials may be discovered at the site. When such conditions are set forth in the Contract Documents, the Contractor acknowledges that such conditions have been considered in establishing the Contract Time and Contract Sum. No extension of the Contract Time or increase in the Contract Sum shall be claimed or allowed with respect to any hazardous substances or materials located at the site which were disclosed in the Contract Documents. The Contractor shall strictly comply with all laws, regulations, rules, orders, ordinances and the like related to the excavation, storage, removal and disposal of any such hazardous substances or materials.

ARTICLE 11 INSURANCE AND BONDS

11.1.2 Delete sub-section 11.1.2 and replace as follows:

§ 11.1.2 The insurance required by Section 11.1.1 shall include all major divisions of coverage, and shall be on a comprehensive general basis including Premises and Operations (including X-C-U), Owner's and Contractor's Protective, Products and Completed Operations, and Owned, Non-owned, and Hired Motor Vehicles. Such insurance shall be written for not less than any limits of liability required by law or those set forth in the Contract Documents, whichever is greater.

All insurance shall be written on an occurrence basis, unless the Owner approves in writing coverage on a claims-made basis. Coverages, whether written on an occurrence or claims-made basis, shall be maintained without interruption from date of commencement of the Work until date of final payment and any further period during which coverage is required to be maintained after final payment by the Contract Documents. The Owner shall be named an Additional Insured on all policies.

Coverage for such liability insurance shall be provided by a company or companies reasonably acceptable to the Owner and authorized to do business in Massachusetts. Contractor shall furnish to Owner written confirmation as to the insurance carrier's most current financial ratings prior to commencing work.

11.1.3 Add to the end of the sub-section as follows:

These certificates shall set forth evidence of all coverage required by Sections 11.1.1 and 11.1.2. The Contractor shall furnish to the Owner copies of any endorsements that are subsequently issued amending limits of coverage.

11.1.3.1 Add new sub-sections 11.1.3.1 and 11.1.3.2 as follows:

-11.1.3.2

11.1.3.1 The Contractor shall be responsible for having acceptable insurance coverage provided by or on behalf of all Subcontractors, with such insurance to be similar to that required of the Contractor under the Agreement and these General Conditions. The Contractor shall not allow any Subcontractor to commence Work on the Project prior to the Contractor's receipt of certificates of insurance that are acceptable in form and limits to the Owner; the Owner shall have no obligation to pay the Contractor for any Work performed by a Subcontractor who has not supplied acceptable insurance certificates prior to starting its Work. The Owner shall be named an additional insured on all such certificates.

11.1.3.2 All insurance policies shall contain provisions or endorsements necessary to assure coverage of claims by one insured against another. All required insurance policies are to be endorsed to state that the Contractor's policies shall be primary to all other insurance available to the Owner and other specified additional insureds for liability arising out of or resulting from the Contractor's operations under the Contract, whether such operations be by the Contractor or by a Subcontractor or by anyone directly or indirectly employed by any of them or by anyone for whose acts any of them may be liable.

11.1.4 Insert "the Owner's Project Manager," after "(1) the Owner,".

11.1.5 Add new sub-section 11.1.5 as follows:

§ 11.1.5 In no case shall the limits of liability be less than the following:

1. Contractor's Liability Insurance
 - a. Workers' Compensation:
 1. State: Statutory
 2. Employer Liability:
 - \$500,000 Bodily Injury by Accident
 - \$500,000 Bodily Injury by Disease - policy limit
 3. \$500,000 Bodily Injury by Disease - each
\$2,000,000 Umbrella Liability - all limits
 - b. Comprehensive General Liability (including Premises-Operations; Independent Contractor's Protective; Products and Completed Operations; Broad Form Property Damage):
 1. Bodily Injury:
\$1,000,000 Each Occurrence
\$3,000,000 Aggregate

2. Products and Completed Operations
\$1,000,000 Each Occurrence (bodily injury and property damage)
\$3,000,000 Aggregate
 3. Property Damage Liability (including coverage for XCU hazards).
\$1,000,000 Each Occurrence
\$3,000,000 Aggregate
 4. Products and Completed Operations insurance shall be maintained for a minimum period of 2 years after final payment and Contractor shall continue to provide evidence of such coverage to Owner on an annual basis during the aforementioned.
 5. Contractual Liability (Hold Harmless Coverage):
\$1,000,000 Bodily Injury Each Occurrence
\$1,000,000 Property Damage Each Occurrence
\$3,000,000 Property Damage Aggregate
 6. Personal Injury, with Employment Exclusion deleted:
\$1,000,000 All Limits
- c. Comprehensive Automobile Liability (owned, non-owned, hired):
1. Bodily Injury
\$1,000,000 Each Person
\$1,000,000 Each Accident
 2. Property Damage
\$1,000,000 Each Accident
- d. Property Insurance / Builders Risk: the full Contract sum
- e. Umbrella Liability Coverage
\$2,000,000 All Limits

11.2 Delete section 11.2 and replace as follows:

§ 11.2 OWNER'S LIABILITY INSURANCE

The Contractor shall procure and pay for an Owner's policy of Owner's protective liability insurance insuring the Owner and its officers, employees and agents

against claims which may arise from operations under the Contract or relating thereto.

11.3.1 Delete sub-section 11.3.1 and replace as follows:

§ 11.3.1 The Contractor shall purchase and maintain property insurance upon the entire Work at the site to the full insurable value thereof. Coverage for such liability insurance shall be provided by a company or companies reasonably acceptable to the Owner. Contractor shall furnish to Owner written confirmation as to the insurance carrier's most current financial ratings prior to commencing work. Such insurance shall include the interests of the Owner, the Contractor, Subcontractors and Sub-subcontractors in the work and shall insure against the perils of fire and extended coverage and shall include "all risks" insurance for physical loss or damage including without duplication, theft, vandalism and malicious mischief. This insurance shall also cover portions of the Work stored off the site or in transit. If this insurance is written with stipulated amounts deductible, the Owner shall not be responsible for any difference between the payments made by the insurance carrier and the claim. The policy shall contain a provision that coverages afforded under policies will not be canceled or allowed to expire until at least 30 days' written notice has been given to the Owner. The Owner shall be named insured within the policy.

11.3.1.1 Delete sub-sections 11.3.1.1, 11.3.1.2, 11.3.1.3, 11.3.1.4, and 11.3.1.5.
-11.3.1.5

11.3.2 Delete sub-sections 11.3.2, 11.3.3, 11.3.4, 11.3.5, 11.3.6, and 11.3.7.
-11.3.7

11.3.8 Delete the first sentence.

11.3.9 Delete sub-sections 11.3.9 and 11.3.10.
-11.3.10

11.3.11 Add new sub-section 11.3.11 as follows:

§ 11.3.11 The Owner shall have the power to adjust and settle with its insurers any loss for which it has obtained insurance.

Upon the occurrence of an insured loss, the Owner and the Contractor shall cooperate with each other and with each other's insurer in the submission of claims and related information and the distribution of any insurance proceeds. If after such a loss no other special agreement is made, replacement of damaged work shall be covered by an appropriate change order.

11.4.1 Delete "Owner shall have the right to require the".

Delete “to” after “Contractor” and replace with “shall”.

Delete the end of the sentence starting after “obligations arising thereunder” and replace as follows:

, each in the amount of 100% of the Contract Price, and each by a surety company qualified to do business under the laws of the Commonwealth of Massachusetts and acceptable to the Owner. The attorney-in-fact who signs the bonds on behalf of the surety, must affix to each bond a certified and current copy of the power of attorney. The Performance and Payment Bonds shall be written in a form satisfactory to the Owner.

ARTICLE 12 UNCOVERING AND CORRECTION OF WORK

12.2.1 Add to the end of the sub-section as follows:

The Contractor shall bear the cost of any loss or damages to the Owner resulting from such failure or defect.

12.2.2.1 Delete the third sentence.

Add to the end of the sub-section as follows:

If the correction or repair of any of the Work is required to avoid impacts to the maintenance, operation or safety of any portion of the Project site or the Owner’s property, the Owner reserves the right to undertake the repairs prior to notifying the Contractor or without waiting for the Contractor to respond, without waiving the Owner’s rights under the warranties and the Owner’s right to correct work under Section 2.4.

ARTICLE 13 MISCELLANEOUS PROVISIONS

13.1 Delete the end of the sentence following the words “by the law of the”, and insert the words “Commonwealth of Massachusetts” at the end of the sentence as revised.

13.2.1 In the second sentence delete “Except as provided in Section 13.2.2”.

13.2.2 Delete sub-section 13.2.2.

13.5.4 Delete sub-section 13.5.4 and replace as follows:

§ 13.5.4 The Contractor shall obtain and deliver promptly to the Architect any occupancy permit and any certificates of final inspection of any part of the Contractor's work and operating permits for any mechanical apparatus, such as elevators, escalators, boilers, air compressors, etc., which may be required by law to permit full use and occupancy of the premises by the Owner. Receipt of such

permits or certificates by the Architect shall be a condition precedent to Substantial Completion of the Work.

13.7 Delete section 13.7.

13.7.1 Add new sub-section 13.7.1 as follows:

§ 13.7.1 It is expressly agreed that the obligations of the Contractor hereunder arise out of contractual duties, and that the failure of the Contractor to comply with the requirements of the Contract Documents shall constitute a breach of contract, not a tort, for the purpose of applicable statutes of limitation and repose. Any cause of action which the Owner may have on account of such failure shall be deemed to accrue only when the Owner has obtained actual knowledge of such failure, not before.

13.8 Add new section 13.8 as follows:

§ 13.8 LIMITATION OF LIABILITY

§ 13.8.1 The Owner shall be liable, if ever, only to the extent of its interest in the Project; and no officer, director, partner, agent or employee of the Owner shall ever be personally or individually liable with respect to this Contract or the Work. Each Subcontract shall include the foregoing limitation, which shall be effective if the Owner ever succeeds to the Contractor's rights and obligations under a Subcontract.

13.9 Add new section 13.9 as follows:

§ 13.9 DEFENSE OF SUITS

§ 13.9.1 The Contractor shall be responsible for, shall defend and pay all costs, attorneys' fees and liabilities both direct and indirect as a result of suits arising out of this Contract.

§ 13.9.2 Neither final acceptance nor occupation of the premises by the Owner shall relieve the Contractor of responsibility for all claims for labor, materials, and equipment arising out of this Contract.

§ 13.9.3 The Contractor shall indemnify and hold harmless the Owner and the Architect and their agents and employees from and against all claims, damages, losses, and expenses including attorneys' fees arising out of or resulting from the performance of the work.

ARTICLE 14 TERMINATION OR SUSPENSION OF THE CONTRACT

14.1.1 Insert in the beginning of the first sentence as follows:

Provided that the Contractor is not in breach of any of its obligations under the Contract,

Delete sub-headings .1, .2, and .4.

14.1.2 Delete sub-section 14.1.2.

14.1.3 Delete sub-section 14.1.3 and replace as follows:

§ 14.1.3 If one of the above reasons exists, the Contractor may, upon seven days written notice to the Owner and Architect, terminate the Contract and recover from the Owner payment for Work properly executed and for all materials or equipment not incorporated in the Work, but delivered and suitably stored at the site. The payment for materials or equipment stored at the site shall be conditioned upon submission by the Contractor of bills of sale or such other evidence as is satisfactory to the Owner to establish the Owner's title to such material or equipment or otherwise protect the Owner's interest.

14.1.4 Delete sub-section 14.1.4.

14.2.1 Delete “repeatedly” from the beginning of sub-headings .1 and .3.

Insert new sub-headings .4 and .5 after sub-heading .3 as follows:

.4 becomes the subject of a voluntary petition in bankruptcy or any voluntary proceeding related to insolvency, receivership, liquidation or comparable proceeding or any assignment for the benefit of creditors or becomes the subject of an involuntary petition in bankruptcy or any involuntary proceeding related to insolvency, receivership, liquidation or comparable proceeding or any assignment for the benefit of creditors.

.5 submits three successive Applications for Payment, each of which indicate that the actual Work completed is less than 90 percent of the values estimated in the construction schedule (submitted by the Contractor pursuant to Section 3.10.1) to be completed by the respective dates.

14.2.2 In the first sentence delete “,upon certification by the Initial Decision Maker that sufficient cause exists to justify such action,”.

Delete the second sentence of sub-heading .3.

14.2.4 In the first sentence:

Insert “all costs and losses incurred by the Owner on account of the Contractor’s failure to comply with the Contract Documents and” after “the Work, including”.

Insert “and Owner’s Project Manager’s” after “for the Architect’s”.

Delete the last sentence of the sub-section and replace as follows:

The Owner shall be entitled to hold all amounts due the Contractor at the date of termination until all of the Owner’s damages have been established, and to apply such amounts to such damages.

14.3.2 Insert “, subject to compliance with the conditions of Section 8.3.” at the end of the first sentence.

Delete the second sentence.

14.4.2 In sub-heading .3 delete “and” after “all existing contracts” and replace with “except for subcontracts, if any, that Owner elects to assume, terminate all”

14.4.3 Delete sub-section 14.4.3 and replace as follows:

§ 14.4.3 In the event that the Contract is terminated for the Owner’s convenience, the Contractor shall be reimbursed in accordance with the Contract Documents for all Work properly performed up to the termination date, and for all materials or equipment not incorporated in the Work, but delivered and suitably stored at the site. Payment for materials or equipment stored at the site shall be conditioned upon submission by the Contractor of bills of sale or such other evidence as is satisfactory to the Owner to establish the Owner’s title to such material or equipment or otherwise protect the Owner’s interest. The Contractor shall not be entitled to payment for overhead and profit on the Work not executed.

ARTICLE 15 CLAIMS AND DISPUTES

15.1.1 Delete sub-section 15.1.1 and replace as follows:

§ 15.1.1 DEFINITION

The word “Claim” shall mean a written demand by the Contractor for an increase in the Contract Time or the Contract Sum. The Contractor is responsible for substantiating its Claims. The word “Claim” shall not include claims by the Owner. The Owner may withhold from the Contractor the value of any claims against the Contractor in accordance with Massachusetts General Laws, including, but not limited to, Sections 39G and 39K of Chapter 30.

15.1.2 Delete sub-section 15.1.2 and replace as follows:

§ 15.1.2 NOTICE OF CLAIMS

Contractor must initiate Claims within fourteen (14) calendar days after occurrence of the event giving rise to such Claim by written notice to the Architect and the Owner. Such written notice must (1) be signed by the Contractor; (2) conspicuously identify on its face that the notice serves as a notice of claim; (3) explain in sufficient detail the basis of the Claim; (4) identify the date of the event giving rise to such Claim; and (5) state the exact dollar amount of the increase in the Contract Sum being requested, if any, and the number of days extension to the Contract Time sought, if any.

15.1.3 Delete “Section 9.7 and” after “as provided in”.

Delete the final sentence.

15.1.5.1 In the second sentence delete “of cost and” after “include an estimate”.

15.1.5.2 Delete sub-section 15.1.5.2.

15.1.6 Delete sub-section 15.1.6.

15.2.1 In the third sentence:

Delete “mediation” after “condition precedent to” and replace with “litigation”.

Delete the end of the sentence beginning after “payment is due”.

15.2.2 Delete sub-section 15.2.2 and replace as follows:

§ 15.2.2 The Initial Decision Maker will review Claims and within 30 days of the receipt of the Claim take one or more of the following actions: (1) request additional supporting data from the Contractor; (2) notify the Contractor that the Initial Decision Maker requires additional time to resolve the Claim; and/or (3) reject the Claim in whole or in part.

15.2.3 Delete the last sentence.

15.2.4 Delete sub-section 15.2.4 and replace as follows:

§ 15.2.4 If the Architect requests the Contractor to furnish additional supporting data in connection with a Claim, the Contractor shall provide such data within ten (10) calendar days of such request. If the Contractor is of the opinion that it is impossible to provide such data within such time, the Contractor shall notify the Architect of such opinion in writing within such ten-day period. If the Architect determines that it is impossible for such data to be provided within such ten-day

period through no fault of the Contractor, the Contractor shall provide such data within 30 calendar days of the Architect's request, unless the Architect fixes another date, in which case the data must be submitted by the date so fixed. Failure of the Contractor to provide such data within the time prescribed herein shall result in the irrevocable waiver of the Claim.

15.2.5 Delete the last sentence and replace as follows:

The rejection of a claim by the Architect and any decisions of the Owner with respect to the same, and the interpretations by the Architect of the plans, drawings and specifications, shall be final and binding on the Contractor in accordance with Section 39J of Chapter 30 of the Massachusetts General Laws.

15.2.6 Delete sub-section 15.2.6 in its entirety.

15.2.7 Delete the capitalized word, "Claim," and replace with lower-case word, "claim," in the first and second sentences.

15.2.8 Delete sub-section 15.2.8.

15.3 Delete sections 15.3 and 15.4 in their entirety.
-15.4

423687v2/KOPE/0068

SECTION 00800

SPECIAL CONDITIONS

Page

1. Introduction
2. Prevailing Wage Rates
3. Insurance Requirements

SECTION 00850 - Incorporation of Applicable Provisions of the Massachusetts General Laws

Attachment A - Wage Rates and Certificate of Compliance

§ SC 1.1 INTRODUCTION

The following provisions modify, change, delete from or add to Section 00700 GENERAL CONDITIONS. Where any Subsection of the General Conditions is modified or any Article Paragraph, Subparagraph or Clause thereof is modified or deleted by these Supplemental General Conditions, the unaltered provisions of that Article, Paragraph, Subparagraph or Clause shall remain in effect.

§ SC 2.1 PREVAILING WAGES

In accordance with General Laws Chapter 149, Section 26 through 27D, the Contractor is obligated to comply with the prevailing wage rates established by the Commissioner of the Department of Labor and Workforce Development for mechanics, apprentices, chauffeurs, teamsters and laborers employed on the Project. The schedule of applicable prevailing wage rates for the Project, together with a Certificate of Compliance therewith, are set forth in Attachment A herein.

§ SC 3.1 CONTRACTOR'S LIABILITY INSURANCE

In no case shall the limits of liability be less than the following:

1. Contractor's Liability Insurance
 - a. Workers' Compensation:
 1. State: Statutory
 2. Employer Liability:
 - \$500,000 Bodily Injury by Accident
 - \$500,000 Bodily Injury by Disease - policy limit
 3. \$500,000 Bodily Injury by Disease - each
\$2,000,000 Umbrella Liability - all limits
 - b. Comprehensive General Liability (including Premises-Operations; Independent Contractor's Protective; Products and Completed Operations; Broad Form Property Damage):
 1. Bodily Injury:
\$1,000,000 Each Occurrence
\$3,000,000 Aggregate
 2. Products and Completed Operations
\$1,000,000 Each Occurrence (bodily injury and property damage)
\$3,000,000 Aggregate
 3. Property Damage Liability (including coverage for XCU hazards).
\$1,000,000 Each Occurrence
\$3,000,000 Aggregate
 4. Products and Completed Operations insurance shall be maintained for a minimum period of 2 years after final payment and Contractor shall continue to provide evidence of such coverage to Owner on an annual basis during the aforementioned.
 5. Contractual Liability (Hold Harmless Coverage):
\$1,000,000 Bodily Injury Each Occurrence
\$1,000,000 Property Damage Each Occurrence
\$3,000,000 Property Damage Aggregate

- 6. Personal Injury, with Employment Exclusion deleted:
\$1,000,000 All Limits

- c. Comprehensive Automobile Liability (owned, non-owned, hired):
 - 1. Bodily Injury
\$1,000,000 Each Person
\$1,000,000 Each Accident

 - 2. Property Damage
\$1,000,000 Each Accident

- d. Property Insurance / Builders Risk: the full Contact sum

- e. Umbrella Liability Coverage
\$2,000,000 All Limits

SECTION 00850

Incorporation of Applicable Provisions of the Massachusetts General Laws

Certain provisions of the Massachusetts General Laws are applicable to Construction contracts including, but not limited to, those contained in Chapter 30 and Chapter 149. All applicable provisions of the Massachusetts General Laws are incorporated into the Contract as if fully set forth herein, and shall prevail over any conflicting provisions of the General or Supplemental General Conditions.

LEGAL NOTICE

Invitation to Bid

Phase 1 Building Stabilization – 12 North Main Street

Town of Westford, Massachusetts

The Town of Westford requests sealed bids for the stabilization of an historic mill building located at 12 North Main Street in Westford, MA. The project will include debris removal, hazardous material abatement, structural reinforcement of historic floor beams, and stabilization of an historic smoke stack.

Specifications are available at the Town Manager's office, 55 Main Street, Westford MA. 01886 or online at www.westfordma.gov/bidlist starting on October 16, 2015. Sealed bids will be received in the office of the Town Manager, 55 Main Street, Westford, MA. 01886 until 2:00 p.m. on November 6, 2015, at which time they will be publicly opened.

The Board of Selectmen is the awarding authority for this contract and reserves the right to reject any and all bids, any part of a bid, or any item in whole or in part, and award the contract as deemed in the best interest of the Town.

SUBSTITUTION REQUEST FORM

INFORMATION AVAILABLE TO BIDDERS

**SUBSTITUTION REQUEST FORM
(to be used during the Bidding Phase)**



SUBSTITUTION REQUEST (During the Bidding Phase)

Project: Phase 1 Stabilization Project, 12 North Main Street Westford, MA
Substitution Request Number:
From:
To:
Date:
A/E Project Number: 3246.00
Re:
Contract For:

Specification Title:
Description:
Section:
Page:
Article/Paragraph:

Proposed Substitution:
Manufacturer:
Address:
Phone:
Trade Name:
Model No.:

Attached data includes product description, specifications, drawings, photographs, and performance and test data adequate for evaluation of the request; applicable portions of the data are clearly identified.

Attached data also includes a description of changes to the Contract Documents that the proposed substitution will require for its proper installation.

The Undersigned certifies:

- Proposed substitution has been fully investigated and determined to be equal or superior in all respects to specified product.
Same warranty will be furnished for proposed substitution as for specified product.
Same maintenance service and source of replacement parts, as applicable, is available.
Proposed substitution will have no adverse effect on other trades and will not affect or delay progress schedule.
Proposed substitution does not affect dimensions and functional clearances.
Payment will be made for changes to building design, including A/E design, detailing, and construction costs caused by the substitution.

Submitted by:
Signed by:
Firm:
Address:
Telephone:

A/E's REVIEW AND ACTION

- Substitution approved - Make submittals in accordance with Specification Section 01330.
Substitution approved as noted - Make submittals in accordance with Specification Section 01330.
Substitution rejected - Use specified materials.
Substitution Request received too late - Use specified materials.

Signed by: Date:

Supporting Data Attached: Drawings Product Data Samples Tests Reports

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes the following:
 - 1. Work covered by the Contract Documents.
 - 2. Drawing List
 - 3. Type of the Contract.
 - 4. Work sequence.
 - 5. Use of premises.
 - 6. Owner's occupancy requirements.
 - 7. Work restrictions, including utility interruptions.
 - 8. Specification formats and conventions.
- B. Related Sections include the following:
 - 1. Division 01 Section "Temporary Facilities and Controls" for temporary access aids and weather and security barriers.

1.3 WORK COVERED BY CONTRACT DOCUMENTS

- A. Project Identification: Phase 1 Building Stabilization Project – 12 North Main Street. The existing building complex is also known as the former Abbot Worsted Company Mill #1 or, simply, the "Abbot Mill."
- B. Project Location: 12 North Main Street, Village of Graniteville, Westford, Massachusetts 01886
- C. Owner: Town of Westford, 55 Main Street, Westford, Massachusetts 01886.
- D. Owner's Project Manager: [Optional; to be determined].
- E. Architect: Bargmann Hendrie + Archetype, Inc., 300 A Street, Boston, MA 02210.
- F. The Work consists of the following:
 - 1. General site access, mobilization and demobilization.
 - 2. Removal of vegetation (clear and grub) surrounding building.
 - 3. Supply and installation of timber shoring posts and associated rough carpentry and hardware.
 - 4. Removal of selected loose bricks from top of smokestack, followed by wrapping and cabling area designated to prevent other loose bricks from falling.
 - 5. Supply and installation of timber-plank walkway assemblies across designated portions of existing, rotted timber flooring.
 - 6. Plywood window boarding assemblies at designated masonry openings.

SECTION 01 10 00
SUMMARY

7. Alternate No. 1: Abatement of designated hazardous materials and removal of collapsed roof, wall and floor assemblies and miscellaneous debris, at east end of main mill block (i.e., between column lines B, D, 1 and 19).
8. Alternate No. 2: Abatement of designated hazardous materials and removal of collapsed roof, wall and floor assemblies and miscellaneous debris, at west end of main mill block (i.e., between column lines B, D, 19 and 29) and at south ell (i.e., between column lines D, F, 28 and 29).
9. Alternate No. 3: Provide water-resistant, tear-resistant, flame-resistant reinforced plastic tarpaulins ("tarps"), secured to upper and lower roofs of belfry with braided ropes and associated hardware. Provide wood-framed, braced, plywood-covered armature as required to protect historic iron cresting. Refer to Drawing A200 and to Specification Sections 01 50 00 Temporary Facilities and Controls and 06 10 00 Rough Carpentry.

1.4 TYPE OF CONTRACT

- A. The project will be constructed under a single prime contract.

1.5 HISTORIC PRESERVATION WORK

- A. The extant building complex dates to 1859, with numerous later additions and alterations. The roof structure added ca. 1970 failed over time, resulting in the near total collapse roof trusses, sheathing, decking and roofing materials in the main mill block. The construction debris resting on the floor beneath has exacerbated water-related deterioration of masonry walls and timber beams and decking.
- B. This project is funded using Community Preservation Act (CPA) money and has been overseen by the Town of Westford Community Preservation Committee (CPC). Construction funding was also authorized by vote at Town Meeting, October 19, 2015.
- C. For definitions of treatment approaches and other relevant terminology and for illustrated examples and guidelines, refer to The Secretary of the Interior's Standards for the Treatment of Historic Properties and Illustrated Guidelines for Preserving, Rehabilitating, Restoring, and Reconstructing Historic Buildings, by Kay D. Weeks and Anne E. Grimmer.

1.6 SITE CONDITIONS

- A. Existing Construction to Remain: All work is to be executed in such a way as to minimize any impact on historic fabric. The Contractor and all subcontractors shall examine the construction site prior to beginning any work and shall satisfy themselves as to the existing conditions under which they will be obliged to operate, or that will in any way affect the work of this Contract.
- B. Existing Utilities
 1. Existing active utility lines, including without limitation, overhead power and telephone wires and cables, shall, if damaged, be immediately repaired, inspected by the utility company, protected and maintained, at no additional cost to the Owner.
 2. Stabilization of the upper portion of the existing smokestack (as specified in Section 02 44 00) may require temporary shut-down and/or relocation of electric power and telephone lines; coordination of work with local utility companies and advance notification of residents may be required as part of the contract work.

SECTION 01 10 00
SUMMARY

- C. Lead Hazard Precautions: Assume that lead-based paint is found on existing surfaces, and take appropriate precautions in accordance with local, state and federal safety and code requirements, during surface preparation and other Contract work.

1.7 USE OF PREMISES

- A. General: Contractor shall have full use of premises for construction operations.
- B. Use of Site: Limit use of premises to work in areas indicated. Do not disturb portions of Project site beyond areas in which the Work is indicated.
 - 1. Owner Occupancy: Allow for Owner access to Project site for security, and for construction observation purposes.
 - 2. Driveways and Entrances: Keep driveways on premises clear and available to abutters and to emergency vehicles at all times. Do not use these areas for parking or storage of materials.
 - a. Schedule deliveries to minimize use of driveways and entrances.
 - b. Schedule deliveries to minimize space and time requirements for storage of materials and equipment on-site.
- C. Use of Existing Building: At the intact north wing and south ell of the complex, maintain the existing building in a weathertight condition throughout the construction period. Repair damage caused by construction operations.
 - 1. At the contractor's discretion, office space adjacent to the bell tower can be outfitted as a construction field office, in lieu of providing a prefabricated trailer on site.

1.8 OWNER'S OCCUPANCY REQUIREMENTS

- A. Owner Occupancy: Work areas will remain unoccupied throughout the renovation project period.

1.9 WORK SEQUENCE

- A. The Contractor and applicable Subcontractors must maintain a sufficient work force at all times to ensure satisfactory completion within the allotted time period.

1.10 WORK RESTRICTIONS

- A. On-Site Work Hours: Work shall be generally performed during normal business working hours and as regulated by the local authorities having jurisdiction. No work will be allowed on weekends or established Holidays without prior permission by the Town of Westford Building Department.
- B. Existing Utility Interruptions: Do not interrupt utilities serving facilities occupied by Owner or others unless permitted under the following conditions and then only after arranging to provide temporary utility services according to requirements indicated:
 - 1. Notify Owner not less than five days in advance of proposed utility interruptions.
 - 2. Do not proceed with utility interruptions without Owner's written permission.
- C. Nonsmoking job site: Smoking is not permitted within the building or within 25 feet of the existing fenced enclosure.

SECTION 01 10 00
SUMMARY

1.11 SPECIFICATION FORMATS AND CONVENTIONS

- A. Specification Format: The Specifications are organized into Divisions and Sections using the CSI MasterFormat™ 2004 numbering system.
 - 1. Section Identification: The Specifications use Section numbers and titles to help cross-referencing in the Contract Documents. Sections in the Project Manual are in numeric sequence; however, the sequence is incomplete because all available Section numbers are not used. Consult the table of contents at the beginning of the Project Manual to determine numbers and names of Sections in the Contract Documents.
 - 2. Division 1: Sections in Division 1 govern the execution of the Work of all Sections in the Specifications.

- B. Specification Content: The Specifications use certain conventions for the style of language and the intended meaning of certain terms, words, and phrases when used in particular situations. These conventions are as follows:
 - 1. Abbreviated Language: Language used in the Specifications and other Contract Documents is abbreviated. Words and meanings shall be interpreted as appropriate. Words implied, but not stated, shall be inferred as the sense requires. Singular words shall be interpreted as plural, and plural words shall be interpreted as singular where applicable as the context of the Contract Documents indicates.
 - 2. Imperative mood and streamlined language are generally used in the Specifications. Requirements expressed in the imperative mood are to be performed by Contractor. Occasionally, the indicative or subjunctive mood may be used in the Section Text for clarity to describe responsibilities that must be fulfilled indirectly by Contractor or by others when so noted.
 - a. The words "shall," "shall be," or "shall comply with," depending on the context, are implied where a colon (:) is used within a sentence or phrase.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION (Not Used)

END OF SECTION 01 10 00

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes administrative and procedural requirements for alternates.

1.3 DEFINITIONS

- A. Alternate: An amount proposed by bidders and stated on the Bid Form for certain work defined in the Bidding Requirements that may be added to or deducted from the Base Bid amount if Owner decides to accept a corresponding change either in the amount of construction to be completed or in the products, materials, equipment, systems, or installation methods described in the Contract Documents.
 - 1. The cost or credit for each alternate is the net addition to or deduction from the Contract Sum to incorporate alternate into the Work. No other adjustments are made to the Contract Sum.

1.4 PROCEDURES

- A. Coordination: Modify or adjust affected adjacent work as necessary to integrate work of alternate into Project.
 - 1. Include as part of each alternate, miscellaneous devices, accessory objects, and similar items incidental to or required for a complete installation, whether or not indicated as part of alternate.
- B. Notification: Immediately following award of the Contract, notify each party involved, in writing, of the status of each alternate. Indicate if alternates have been accepted, rejected, or deferred for later consideration. Include a complete description of negotiated modifications to alternates.
- C. Execute accepted alternates under the same conditions as other work of the Contract.
- D. Schedule: A Schedule of Alternates is included at the end of this Section. Specification Sections referenced in schedule contain requirements for materials necessary to achieve the work described under each alternate.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION

3.1 SCHEDULE OF ALTERNATES

1. **Alternate No. 1:** At east end of main mill block (i.e., between column lines B, D, 1 and 19; see Drawings A101 and A102), abate designated hazardous materials, concurrent with other contract work. Refer to attached Abatement Work Plan dated October 13, 2015; abatement work under this Alternate shall include the interior volumes and perimeter walls. Remove collapsed roof structure, roofing materials, finishes and miscellaneous debris from surface of first-floor deck, leaving it "broom-clean." Remove collapsed first-floor areas and related debris at and beneath collapsed areas indicated on Drawings.
2. **Alternate No. 2:** At west end of main mill block (between column lines B, D, 19 and 29; see Drawings A101 and A102) and at south ell (between column lines D, F, 28 and 29), abate designated hazardous materials, concurrent with other contract work. Refer to attached Abatement Work Plan dated October 13, 2015; abatement work under this Alternate shall include the interior volumes and perimeter walls. Remove collapsed roof structure, roofing materials, finishes and miscellaneous debris from surface of first-floor deck, leaving it "broom-clean." Remove collapsed first-floor areas and related debris at and beneath collapsed areas indicated on Drawings.
3. **Alternate No. 3:** Provide tear-resistant, reinforced plastic tarpaulins ("tarps"), secured to upper and lower roofs of belfry with braided ropes. Provide wood-framed armature as required to protect iron cresting. Refer to Drawing A200 and to Specification Sections 01 50 00 Temporary Facilities and Controls and 06 10 00 Rough Carpentry.

END OF SECTION 01 23 00

SECTION 01 25 00
CONTRACT MODIFICATION PROCEDURES

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section specifies administrative and procedural requirements for handling and processing Contract modifications.
- B. Related Sections include the following:
 - 1. Division 01 Section "Alternates" for administrative requirements for using alternates.
 - 2. Division 01 Section "Project Management and Coordination"

1.3 MINOR CHANGES IN THE WORK

- A. Architect will issue supplemental instructions authorizing Minor Changes in the Work, not involving adjustment to the Contract Sum or the Contract Time, on AIA Document G710, "Architect's Supplemental Instructions."

1.4 PROPOSAL REQUESTS

- A. Owner-Initiated Proposal Requests: Architect will issue a detailed description of proposed changes in the Work that may require adjustment to the Contract Sum or the Contract Time. If necessary, the description will include supplemental or revised Drawings and Specifications.
 - 1. Proposal Requests issued by Architect are for information only. Do not consider them instructions either to stop work in progress or to execute the proposed change.
 - 2. Within 7 calendar days after receipt of Proposal Request, submit a quotation estimating cost adjustments to the Contract Sum and the Contract Time necessary to execute the change.
 - a. Include a list of quantities of products required or eliminated and unit costs, with total amount of purchases and credits to be made. If requested, furnish survey data to substantiate quantities.
 - b. Indicate applicable taxes, delivery charges, equipment rental, and amounts of trade discounts.
 - c. Include costs of labor and supervision directly attributable to the change.
 - d. Include an updated Contractor's Construction Schedule that indicates the effect of the change, including, but not limited to, changes in activity duration, start and finish times, and activity relationship. Use available total float before requesting an extension of the Contract Time.
- B. Contractor-Initiated Proposals: If latent or unforeseen conditions require modifications to the Contract, Contractor may propose changes by submitting a request for a change to Architect.
 - 1. Include a statement outlining reasons for the change and the effect of the change on the Work. Provide a complete description of the proposed change. Indicate the effect of the proposed change on the Contract Sum and the Contract Time.
 - 2. Include a list of quantities of products required or eliminated and unit costs, with total amount of purchases and credits to be made. If requested, furnish survey data to substantiate quantities.

SECTION 01 25 00
CONTRACT MODIFICATION PROCEDURES

3. Indicate applicable taxes, delivery charges, equipment rental, and amounts of trade discounts.
 4. Include costs of labor and supervision directly attributable to the change.
 5. Include an updated Contractor's Construction Schedule that indicates the effect of the change, including, but not limited to, changes in activity duration, start and finish times, and activity relationship. Use available total float before requesting an extension of the Contract Time.
 6. Comply with requirements in Division 01 Section "Product Requirements" if the proposed change requires substitution of one product or system for product or system specified.
- C. Proposal Request Form: Use AIA Document G709 for Proposal Requests or similar form acceptable to the Owner and Architect.

1.5 CHANGE ORDER PROCEDURES

- A. On Owner's approval of a Proposal Request, Architect will issue a Change Order for signatures of Owner and Contractor on AIA Document G701.

1.6 CONSTRUCTION CHANGE DIRECTIVE

- A. Construction Change Directive: Architect may issue a Construction Change Directive on AIA Document G714. Construction Change Directive instructs Contractor to proceed with a change in the Work, for subsequent inclusion in a Change Order.
1. Construction Change Directive contains a complete description of change in the Work. It also designates method to be followed to determine change in the Contract Sum or the Contract Time.
- B. Documentation: Maintain detailed records on a time and material basis of work required by the Construction Change Directive.
1. After completion of change, submit an itemized account and supporting data necessary to substantiate cost and time adjustments to the Contract.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION (Not Used)

END OF SECTION 01 25 00

BULLETIN

Distribution to the Representative of the:

- Owner - _____
- Architect - _____
- Consultant - _____
- Contractor - _____
- Field - _____
- Other - _____

BH+A Document B

PROJECT: 12 North Main Street Phase 1 Stabilization Project BULLETIN: **B -**
Westford, Massachusetts

OWNER: Town of Westford DATE OF ISSUANCE:

TO: ARCHITECT: Bargmann Hendrie + Archetype
(Contractor) 300 A Street
Boston, MA 02210-1710

ARCHITECT'S PROJECT NO: 3246.00

CONTRACT FOR: General Construction CONTRACT DATE:

Proposal Request (PR): Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein. Refer to this Document in the Proposal. Submit final costs for Work involved and change in Contract Time (if any) within _____ Working Days to the Architect. Note: This is neither a Change Order nor a direction to proceed with the work herein.

Supplemental Instructions (SI): The Work shall be carried out in accordance with the following supplemental instructions issued in accordance with the Contract Documents without change in Contract Sum or Contract Time. Prior to proceeding in accordance with these instructions, indicate your acceptance of these instructions for minor change to the Work as consistent with the Contract Documents and return a copy to the Architect within _____ Working Days.

Summary:
Description: (written description of work)

Attachments: (list attached documents which support description)

ISSUED: CONFIRMED:
BY _____ By: _____
Architect: BH+A Date Contractor: Date

AUTHORIZED:
BY _____
Owner's Agent: Date

SECTION 01 29 00
PAYMENT PROCEDURES

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section specifies administrative and procedural requirements necessary to prepare and process Applications for Payment.
- B. Related Sections include the following:
 - 1. Division 01 Section "Contract Modification Procedures" for administrative procedures for handling changes to the Contract.

1.3 DEFINITIONS

- A. Schedule of Values: A statement furnished by Contractor allocating portions of the Contract Sum to various portions of the Work and used as the basis for reviewing Contractor's Applications for Payment.

1.4 SCHEDULE OF VALUES

- A. Coordination: Coordinate preparation of the Schedule of Values with preparation of Contractor's Construction Schedule.
 - 1. Correlate line items in the Schedule of Values with other required administrative forms and schedules, including the following:
 - a. Application for Payment forms with Continuation Sheets.
 - b. Submittals Schedule.
 - c. Contractor's Construction Schedule.
 - 2. Submit the Schedule of Values to Owner's Project Manager at earliest possible date but no later than seven days before the date scheduled for submittal of initial Applications for Payment.
- B. Format and Content: Use the Project Manual table of contents as a guide to establish line items for the Schedule of Values. Provide at least one line item for each Specification Section.
 - 1. Identification: Include the following Project identification on the Schedule of Values:
 - a. Project name and location.
 - b. Name of Architect.
 - c. Architect's project number.
 - d. Contractor's name and address.
 - e. Date of submittal.

SECTION 01 29 00
PAYMENT PROCEDURES

2. Submit draft of AIA Document G703 Continuation Sheets.
3. Arrange the Schedule of Values in tabular form with separate columns to indicate the following for each item listed:
 - a. Related Specification Section or Division.
 - b. Description of the Work.
 - c. Name of subcontractor.
 - d. Change Orders (numbers) that affect value.
 - e. Dollar value.
 - 1) Percentage of the Contract Sum to nearest one-hundredth percent, adjusted to total 100 percent.
4. Provide a breakdown of the Contract Sum in enough detail to facilitate continued evaluation of Applications for Payment and progress reports. Coordinate with the Project Manual table of contents. Provide several line items for principal subcontract amounts, where appropriate. A minimum breakdown shall be as follows. Owner and Architect will expand this list upon receipt of preliminary Schedule of Values.
 - a. General Conditions
 - b. Bonds/Insurance
 - c. Mobilization
 - d. Contract Closeout
 - e. Selective Demolition
 - f. Shoring, Bracing and Support
 - g. All other Rough Carpentry not listed above
 - h. Hazardous Materials Abatement (Alternate No. 1)
 - i. Debris Removal (Alternate No. 2)
 - j. Tarps at Bell Tower Roofs (Alternate No. 3)
5. Round amounts to nearest whole dollar; total shall equal the Contract Sum.
6. Provide a separate line item in the Schedule of Values for each part of the Work where Applications for Payment may include materials or equipment purchased or fabricated and stored, but not yet installed.
 - a. Differentiate between items stored on-site and items stored off-site. If specified, include evidence of insurance or bonded warehousing.
7. Provide separate line items in the Schedule of Values for initial cost of materials, for each subsequent stage of completion, and for total installed value of that part of the Work.
8. Each item in the Schedule of Values and Applications for Payment shall be complete. Include total cost and proportionate share of general overhead and profit for each item.
 - a. Temporary facilities and other major cost items that are not direct cost of actual work-in-place may be shown either as separate line items in the Schedule of Values or distributed as general overhead expense, at Contractor's option.
9. Schedule Updating: Update and resubmit the Schedule of Values before the next Applications for Payment when Change Orders or Construction Change Directives result in a change in the Contract Sum.

SECTION 01 29 00
PAYMENT PROCEDURES

1.5 APPLICATIONS FOR PAYMENT

- A. Each Application for Payment shall be consistent with previous applications and payments as certified by Architect and paid for by Owner.
1. Initial Application for Payment, Application for Payment at time of Substantial Completion, and final Application for Payment involve additional requirements.
- B. Payment Application Times: The date for each progress payment is indicated in the Agreement between Owner and Contractor. The period of construction Work covered by each Application for Payment is the period indicated in the Agreement.
- C. Payment Application Forms: Use AIA Document G702 and AIA Document G703 Continuation Sheets as form for Applications for Payment.
- D. Application Preparation: Complete every entry on form. Notarize and execute by a person authorized to sign legal documents on behalf of Contractor. Owner's Project Manager will return incomplete applications without action.
1. Entries shall match data on the Schedule of Values and Contractor's Construction Schedule. Use updated schedules if revisions were made.
 2. Include amounts of Change Orders and Construction Change Directives issued before last day of construction period covered by application.
- E. Transmittal: Submit 4 signed and notarized original copies of each Application for Payment to Owner's Project Manager by a method ensuring receipt. One copy shall include waivers of lien and similar attachments if required.
1. Transmit each copy with a transmittal form listing attachments and recording appropriate information about application.
- F. Waivers of Mechanic's Lien: With each Application for Payment, submit waivers of mechanic's lien from every entity who is lawfully entitled to file a mechanic's lien arising out of the Contract and related to the Work covered by the payment.
1. Submit partial waivers on each item for amount requested in previous application, after deduction for retainage, on each item.
 2. When an application shows completion of an item, submit final or full waivers.
 3. Owner reserves the right to designate which entities involved in the Work must submit waivers.
 4. Waiver Forms: Submit waivers of lien on forms, executed in a manner acceptable to Owner.
- G. Initial Application for Payment: Administrative actions and submittals that must precede or coincide with submittal of first Application for Payment include the following:
1. List of subcontractors.
 2. Schedule of Values.
 3. Contractor's Construction Schedule (preliminary if not final).
 4. Submittals Schedule (preliminary if not final).
 5. List of Contractor's staff assignments.
 6. List of Contractor's principal consultants.
 7. Copies of building permits.
 8. Copies of authorizations and licenses from authorities having jurisdiction for performance of the Work.
 9. Initial progress report.
 10. Report of preconstruction conference.
 11. Certificates of insurance and insurance policies.

SECTION 01 29 00
PAYMENT PROCEDURES

12. Performance and payment bonds.
 13. Data needed to acquire Owner's insurance.
 14. Initial settlement survey and damage report if required.
- H. Application for Payment at Substantial Completion: After issuing the Certificate of Substantial Completion, submit an Application for Payment showing 100 percent completion for portion of the Work claimed as substantially complete.
1. Include documentation supporting claim that the Work is substantially complete and a statement showing an accounting of changes to the Contract Sum.
 2. This application shall reflect Certificates of Partial Substantial Completion issued previously for Owner occupancy of designated portions of the Work.
- I. Final Payment Application: Submit final Application for Payment with releases and supporting documentation not previously submitted and accepted, including, but not limited, to the following:
1. Evidence of completion of Project closeout requirements.
 2. Insurance certificates for products and completed operations where required and proof that taxes, fees, and similar obligations were paid.
 3. Updated final statement, accounting for final changes to the Contract Sum.
 4. AIA Document G706, "Contractor's Affidavit of Payment of Debts and Claims."
 5. AIA Document G706A, "Contractor's Affidavit of Release of Liens."
 6. AIA Document G707, "Consent of Surety to Final Payment."
 7. Evidence that claims have been settled.
 8. Final, liquidated damages settlement statement.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION (Not Used)

END OF SECTION 01 29 00



REQUEST FOR INTERPRETATION

Project: _____	R.F.I. Number: _____
_____	From: _____
To: _____	Date: _____
_____	A/E Project Number: _____
Re: _____	Contract For: _____

Specification Section: _____	Paragraph: _____	Drawing Reference: _____	Detail: _____
------------------------------	------------------	--------------------------	---------------

Request:

Signed by: _____	Date: _____
------------------	-------------

Response:

Attachments

Response From: _____	To: _____	Date Rec'd: _____	Date Ret'd: _____
----------------------	-----------	-------------------	-------------------

Signed by: _____	Date: _____
------------------	-------------

Copies: Owner Consultants _____ _____ _____ _____ File

ARCHITECT'S RESPONSE TO REQUEST FOR INFORMATION

Project: 12 North Main Street
Phase 1 Building Stabilization Project
Westford, Massachusetts

Owner: Town of Westford, Massachusetts

DATE:

CONTRACTOR'S RFI No.

FROM: **Bargmann Hendrie + Archetype, Inc.**
300 A Street
Boston, MA 02210
T: 617-350-0450
F: 617-350-0215
BH+A Project No. 3246.00

To:

Fax:
Pages:

The following is our response to the issues raised in the "Request for Information", noted above:

Attachments:

Distribution:

Comments:

SECTION 01 32 20
PHOTOGRAPHIC DOCUMENTATION

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes administrative and procedural requirements for the following:
 - 1. Preconstruction photographs.
 - 2. Periodic construction photographs.
 - 3. Final Completion construction photographs.
- B. Related Sections include the following:
 - 1. Division 01 Section "Submittal Procedures" for submitting photographic documentation.
 - 2. Division 01 Section "Closeout Procedures" for submitting digital media as Project Record Documents at Project closeout.
 - 3. Division 01 Section "Selective Demolition" for photographic documentation before selective demolition operations commence.

1.3 SUBMITTALS

- A. Qualification Data: For photographer.
- B. Key Plan: Submit key plan of Project site and building with notation of vantage points marked for location and direction of each photograph. Indicate elevation or story of construction. Include same label information as corresponding set of photographs.
- C. Construction Photographs: Submit two (2) prints of each photographic view within seven (7) days of taking photographs.
- D. Construction Photographs: Submit two (2) prints of each photographic view within seven (7) days of taking photographs.
 - 1. Format: 5-by-7 and/or 8-by-10-inch smooth-surface matte prints on digital photo paper, punched for standard 3-ring binder.
 - 2. Identification: On back of each page, print, provide an applied label, or rubber-stamp an impression with the following information:
 - a. Name of Project.
 - b. Name and address of photographer.
 - c. Name of Architect.
 - d. Name of Contractor.
 - e. Date photograph was taken if not date stamped by camera.

SECTION 01 32 20
PHOTOGRAPHIC DOCUMENTATION

- f. Description of vantage point, indicating location, direction (by compass point), and elevation or story of construction.
 - g. Unique sequential identifier.
3. Digital Images: Submit a complete set of digital image electronic files as a Project Record Document on CD-ROM. Identify electronic media with date photographs were taken. Submit images that have same aspect ratio as the sensor, uncropped.

1.4 QUALITY ASSURANCE

- A. Photographer Qualifications: An individual who has been regularly engaged as a photographer of construction projects for no less than three years.

1.5 COORDINATION

- A. Auxiliary Services: Cooperate with photographer and provide auxiliary services requested, including access to Project site and use of temporary facilities, including temporary lighting required to produce clear, well-lit photographs without obscuring shadows.

1.6 USAGE RIGHTS

- A. Obtain and transfer copyright usage rights from photographer to Owner for unlimited reproduction of photographic documentation.

1.7 EXTRA PRINTS

- A. Extra Prints: If requested by Architect, photographer shall prepare extra prints of photographs. Photographer shall distribute these prints directly to designated parties who will pay the costs for extra prints.

PART 2 - PRODUCTS

2.1 PHOTOGRAPHIC MEDIA

- A. Digital Images: Provide images in JPEG format, produced by a digital camera with minimum sensor size of 4.0 megapixels, and at an image resolution of not less than 1600 by 1200 pixels.

PART 3 - EXECUTION

3.1 CONSTRUCTION PHOTOGRAPHS

- A. Photographer: Engage a qualified in-house or commercial photographer to take construction photographs.
- B. General: Take photographs using the maximum range of depth of field, and that are in focus, to clearly show the Work. Photographs with blurry or out-of-focus areas will not be accepted.

SECTION 01 32 20
PHOTOGRAPHIC DOCUMENTATION

1. Maintain key plan with each set of construction photographs that identifies each photographic location.
- C. Digital Images: Submit digital images exactly as originally recorded in the digital camera, without alteration, manipulation, editing, or modifications using image-editing software.
1. Date and Time: Include date and time in filename for each image.
 2. Field Office Images: Maintain one set of images on CD-ROM in the field office at Project site, available at all times for reference. Identify images same as for those submitted to Architect.
- D. Preconstruction Photographs: Before commencement of demolition, take color, digital photographs of Project site and surrounding properties, including existing items to remain during construction, from different vantage points, as directed by Architect.
1. Flag construction limits before taking construction photographs.
 2. Take eight (8) photographs to show existing conditions adjacent to property before starting the Work.
 3. Take eight (8) photographs of existing buildings either on or adjoining property to accurately record physical conditions at start of construction.
 4. Take additional photographs as required to record settlement or cracking of adjacent structures, pavements, and improvements.
- E. Periodic Construction Photographs: Take eight (8) color, digital photographs weekly, with timing each month adjusted to coincide with the cutoff date associated with each Application for Payment. Select vantage points to show status of construction and progress since last photographs were taken.
- F. Final Completion Construction Photographs: Take eight (8) color photographs after date of Substantial Completion for submission as Project Record Documents. Architect will direct photographer for desired vantage points.
1. Do not include date stamp.
- G. Additional Photographs: Architect may issue requests for additional photographs, in addition to periodic photographs specified. Additional photographs will be paid for by Change Order and are not included in the Contract Sum.
1. Three days' notice will be given, where feasible.
 2. In emergency situations, take additional photographs within 24 hours of request.
 3. Circumstances that could require additional photographs include, but are not limited to, the following:
 - a. Special events planned at Project site.
 - b. Immediate follow-up when on-site events result in construction damage or losses.
 - c. Photographs to be taken at fabrication locations away from Project site. These photographs are not subject to unit prices or unit-cost allowances.
 - d. Substantial Completion of a major phase or component of the Work.
 - e. Extra record photographs at time of final acceptance.
 - f. Owner's request for special publicity photographs.

END OF SECTION 01 32 20

SECTION 01 33 00
SUBMITTAL PROCEDURES

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes administrative and procedural requirements for submitting Shop Drawings, Product Data, Samples, and other submittals.
- B. Related Sections include the following:
 - 1. Division 01 Section "Payment Procedures" for submitting Applications for Payment and the Schedule of Values.
 - 2. Division 01 Section "Project Management and Coordination" for submitting and distributing meeting and conference minutes and for submitting Coordination Drawings.
 - 3. Division 01 Section "Construction Progress Documentation" for submitting schedules and reports, including Contractor's Construction Schedule and the Submittals Schedule.
 - 4. Division 01 Section "Quality Requirements" for submitting test and inspection reports [and for mockup requirements].
 - 5. Division 01 Section "Closeout Procedures" for submitting warranties.
 - 6. Division 01 Section "Project Record Documents" for submitting Record Drawings, Record Specifications, and Record Product Data.
 - 7. Divisions 06 Sections for specific requirements for submittals in those Sections.

1.3 DEFINITIONS

- A. Action Submittals: Written and graphic information that requires Architect's responsive action.
- B. Informational Submittals: Written information that does not require Architect's responsive action. Submittals may be rejected for not complying with requirements.

1.4 SUBMITTAL PROCEDURES

- A. General: Electronic copies of CAD Drawings of the Contract Drawings will be provided by Architect for Contractor's use in preparing submittals. The Contractor will be required to sign a "Release Form" as provided by the Architect prior to release of the CADD file.
- B. Coordination: Coordinate preparation and processing of submittals with performance of construction activities.
 - 1. Coordinate each submittal with fabrication, purchasing, testing, delivery, other submittals, and related activities that require sequential activity.
 - 2. Coordinate transmittal of different types of submittals for related parts of the Work so processing will not be delayed because of need to review submittals concurrently for coordination.

SECTION 01 33 00
SUBMITTAL PROCEDURES

- a. Architect reserves the right to withhold action on a submittal requiring coordination with other submittals until related submittals are received.
- C. Submittals Schedule: Comply with requirements in Division 01 Section "Construction Progress Documentation" for list of submittals and time requirements for scheduled performance of related construction activities.
- D. Processing Time: Allow enough time for submittal review, including time for resubmittals, as follows. Time for review shall commence on Architect's receipt of submittal. No extension of the Contract Time will be authorized because of failure to transmit submittals enough in advance of the Work to permit processing, including resubmittals.
 1. Initial Review: Allow 10 days for initial review of each submittal. Allow additional time if coordination with subsequent submittals is required. Architect will advise Contractor when a submittal being processed must be delayed for coordination.
 2. Intermediate Review: If intermediate submittal is necessary, process it in same manner as initial submittal.
 3. Resubmittal Review: Allow 10 days for review of each resubmittal.
 4. Concurrent Consultant Review: Where the Contract Documents indicate that submittals may be transmitted simultaneously to Architect and to Architect's consultants, allow 15 days for review of each submittal. Submittal will be returned to Architect before being returned to Contractor.
- E. Identification: Place a permanent label or title block on each submittal for identification.
 1. Indicate name of firm or entity that prepared each submittal on label or title block.
 2. Provide a space approximately 6 by 8 inches (150 by 200 mm) on label or beside title block to record Contractor's review and approval markings and action taken by Architect.
 3. Include the following information on label for processing and recording action taken:
 - a. Project name.
 - b. Date.
 - c. Name and address of Architect.
 - d. Name and address of Contractor.
 - e. Name and address of subcontractor.
 - f. Name and address of supplier.
 - g. Name of manufacturer.
 - h. Submittal number or other unique identifier, including revision identifier.
 - 1) Submittal number shall use Specification Section number followed by a decimal point and then a sequential number (e.g., 06100.01). Resubmittals shall include an alphabetic suffix after another decimal point (e.g., 06100.01.A).
 - i. Number and title of appropriate Specification Section.
 - j. Drawing number and detail references, as appropriate.
 - k. Location(s) where product is to be installed, as appropriate.
 - l. Other necessary identification.
- F. Deviations: Highlight or otherwise specifically identify deviations from the Contract Documents on submittals.
- G. Additional Copies: Unless additional copies are required for final submittal, and unless Architect observes noncompliance with provisions in the Contract Documents, initial submittal may serve as final submittal.
 1. Submit one copy of submittal to concurrent reviewer in addition to specified number of copies to Architect.
 2. Additional copies submitted for maintenance manuals will be marked with action taken and will be returned.

SECTION 01 33 00
SUBMITTAL PROCEDURES

- H. Transmittal: Package each submittal individually and appropriately for transmittal and handling. Transmit each submittal using a transmittal form. Architect will return submittals received from sources other than Contractor.
1. Transmittal Form: Provide locations on form for the following information:
 - a. Project name.
 - b. Date.
 - c. Destination (To:).
 - d. Source (From:).
 - e. Names of subcontractor, manufacturer, and supplier.
 - f. Category and type of submittal.
 - g. Submittal purpose and description.
 - h. Specification Section number and title.
 - i. Drawing number and detail references, as appropriate.
 - j. Transmittal number numbered consecutively.
 - k. Submittal and transmittal distribution record.
 - l. Remarks.
 - m. Signature of transmitter.
 2. On an attached separate sheet, prepared on Contractor's letterhead, record relevant information, requests for data, revisions other than those requested by Architect on previous submittals, and deviations from requirements in the Contract Documents, including minor variations and limitations. Include same label information as related submittal.
- I. Resubmittals: Make resubmittals in same form and number of copies as initial submittal.
1. Note date and content of previous submittal.
 2. Note date and content of revision in label or title block and clearly indicate extent of revision.
 3. Resubmit submittals until they are marked "Approved as Noted".
- J. Distribution: Furnish copies of final submittals to manufacturers, subcontractors, suppliers, fabricators, installers, authorities having jurisdiction, and others as necessary for performance of construction activities. Show distribution on transmittal forms.
- K. Use for Construction: Use only final submittals with mark indicating "Approved as Noted" taken by Architect.

1.5 CONTRACTOR'S USE OF ARCHITECT'S CAD FILES

- A. General: At Contractor's written request, copies of Architect's CAD files will be provided to Contractor for Contractor's use in connection with Project, subject to the following conditions:
1. Release Form provided by Architect is signed by Contractor prior to CAD files being send.

PART 2 - PRODUCTS

2.1 ACTION SUBMITTALS

- A. General: Prepare and submit Action Submittals required by individual Specification Sections.

SECTION 01 33 00
SUBMITTAL PROCEDURES

- B. Product Data: Collect information into a single submittal for each element of construction and type of product or equipment.
1. If information must be specially prepared for submittal because standard printed data are not suitable for use, submit as Shop Drawings, not as Product Data.
 2. Mark each copy of each submittal to show which products and options are applicable.
 3. Include the following information, as applicable:
 - a. Manufacturer's written recommendations.
 - b. Manufacturer's product specifications.
 - c. Manufacturer's installation instructions.
 - d. Standard color charts.
 - e. Manufacturer's catalog cuts.
 - f. Wiring diagrams showing factory-installed wiring.
 - g. Printed performance curves.
 - h. Operational range diagrams.
 - i. Mill reports.
 - j. Standard product operation and maintenance manuals.
 - k. Compliance with specified referenced standards.
 - l. Testing by recognized testing agency.
 - m. Application of testing agency labels and seals.
 - n. Notation of coordination requirements.
 4. Submit Product Data before or concurrent with Samples.
 5. Number of Copies: Submit five copies of Product Data, unless otherwise indicated. Architect will return three copies. Mark up and retain one returned copy as a Project Record Document.
- C. Shop Drawings: Prepare Project-specific information, drawn accurately to scale. Do not base Shop Drawings on reproductions of the Contract Documents or standard printed data.
1. Preparation: Fully illustrate requirements in the Contract Documents. Include the following information, as applicable:
 - a. Dimensions.
 - b. Identification of products.
 - c. Fabrication and installation drawings.
 - d. Roughing-in and setting diagrams.
 - e. Wiring diagrams showing field-installed wiring, including power, signal, and control wiring.
 - f. Shopwork manufacturing instructions.
 - g. Templates and patterns.
 - h. Schedules.
 - i. Design calculations.
 - j. Compliance with specified standards.
 - k. Notation of coordination requirements.
 - l. Notation of dimensions established by field measurement.
 - m. Relationship to adjoining construction clearly indicated.
 - n. Seal and signature of professional engineer if specified.
 - o. Wiring Diagrams: Differentiate between manufacturer-installed and field-installed wiring.
 2. Sheet Size: Except for templates, patterns, and similar full-size drawings, submit Shop Drawings on sheets at least 8-1/2 by 11 inches (215 by 280 mm) but no larger than 30 by 40 inches (750 by 1000 mm).
 3. Number of Copies: Submit five opaque copies of each submittal, unless copies are required for operation and maintenance manuals. Submit five copies where copies are required for operation and maintenance manuals. Architect will retain two copies; remainder will be returned.

SECTION 01 33 00
SUBMITTAL PROCEDURES

- D. Samples: Submit Samples for review of kind, color, pattern, and texture for a check of these characteristics with other elements and for a comparison of these characteristics between submittal and actual component as delivered and installed.
1. Transmit Samples that contain multiple, related components such as accessories together in one submittal package.
 2. Identification: Attach label on unexposed side of Samples that includes the following:
 - a. Generic description of Sample.
 - b. Product name and name of manufacturer.
 - c. Sample source.
 - d. Number and title of appropriate Specification Section.
 3. Disposition: Maintain sets of approved Samples at Project site, available for quality-control comparisons throughout the course of construction activity. Sample sets may be used to determine final acceptance of construction associated with each set.
 - a. Samples that may be incorporated into the Work are indicated in individual Specification Sections. Such Samples must be in an undamaged condition at time of use.
 - b. Samples not incorporated into the Work, or otherwise designated as Owner's property, are the property of Contractor.
 4. Samples for Initial Selection: Submit manufacturer's color charts consisting of units or sections of units showing the full range of colors, textures, and patterns available.
 - a. Number of Samples: Submit two full set(s) of available choices where color, pattern, texture, or similar characteristics are required to be selected from manufacturer's product line. Architect will return submittal with options selected.
 5. Samples for Verification: Submit full-size units or Samples of size indicated, prepared from same material to be used for the Work, cured and finished in manner specified, and physically identical with material or product proposed for use, and that show full range of color and texture variations expected. Samples include, but are not limited to, the following: partial sections of manufactured or fabricated components; small cuts or containers of materials; complete units of repetitively used materials; swatches showing color, texture, and pattern; color range sets; and components used for independent testing and inspection.
 - a. Number of Samples: Submit three sets of Samples. Architect will retain two. Sample sets; remainder will be returned.
 - 1) Submit a single Sample where assembly details, workmanship, fabrication techniques, connections, operation, and other similar characteristics are to be demonstrated.
 - 2) If variation in color, pattern, texture, or other characteristic is inherent in material or product represented by a Sample, submit at least three sets of paired units that show approximate limits of variations.
- E. Product Schedule or List: As required in individual Specification Sections, prepare a written summary indicating types of products required for the Work and their intended location. Include the following information in tabular form:
1. Type of product. Include unique identifier for each product.
 2. Number and name of room or space.
 3. Location within room or space.
 4. Number of Copies: Submit three copies of product schedule or list, unless otherwise indicated. Architect will return two copies.

SECTION 01 33 00
SUBMITTAL PROCEDURES

- a. Mark up and retain one returned copy as a Project Record Document.
- F. Submittals Schedule: Comply with requirements specified in Division 01 Section "Construction Progress Documentation."
- G. Application for Payment: Comply with requirements specified in Division 01 Section "Payment Procedures."
- H. Schedule of Values: Comply with requirements specified in Division 01 Section "Payment Procedures."

2.2 INFORMATIONAL SUBMITTALS

- A. General: Prepare and submit Informational Submittals required by other Specification Sections.
 - 1. Number of Copies: Submit **two** copies of each submittal, unless otherwise indicated. Architect will not return copies.
 - 2. Certificates and Certifications: Provide a notarized statement that includes signature of entity responsible for preparing certification. Certificates and certifications shall be signed by an officer or other individual authorized to sign documents on behalf of that entity.
 - 3. Test and Inspection Reports: Comply with requirements specified in Division 01 Section "Quality Requirements."
- B. Coordination Drawings: Comply with requirements specified in Division 01 Section "Project Management and Coordination."
- C. Contractor's Construction Schedule: Comply with requirements specified in Division 01 Section "Construction Progress Documentation."
- D. Qualification Data: Prepare written information that demonstrates capabilities and experience of firm or person. Include lists of completed projects with project names and addresses, names and addresses of architects and owners, and other information specified.
- E. Installer Certificates: Prepare written statements on manufacturer's letterhead certifying that Installer complies with requirements in the Contract Documents and, where required, is authorized by manufacturer for this specific Project.
- F. Manufacturer Certificates: Prepare written statements on manufacturer's letterhead certifying that manufacturer complies with requirements in the Contract Documents. Include evidence of manufacturing experience where required.
- G. Product Certificates: Prepare written statements on manufacturer's letterhead certifying that product complies with requirements in the Contract Documents.
- H. Material Certificates: Prepare written statements on manufacturer's letterhead certifying that material complies with requirements in the Contract Documents.
- I. Material Test Reports: Prepare reports written by a qualified testing agency, on testing agency's standard form, indicating and interpreting test results of material for compliance with requirements in the Contract Documents.
- J. Product Test Reports: Prepare written reports indicating current product produced by manufacturer complies with requirements in the Contract Documents. Base reports on evaluation of tests performed by manufacturer and witnessed by a qualified testing agency, or on comprehensive tests performed by a qualified testing agency.

SECTION 01 33 00
SUBMITTAL PROCEDURES

- K. Research/Evaluation Reports: Prepare written evidence, from a model code organization acceptable to authorities having jurisdiction, that product complies with building code in effect for Project. Include the following information:
1. Name of evaluation organization.
 2. Date of evaluation.
 3. Time period when report is in effect.
 4. Product and manufacturers' names.
 5. Description of product.
 6. Test procedures and results.
 7. Limitations of use.
- L. Schedule of Tests and Inspections: Comply with requirements specified in Division 01 Section "Quality Requirements."
- M. Preconstruction Test Reports: Prepare reports written by a qualified testing agency, on testing agency's standard form, indicating and interpreting results of tests performed before installation of product, for compliance with performance requirements in the Contract Documents.
- N. Compatibility Test Reports: Prepare reports written by a qualified testing agency, on testing agency's standard form, indicating and interpreting results of compatibility tests performed before installation of product. Include written recommendations for primers and substrate preparation needed for adhesion.
- O. Field Test Reports: Prepare reports written by a qualified testing agency, on testing agency's standard form, indicating and interpreting results of field tests performed either during installation of product or after product is installed in its final location, for compliance with requirements in the Contract Documents.
- P. Maintenance Data: Prepare written and graphic instructions and procedures for operation and normal maintenance of products and equipment. Comply with requirements specified in Division 01 Section "Operation and Maintenance Data."
- Q. Design Data: Prepare written and graphic information, including, but not limited to, performance and design criteria, list of applicable codes and regulations, and calculations. Include list of assumptions and other performance and design criteria and a summary of loads. Include load diagrams if applicable. Provide name and version of software, if any, used for calculations. Include page numbers.
- R. Manufacturer's Instructions: Prepare written or published information that documents manufacturer's recommendations, guidelines, and procedures for installing or operating a product or equipment. Include name of product and name, address, and telephone number of manufacturer. Include the following, as applicable:
1. Preparation of substrates.
 2. Required substrate tolerances.
 3. Sequence of installation or erection.
 4. Required installation tolerances.
 5. Required adjustments.
 6. Recommendations for cleaning and protection.
- S. Manufacturer's Field Reports: Prepare written information documenting factory-authorized service representative's tests and inspections. Include the following, as applicable:
1. Name, address, and telephone number of factory-authorized service representative making report.
 2. Statement on condition of substrates and their acceptability for installation of product.
 3. Statement that products at Project site comply with requirements.

SECTION 01 33 00
SUBMITTAL PROCEDURES

4. Summary of installation procedures being followed, whether they comply with requirements and, if not, what corrective action was taken.
 5. Results of operational and other tests and a statement of whether observed performance complies with requirements.
 6. Statement whether conditions, products, and installation will affect warranty.
 7. Other required items indicated in individual Specification Sections.
- T. Insurance Certificates and Bonds: Prepare written information indicating current status of insurance or bonding coverage. Include name of entity covered by insurance or bond, limits of coverage, amounts of deductibles, if any, and term of the coverage.
- U. Material Safety Data Sheets (MSDSs): Submit information directly to Owner; do not submit to Architect.
1. Architect will not review submittals that include MSDSs and will return the entire submittal for resubmittal.

PART 3 - EXECUTION

3.1 CONTRACTOR'S REVIEW

- A. Review each submittal and check for coordination with other Work of the Contract and for compliance with the Contract Documents. Note corrections and field dimensions. Mark with approval stamp before submitting.
- B. Approval Stamp: Stamp each submittal with a uniform, approval stamp. Include Project name and location, submittal number, Specification Section title and number, name of reviewer, date of Contractor's approval, and statement certifying that submittal has been reviewed, checked, and approved for compliance with the Contract Documents.

3.2 ARCHITECT'S ACTION

- A. General: Architect will not review submittals that do not bear Contractor's approval stamp and will return them without action.
- B. Action Submittals: Architect will review each submittal, make marks to indicate corrections or modifications required, and return it. Architect will stamp each submittal with an action stamp and will mark stamp appropriately to indicate action taken, as follows:
 1. Architect may use a Submittal Response Form in lieu of stamping each submittal; a sample is included at the end of the Section
- C. Informational Submittals: Architect will review each submittal and will not return it, or will return it if it does not comply with requirements.
- D. Partial submittals are not acceptable, will be considered nonresponsive, and will be returned without review.
- E. Submittals not required by the Contract Documents may not be reviewed and may be discarded.

END OF SECTION 01 33 00



BARGMANN HENDRIE + ARCHETYPE, INC.

Architecture | Planning | Interior Design

300 A Street
Boston, MA 02210-1710

617 350 0450 tel
617 350 0215 fax

bha@bhplus.com
www.bhplus.com

submittal response form

date: October 27, 2015

project & number: 12 North Main Street Phase 1 Stabilization Project - # 3246.00

submittal no:

This submittal has been reviewed for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. This review has not been conducted for the purpose of determining the accuracy and completeness of other details such as dimensions and quantities or for substantiating instructions for installation or performances of equipment or systems designed by the Contractor, all of which remain the responsibility of the Contractor to the extent required by the Contract Documents. The Architect's review shall not constitute approval of safety precautions or, unless otherwise specifically stated by the Architect, of construction means, methods, techniques, sequences or procedures. The Architect's approval of a specific item shall not indicate approval of an assembly of which the item is a component. When professional certification of performance characteristics of materials, systems or equipment is required by the Contract Documents, the Architect shall be entitled to rely upon such certification to establish that the materials, systems or equipment will meet the performance criteria required by the Contract Documents.

action: Reviewed and approved, subject to the limitations noted above.

Reviewed and approved as noted, subject to the limitations noted above.

Revise and Resubmit

Disapproved

reviewed by: Jack Glassman AIA

comments:
1.
2.

SECTION 01 40 00
QUALITY REQUIREMENTS

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes administrative and procedural requirements for quality assurance and quality control.
- B. Testing and inspecting services may be required to verify compliance with requirements specified or indicated. These services do not relieve Contractor of responsibility for compliance with the Contract Document requirements.
 - 1. Specific quality-assurance and -control requirements for individual construction activities are specified in the Sections that specify those activities. Requirements in those Sections may also cover production of standard products.
 - 2. Specified tests, inspections, and related actions do not limit Contractor's other quality-assurance and -control procedures that facilitate compliance with the Contract Document requirements.
 - 3. Requirements for Contractor to provide quality-assurance and -control services required by Architect, Owner, or authorities having jurisdiction are not limited by provisions of this Section.
- C. Related Sections include the following:
 - 1. Division 01 Section "Construction Progress Documentation" for developing a schedule of required tests and inspections.
 - 2. Technical Sections for specific test and inspection requirements.

1.3 DEFINITIONS

- A. Quality-Assurance Services: Activities, actions, and procedures performed before and during execution of the Work to guard against defects and deficiencies and substantiate that proposed construction will comply with requirements.
- B. Quality-Control Services: Tests, inspections, procedures, and related actions during and after execution of the Work to evaluate that actual products incorporated into the Work and completed construction comply with requirements. Services do not include contract enforcement activities performed by Architect.
- C. Mockups: Full-size, physical assemblies that are constructed on-site. Mockups are used to verify selections made under sample submittals, to demonstrate aesthetic effects and, where indicated, qualities of materials and execution, and to review construction, coordination, testing, or operation; they are not Samples. Approved mockups establish the standard by which the Work will be judged.
- D. Product Testing: Tests and inspections that are performed by an NRTL, an NVLAP, or a testing agency qualified to conduct product testing and acceptable to authorities having jurisdiction, to establish product performance and compliance with industry standards.
- E. Source Quality-Control Testing: Tests and inspections that are performed at the source, i.e., plant, mill, factory, or shop.

SECTION 01 40 00
QUALITY REQUIREMENTS

- F. Field Quality-Control Testing: Tests and inspections that are performed on-site for installation of the Work and for completed Work.
- G. Testing Agency: An entity engaged to perform specific tests, inspections, or both. Testing laboratory shall mean the same as testing agency.
- H. Installer/Applicator/Erector: Contractor or another entity engaged by Contractor as an employee, Subcontractor, or Sub-subcontractor, to perform a particular construction operation, including installation, erection, application, and similar operations.
 - 1. Using a term such as "carpentry" does not imply that certain construction activities must be performed by accredited or unionized individuals of a corresponding generic name, such as "carpenter." It also does not imply that requirements specified apply exclusively to tradespeople of the corresponding generic name.
- I. Experienced: When used with an entity, "experienced" means having successfully completed a minimum of five previous projects similar in size and scope to this Project; being familiar with special requirements indicated; and having complied with requirements of authorities having jurisdiction.

1.4 CONFLICTING REQUIREMENTS

- A. General: If compliance with two or more standards is specified and the standards establish different or conflicting requirements for minimum quantities or quality levels, comply with the most stringent requirement. Refer uncertainties and requirements that are different, but apparently equal, to Architect for a decision before proceeding.
- B. Minimum Quantity or Quality Levels: The quantity or quality level shown or specified shall be the minimum provided or performed. The actual installation may comply exactly with the minimum quantity or quality specified, or it may exceed the minimum within reasonable limits. To comply with these requirements, indicated numeric values are minimum or maximum, as appropriate, for the context of requirements. Refer uncertainties to Architect for a decision before proceeding.

1.5 SUBMITTALS

- A. Qualification Data: For testing agencies specified in "Quality Assurance" Article to demonstrate their capabilities and experience. Include proof of qualifications in the form of a recent report on the inspection of the testing agency by a recognized authority.
- B. Schedule of Tests and Inspections (as applicable): Prepare in tabular form and include the following:
 - 1. Specification Section number and title.
 - 2. Description of test and inspection.
 - 3. Identification of applicable standards.
 - 4. Identification of test and inspection methods.
 - 5. Number of tests and inspections required.
 - 6. Time schedule or time span for tests and inspections.
 - 7. Entity responsible for performing tests and inspections.
 - 8. Requirements for obtaining samples.
 - 9. Unique characteristics of each quality-control service.
- C. Permits, Licenses, and Certificates: For Owner's records, submit copies of permits, licenses, certifications, inspection reports, releases, jurisdictional settlements, notices, receipts for fee payments, judgments,

SECTION 01 40 00
QUALITY REQUIREMENTS

correspondence, records, and similar documents, established for compliance with standards and regulations bearing on performance of the Work.

1.6 QUALITY ASSURANCE

- A. General: Qualifications paragraphs in this Article establish the minimum qualification levels required; individual Specification Sections specify additional requirements.
- B. Installer Qualifications: A firm or individual experienced in installing, erecting, or assembling work similar in material, design, and extent to that indicated for this Project, whose work has resulted in construction with a record of successful in-service performance.
- C. Manufacturer Qualifications: A firm experienced in manufacturing products or systems similar to those indicated for this Project and with a record of successful in-service performance, as well as sufficient production capacity to produce required units.
- D. Fabricator Qualifications: A firm experienced in producing products similar to those indicated for this Project and with a record of successful in-service performance, as well as sufficient production capacity to produce required units.
- E. Professional Engineer Qualifications: A professional engineer who is legally qualified to practice in jurisdiction where Project is located and who is experienced in providing engineering services of the kind indicated. Engineering services are defined as those performed for installations of the system, assembly, or product that are similar to those indicated for this Project in material, design, and extent.
- F. Specialists: Certain sections of the Specifications require that specific construction activities shall be performed by entities who are recognized experts in those operations. Specialists shall satisfy qualification requirements indicated and shall be engaged for the activities indicated.
 - 1. Requirement for specialists shall not supersede building codes and regulations governing the Work.
- G. Testing Agency Qualifications: An NRTL, an NVLAP, or an independent agency with the experience and capability to conduct testing and inspecting indicated, as documented according to ASTM E 548; and with additional qualifications specified in individual Sections; and where required by authorities having jurisdiction, that is acceptable to authorities.
 - 1. NRTL: A nationally recognized testing laboratory according to 29 CFR 1910.7.
 - 2. NVLAP: A testing agency accredited according to NIST's National Voluntary Laboratory Accreditation Program.
 - 3. Testing Agency Responsibilities: Submit a certified written report of each test, inspection, and similar quality-assurance service to Architect, with copy to Contractor. Interpret tests and inspections and state in each report whether tested and inspected work complies with or deviates from the Contract Documents.
- H. Mockups: Before installing portions of the Work requiring mockups, build mockups for each form of construction and finish required to comply with the following requirements, using materials indicated for the completed Work:
 - 1. Build mockups in location and of size indicated or, if not indicated, as directed by Architect.
 - 2. Notify Architect seven days in advance of dates and times when mockups will be constructed.
 - 3. Demonstrate the proposed range of aesthetic effects and workmanship.
 - 4. Obtain Architect's approval of mockups before starting work, fabrication, or construction.
 - a. Allow seven days for initial review and each re-review of each mockup.

SECTION 01 40 00
QUALITY REQUIREMENTS

5. Maintain mockups during construction in an undisturbed condition as a standard for judging the completed Work.
6. Demolish and remove mockups when directed, unless otherwise indicated.

1.7 QUALITY CONTROL

- A. Tests and inspections not explicitly assigned to Owner are Contractor's responsibility. Unless otherwise indicated, provide quality-control services specified and those required by authorities having jurisdiction. Perform quality-control services required of Contractor by authorities having jurisdiction, whether specified or not.
 1. Where services are indicated as Contractor's responsibility, engage a qualified testing agency to perform these quality-control services.
 - a. Contractor shall not employ same entity engaged by Owner, unless agreed to in writing by Owner.
 2. Notify testing agencies at least 24 hours in advance of time when Work that requires testing or inspecting will be performed.
 3. Where quality-control services are indicated as Contractor's responsibility, submit a certified written report, in duplicate, of each quality-control service.
 4. Testing and inspecting requested by Contractor and not required by the Contract Documents are Contractor's responsibility.
 5. Submit additional copies of each written report directly to authorities having jurisdiction, when they so direct.
- B. Coordination: Coordinate sequence of activities to accommodate required quality-assurance and -control services with a minimum of delay and to avoid necessity of removing and replacing construction to accommodate testing and inspecting.
 1. Schedule times for tests, inspections, obtaining samples, and similar activities.

1.8 SPECIAL TESTS AND INSPECTIONS

- A. Special Tests and Inspections: Conducted by a qualified testing agency as required by authorities having jurisdiction, as indicated in individual Specification Sections, and as follows:
 1. Verifying that manufacturer maintains detailed fabrication and quality-control procedures and reviewing the completeness and adequacy of those procedures to perform the Work.
 2. Notifying Architect and Contractor promptly of irregularities and deficiencies observed in the Work during performance of its services.
 3. Submitting a certified written report of each test, inspection, and similar quality-control service to Architect with copy to Contractor and to authorities having jurisdiction.
 4. Submitting a final report of special tests and inspections at Substantial Completion, which includes a list of unresolved deficiencies.
 5. Interpreting tests and inspections and stating in each report whether tested and inspected work complies with or deviates from the Contract Documents.
 6. Retesting and reinspecting corrected work.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION

3.1 TEST AND INSPECTION LOG

- A. Prepare a record of tests and inspections. Maintain log at Project site.

3.2 REPAIR AND PROTECTION

- A. General: On completion of testing, inspecting, sample taking, and similar services, repair damaged construction and restore substrates and finishes.
 - 1. Provide materials and comply with installation requirements specified in other Specification Sections. Restore patched areas and extend restoration into adjoining areas with durable seams that are as invisible as possible.
- B. Protect construction exposed by or for quality-control service activities.
- C. Repair and protection are Contractor's responsibility, regardless of the assignment of responsibility for quality-control services.

END OF SECTION 01 40 00

SECTION 01 50 00
TEMPORARY FACILITIES AND CONTROLS

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes:
 - 1. Requirements for temporary protective walkways, temporary utilities, support facilities, and security and protection facilities.
 - 2. Requirements for protective measures to remain on site following completion of work, including without limitation, Alternate No. 3 plastic tarpaulins ("tarps") and associated rough carpentry.
- B. Related Sections include the following:
 - 1. Division 01 Section "Summary" for limitations on utility interruptions and other work restrictions.
 - 2. Division 01 Section "Submittal Procedures" for procedures for submitting copies of implementation and termination schedule and utility reports.
 - 3. Division 02 44 00 "Temporary Shoring" for timber shoring solutions and for smokestack masonry stabilization.
 - 4. Division 06 10 00 "Rough Carpentry" for plank walkway assemblies, door/window boarding and Alternate No. 3 protective tarp armature.

1.3 DEFINITIONS

- A. Permanent Enclosure: As determined by Architect, permanent or temporary roofing is complete, insulated, and weathertight; exterior walls are insulated and weathertight; and all openings are closed with permanent construction or substantial temporary closures.

1.4 USE CHARGES

- A. General: Cost or use charges for temporary facilities shall be included in the Contract Sum.
- B. Water Service: No water service is available on site.
- C. Electric Service: Provide electric power service of sufficient size, capacity and power characteristics required for construction operations. Contractor is responsible for disconnecting the temporary service upon completion of the project.

1.5 SUBMITTALS

- A. Protection and Safety Plan: Submit drawings and written description of temporary protective walkways and other physical and operational protection measures intended to protect building occupants and visitors and passersby from harm associated with construction activities.

SECTION 01 50 00
TEMPORARY FACILITIES AND CONTROLS

- B. Site Plan: Show temporary facilities, utility hookups, staging areas, and parking areas for construction personnel.
- C. Alternate No. 3 Plastic Tarpaulins ("Tarps") at Bell Tower Roofs: Submit product literature for proposed tarp product(s) and for associated rope materials.

1.6 QUALITY ASSURANCE

- A. Electric Service: Comply with NECA, NEMA, and UL standards and regulations for temporary electric service. Install service to comply with NFPA 70.
- B. Tests and Inspections: Arrange for authorities having jurisdiction to test and inspect each temporary utility before use. Obtain required certifications and permits.

PART 2 - PRODUCTS

2.1 MATERIALS

- A. Existing Portable Chain-Link Fencing: Retain existing chain-link fencing, adjusting location as needed for operations. Reset fencing in original location and configuration at Closeout.
- B. Lumber and Plywood: Comply with requirements in Division 06 Section "Rough Carpentry."

2.2 TEMPORARY FACILITIES

- A. Field Offices, General: Contractor shall provide adequately furnished prefabricated or mobile unit with serviceable finishes, temperature controls and foundations adequate for normal loading. At contractor's discretion, an existing room in the north wing of 12 North Main Street may be provided with temporary power and repurposed for use as a field office.
- B. Common-Use Field Office: Of sufficient size to accommodate needs of construction personnel. Keep office clean and orderly. Furnish and equip offices as follows:
 - 1. Furniture required for Project-site documents including a file cabinet, plan table and bookcase.
 - 2. Drinking water.
 - 3. Coffee machine and supplies.
 - 4. Lighting fixture(s) capable of maintaining average illumination of 20 fc (215 lx) at desk height.
- C. Storage and Fabrication Sheds/Containers: If needed, provide secure sheds or containers sized, furnished and equipped to accommodate materials and equipment for construction operations, in location pre-approved by the Town.

2.3 TEMPORARY STAGING AND SCAFFOLDING

- A. The General Contractor shall furnish, erect, and maintain in safe condition all exterior and interior staging and scaffolding required for his/her own use.

SECTION 01 50 00
TEMPORARY FACILITIES AND CONTROLS

2.4 PROTECTIVE WALKWAYS

- A. Design, engineer, furnish and install the following temporary access aids that will remain on site following completion of the work:
1. Wood-plank and/or framed access "bridges across rotted floor sections (basement level).
 2. Braced 2x4 handrails/guards at sides of access "bridges" and/or posts connected with nylon ropes.

2.5 ALTERNATE NO. 3: TARPS AT BELL TOWER ROOFS

1. Provide water-resistant, UV-resistant, tear-resistant, flame-resistant polyethylene tarpaulins ("tarps") secured to bell tower roof above belfry and to lower roof surrounding belfry, as indicated on Drawing A200. Protect existing iron cresting by constructing a wood-framed, plywood capped box (covered in Division 06 10 00 Rough Carpentry.).
2. Equal in quality to manufactured tarp products supplied by Grainger, Everbilt or TarpsPlus.
3. Provide corrosion-resistant aluminum or brass grommets at perimeter, minimum spacing 36".
4. Provide ¼" braided nylon or polypropylene rope, of test strength to fully secure tarps to existing bell tower.
5. Minimum Performance Requirements:
 - a. Water-resistant.
 - b. Mildew-resistant.
 - c. Ultraviolet (UV) sun-resistant.
 - d. Tear-resistant and/or reinforced polyethylene fabric, minimum thickness 5 mils.
 - e. Flame-resistant or fire-retardant, to meet minimum California State Fire Marshal guidelines and NFPA 701 standards.
 - f. Heat-sealed seams; reinforced hems.
 - g. Color: Blue or White.

PART 3 - EXECUTION

3.1 INSTALLATION, GENERAL

- A. Maintain emergency egress pathways at all times or, subject to prior approval by the Town, provide fully-compliant alternative pathways as the Work progresses.
- B. Locate facilities where they will serve Project adequately and result in minimum interference with performance of the Work. Relocate and modify facilities as required by progress of the Work.

3.2 TEMPORARY UTILITY INSTALLATION

- A. General: Install temporary service or connect to existing service.
1. Arrange with utility company, Owner, and existing users for time when service can be interrupted, if necessary, to make connections for temporary services.
- B. Sanitary Facilities: Provide temporary toilets, wash facilities and drinking water for use by construction personnel. Comply with authorities having jurisdiction for type, number, location, operation and maintenance of fixtures and facilities.

SECTION 01 50 00
TEMPORARY FACILITIES AND CONTROLS

- C. Electric Power Service: Provide electric power service of sufficient size, capacity and power characteristics required for construction operations. Contractor is responsible for disconnecting the temporary service upon completion of the project.
- D. Lighting: Provide temporary lighting with local switching that provides adequate illumination for construction operations, observations, inspections and traffic conditions.
- E. Telephone Service: Provide superintendent with cellular telephone.

3.3 SUPPORT FACILITIES INSTALLATION

- A. General: Comply with the following:
 - 1. Provide incombustible construction for offices, shops, and sheds located within construction area or within 30 feet (9 m) of building lines. Comply with NFPA 241.
 - 2. Maintain support facilities until near Substantial Completion. Remove before Substantial Completion. Personnel remaining after Substantial Completion will be permitted to use permanent facilities, under conditions acceptable to Owner.
- B. Traffic Controls: Comply with requirements of authorities having jurisdiction.
 - 1. Protect existing site improvements to remain including curbs, pavement, and utilities.
 - 2. Maintain access for fire-fighting equipment and access to fire hydrants.
- C. Parking: Construction personnel shall park only in areas designated by Owner during preconstruction meeting, or as later amended by Owner.
- D. Project Identification and Temporary Signs: Provide Project identification sign. Install sign where indicated to inform public and individuals seeking entrance to Project. Unauthorized signs are not permitted.
 - 1. Maintain and touchup signs so they remains legible at all times.

3.4 SECURITY AND PROTECTION FACILITIES INSTALLATION

- A. Environmental Protection: Provide protection, operate temporary facilities, and conduct construction in ways and by methods that comply with environmental regulations and that minimize possible air, waterway, and subsoil contamination or pollution or other undesirable effects.
 - 1. Comply with work restrictions specified in Division 01 Section "Summary."
- B. Barricades, Warning Signs, and Lights: Comply with requirements of authorities having jurisdiction for erecting structurally adequate barricades, including warning signs and lighting.
- C. Temporary Enclosures: Maintain existing temporary enclosures for protection of construction, in progress and completed.

SECTION 01 50 00
TEMPORARY FACILITIES AND CONTROLS

3.5 PROTECTIVE WALKWAY INSTALLATION

- A. Erect all rough carpentry work plumb, level, and true with tight, close fitting joints, securely attached and braced to surrounding construction, all in a first-class, workmanlike manner. Bear complete responsibility for structural integrity, connections, and anchorage of all rough carpentry work.
- B. Install blocking, grounds and furring, as required for proper attachment of the work.

3.6 ALTERNATE NO. 3: INSTALLATION OF TARPS AT BELL TOWER ROOFS

- A. Drawing A200 illustrates a suggested fastening methodology and protective armature for iron cresting. Contractor shall be responsible for all means and methods of access and construction employed in installation of tarps and a durable armature.
- B. Using braided rope and additional hardware as needed, secure tarps to upper and lower roofs of bell tower roof and cornices, in order to minimize water infiltration. Do not cover belfry "interior" floor or ceiling.

3.7 OPERATION, TERMINATION, AND REMOVAL

- A. Supervision: Enforce strict discipline in use of temporary facilities. To minimize waste and abuse, limit availability of temporary facilities to essential and intended uses.
- B. Maintenance: Maintain facilities in good operating condition until removal.
- C. Operate Project-identification-sign lighting daily from dusk until 12:00 midnight.
- D. Retain protective measures intended to remain in place, e.g. walkways, Alternate No. 3 tarps.
- E. Termination and Removal: Remove each temporary facility when need for its service has ended, or no later than Substantial Completion.
 - 1. Materials and facilities that constitute temporary facilities are property of Contractor. Owner reserves right to take possession of Project identification signs.
 - 2. At Substantial Completion, clean and renovate permanent facilities used during construction period. Comply with final cleaning requirements specified in Division 01 Section "Closeout Procedures."

END OF SECTION 01 50 00

SECTION 01 60 00
PRODUCT REQUIREMENTS

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes administrative and procedural requirements for selection of products for use in Project; product delivery, storage, and handling; manufacturers' standard warranties on products; special warranties; product substitutions; and comparable products.
- B. Related Sections include the following:
 - 1. Division 01 Section "Closeout Procedures" for submitting warranties for Contract closeout.
 - 2. Technical Sections for specific requirements for warranties on products and installations specified to be warranted.

1.3 DEFINITIONS

- A. Products: Items purchased for incorporating into the Work, whether purchased for Project or taken from previously purchased stock. The term "product" includes the terms "material," "equipment," "system," and terms of similar intent.
 - 1. Named Products: Items identified by manufacturer's product name, including make or model number or other designation shown or listed in manufacturer's published product literature that is current as of date of the Contract Documents.
 - 2. New Products: Items that have not previously been incorporated into another project or facility. Products salvaged or recycled from other projects are not considered new products.
 - 3. Comparable Product: Product that is demonstrated and approved through submittal process, or where indicated as a product substitution, to have the indicated qualities related to type, function, dimension, in-service performance, physical properties, appearance, and other characteristics that equal or exceed those of specified product.
- B. Substitutions: Changes in products, materials, equipment, and methods of construction from those required by the Contract Documents and proposed by Contractor.
- C. Basis-of-Design Product Specification: Where a specific manufacturer's product is named and accompanied by the words "basis of design," including make or model number or other designation, to establish the significant qualities related to type, function, dimension, in-service performance, physical properties, appearance, and other characteristics for purposes of evaluating comparable products of other named manufacturers.

1.4 SUBMITTALS

- A. Product List: Submit a list, in tabular form, showing specified products. Include generic names of products required. Include manufacturer's name and proprietary product names for each product.

SECTION 01 60 00
PRODUCT REQUIREMENTS

1. Coordinate product list with Contractor's Construction Schedule and the Submittals Schedule.
 2. Form: Tabulate information for each product under the following column headings:
 - a. Specification Section number and title.
 - b. Generic name used in the Contract Documents.
 - c. Proprietary name, model number, and similar designations.
 - d. Manufacturer's name and address.
 - e. Supplier's name and address.
 - f. Installer's name and address.
 - g. Projected delivery date or time span of delivery period.
 - h. Identification of items that require early submittal approval for scheduled delivery date.
 3. Initial Submittal: Within 15 days after date of commencement of the Work, submit 4 copies of initial product list. Include a written explanation for omissions of data and for variations from Contract requirements.
 4. Completed List: Within 30 days after date of commencement of the Work, submit 4 copies of completed product list. Include a written explanation for omissions of data and for variations from Contract requirements.
 5. Architect's Action: Architect will respond in writing to Contractor within 15 days of receipt of completed product list. Architect's response will include a list of unacceptable product selections and a brief explanation of reasons for this action. Architect's response, or lack of response, does not constitute a waiver of requirement to comply with the Contract Documents.
- B. Substitution Requests: Submit three copies of each request for consideration. Identify product or fabrication or installation method to be replaced. Include Specification Section number and title and Drawing numbers and titles.
1. Substitution Request Form: Use CSI Form 13.1A or similar form acceptable to the Architect.
 2. Documentation: Show compliance with requirements for substitutions and the following, as applicable:
 - a. Statement indicating why specified material or product cannot be provided.
 - b. Coordination information, including a list of changes or modifications needed to other parts of the Work and to construction performed by Owner and separate contractors that will be necessary to accommodate proposed substitution.
 - c. Detailed comparison of significant qualities of proposed substitution with those of the Work specified. Significant qualities may include attributes such as performance, weight, size, durability, visual effect, and specific features and requirements indicated.
 - d. Product Data, including drawings and descriptions of products and fabrication and installation procedures.
 - e. Samples, where applicable or requested.
 - f. List of similar installations for completed projects with project names and addresses and names and addresses of architects and owners.
 - g. Material test reports from a qualified testing agency indicating and interpreting test results for compliance with requirements indicated.
 - h. Research/evaluation reports evidencing compliance with building code in effect for Project, from a model code organization acceptable to authorities having jurisdiction.
 - i. Detailed comparison of Contractor's Construction Schedule using proposed substitution with products specified for the Work, including effect on the overall Contract Time. If specified product or method of construction cannot be provided within the Contract Time, include letter from manufacturer, on manufacturer's letterhead, stating lack of availability or delays in delivery.
 - j. Cost information, including a proposal of change, if any, in the Contract Sum.
 - k. Contractor's certification that proposed substitution complies with requirements in the Contract Documents and is appropriate for applications indicated.

SECTION 01 60 00
PRODUCT REQUIREMENTS

- I. Contractor's waiver of rights to additional payment or time that may subsequently become necessary because of failure of proposed substitution to produce indicated results.
3. Architect's Action: If necessary, Architect will request additional information or documentation for evaluation within 7 days of receipt of a request for substitution. Architect will notify Contractor of acceptance or rejection of proposed substitution within 15 days of receipt of request, or 7 days of receipt of additional information or documentation, whichever is later.
 - a. Form of Acceptance: Change Order.
 - b. Use product specified if Architect cannot make a decision on use of a proposed substitution within time allocated.
- C. Comparable Product Requests: Submit three copies of each request for consideration. Identify product or fabrication or installation method to be replaced. Include Specification Section number and title and Drawing numbers and titles.
 1. Architect's Action: If necessary, Architect will request additional information or documentation for evaluation within one week of receipt of a comparable product request. Architect will notify Contractor of approval or rejection of proposed comparable product request within 15 days of receipt of request, or 7 days of receipt of additional information or documentation, whichever is later.
 - a. Form of Approval: As specified in Division 01 Section "Submittal Procedures."
 - b. Use product specified if Architect cannot make a decision on use of a comparable product request within time allocated.
- D. Basis-of-Design Product Specification Submittal: Comply with requirements in Division 01 Section "Submittal Procedures." Show compliance with requirements.

1.5 QUALITY ASSURANCE

- A. Compatibility of Options: If Contractor is given option of selecting between two or more products for use on Project, product selected shall be compatible with products previously selected, even if previously selected products were also options.

1.6 PRODUCT DELIVERY, STORAGE, AND HANDLING

- A. Deliver, store, and handle products using means and methods that will prevent damage, deterioration, and loss, including theft. Comply with manufacturer's written instructions.
- B. Delivery and Handling:
 1. Schedule delivery to minimize long-term storage at Project site and to prevent overcrowding of construction spaces.
 2. Coordinate delivery with installation time to ensure minimum holding time for items that are flammable, hazardous, easily damaged, or sensitive to deterioration, theft, and other losses.
 3. Deliver products to Project site in an undamaged condition in manufacturer's original sealed container or other packaging system, complete with labels and instructions for handling, storing, unpacking, protecting, and installing.
 4. Inspect products on delivery to ensure compliance with the Contract Documents and to ensure that products are undamaged and properly protected.

SECTION 01 60 00
PRODUCT REQUIREMENTS

C. Storage:

1. Store products to allow for inspection and measurement of quantity or counting of units.
2. Store materials in a manner that will not endanger Project structure.
3. Store products that are subject to damage by the elements, under cover in a weathertight enclosure above ground, with ventilation adequate to prevent condensation.
4. Store cementitious products and materials on elevated platforms.
5. Store foam plastic from exposure to sunlight, except to extent necessary for period of installation and concealment.
6. Comply with product manufacturer's written instructions for temperature, humidity, ventilation, and weather-protection requirements for storage.
7. Protect stored products from damage and liquids from freezing.

1.7 PRODUCT WARRANTIES

- A. Warranties specified in other Sections shall be in addition to, and run concurrent with, other warranties required by the Contract Documents. Manufacturer's disclaimers and limitations on product warranties do not relieve Contractor of obligations under requirements of the Contract Documents.
1. **Manufacturer's Warranty:** Preprinted written warranty published by individual manufacturer for a particular product and specifically endorsed by manufacturer to Owner.
 2. **Special Warranty:** Written warranty required by or incorporated into the Contract Documents, either to extend time limit provided by manufacturer's warranty or to provide more rights for Owner.
- B. **Special Warranties:** Prepare a written document that contains appropriate terms and identification, ready for execution. Submit a draft for approval before final execution.
1. **Manufacturer's Standard Form:** Modified to include Project-specific information and properly executed.
 2. **Specified Form:** When specified forms are included with the Specifications, prepare a written document using appropriate form properly executed.
 3. Refer to Divisions 02 through 49 Sections for specific content requirements and particular requirements for submitting special warranties.
- C. **Submittal Time:** Comply with requirements in Division 01 Section "Closeout Procedures."

PART 2 - PRODUCTS

2.1 PRODUCT SELECTION PROCEDURES

- A. **General Product Requirements:** Provide products that comply with the Contract Documents, that are undamaged and, unless otherwise indicated, that are new at time of installation.
1. Provide products complete with accessories, trim, finish, fasteners, and other items needed for a complete installation and indicated use and effect.
 2. **Standard Products:** If available, and unless custom products or nonstandard options are specified, provide standard products of types that have been produced and used successfully in similar situations on other projects.
 3. Owner reserves the right to limit selection to products with warranties not in conflict with requirements of the Contract Documents.
 4. Where products are accompanied by the term "as selected," Architect will make selection.

SECTION 01 60 00
PRODUCT REQUIREMENTS

5. Where products are accompanied by the term "match sample," sample to be matched is Architect's.
6. Descriptive, performance, and reference standard requirements in the Specifications establish "salient characteristics" of products.
7. Or Equal: Where products are specified by name and accompanied by the term "or equal" or "or approved equal" or "or approved," comply with provisions in Part 2 "Comparable Products" Article to obtain approval for use of an unnamed product.

B. Product Selection Procedures:

1. Product: Where Specifications name a single product and manufacturer, provide the named product that complies with requirements.
2. Manufacturer/Source: Where Specifications name a single manufacturer or source, provide a product by the named manufacturer or source that complies with requirements.
3. Products: Where Specifications include a list of names of both products and manufacturers, provide one of the products listed that complies with requirements.
4. Manufacturers: Where Specifications include a list of manufacturers' names, provide a product by one of the manufacturers listed that complies with requirements.
5. Product Options: Where Specifications indicate that sizes, profiles, and dimensional requirements on Drawings are based on a specific product or system, provide the specified product or system. Comply with provisions in Part 2 "Product Substitutions" Article for consideration of an unnamed product or system.
6. Basis-of-Design Product: Where Specifications name a product and include a list of manufacturers, provide the specified product or a comparable product by one of the other named manufacturers. Drawings and Specifications indicate sizes, profiles, dimensions, and other characteristics that are based on the product named. Comply with provisions in Part 2 "Comparable Products" Article for consideration of an unnamed product by the other named manufacturers.
7. Visual Matching Specification: Where Specifications require matching an established Sample, select a product that complies with requirements and matches Architect's sample. Architect's decision will be final on whether a proposed product matches.
 - a. If no product available within specified category matches and complies with other specified requirements, comply with provisions in Part 2 "Product Substitutions" Article for proposal of product.
8. Visual Selection Specification: Where Specifications include the phrase "as selected from manufacturer's colors, patterns, textures" or a similar phrase, select a product that complies with other specified requirements.
 - a. Standard Range: Where Specifications include the phrase "standard range of colors, patterns, textures" or similar phrase, Architect will select color, pattern, density, or texture from manufacturer's product line that does not include premium items.
 - b. Full Range: Where Specifications include the phrase "full range of colors, patterns, textures" or similar phrase, Architect will select color, pattern, density, or texture from manufacturer's product line that includes both standard and premium items.

2.2 PRODUCT SUBSTITUTIONS

- A. Timing: Architect will consider requests for substitution if received within 60 days after commencement of the Work. Requests received after that time may be considered or rejected at discretion of Architect.
- B. Conditions: Architect will consider Contractor's request for substitution when the following conditions are satisfied. If the following conditions are not satisfied, Architect will return requests without action, except to record noncompliance with these requirements:

SECTION 01 60 00
PRODUCT REQUIREMENTS

1. Requested substitution offers Owner a substantial advantage in cost, time, energy conservation, or other considerations, after deducting additional responsibilities Owner must assume. Owner's additional responsibilities may include compensation to Architect for redesign and evaluation services, increased cost of other construction by Owner, and similar considerations.
2. Requested substitution does not require extensive revisions to the Contract Documents.
3. Requested substitution is consistent with the Contract Documents and will produce indicated results.
4. Substitution request is fully documented and properly submitted.
5. Requested substitution will not adversely affect Contractor's Construction Schedule.
6. Requested substitution has received necessary approvals of authorities having jurisdiction.
7. Requested substitution is compatible with other portions of the Work.
8. Requested substitution has been coordinated with other portions of the Work.
9. Requested substitution provides specified warranty.
10. If requested substitution involves more than one contractor, requested substitution has been coordinated with other portions of the Work, is uniform and consistent, is compatible with other products, and is acceptable to all contractors involved.

2.3 COMPARABLE PRODUCTS

- A. Conditions: Architect will consider Contractor's request for comparable product when the following conditions are satisfied. If the following conditions are not satisfied, Architect will return requests without action, except to record noncompliance with these requirements:
1. Evidence that the proposed product does not require extensive revisions to the Contract Documents, that it is consistent with the Contract Documents and will produce the indicated results, and that it is compatible with other portions of the Work.
 2. Detailed comparison of significant qualities of proposed product with those named in the Specifications. Significant qualities include attributes such as performance, weight, size, durability, visual effect, and specific features and requirements indicated.
 3. Evidence that proposed product provides specified warranty.
 4. List of similar installations for completed projects with project names and addresses and names and addresses of architects and owners, if requested.
 5. Samples, if requested.

PART 3 - EXECUTION (Not Used)

END OF SECTION 01 60 00

SECTION 01 70 00
EXECUTION REQUIREMENTS

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes general procedural requirements governing execution of the Work including, but not limited to, the following:
 - 1. Construction layout.
 - 2. General installation of products.
 - 3. Progress cleaning.
 - 4. Starting and adjusting.
 - 5. Protection of installed construction.
 - 6. Correction of the Work.
- B. Related Sections include the following:
 - 1. Division 01 Section "Project Management and Coordination" for procedures for coordinating field engineering with other construction activities.
 - 2. Division 01 Section "Cutting and Patching" for procedural requirements for cutting and patching necessary for the installation or performance of other components of the Work.
 - 3. Division 01 Section "Closeout Procedures" for submitting recording of Owner-accepted deviations from indicated lines and levels, and final cleaning.
 - 4. Abatement Work Plan for Alternate No. 1 abatement of designated hazardous building materials.

1.3 SUBMITTALS

- A. Landfill Receipts: Submit copy of receipts issued by a landfill facility, licensed to accept hazardous materials, for hazardous waste disposal.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION

3.1 EXAMINATION

- A. Existing Conditions: The existence and location of site improvements, utilities, and other construction indicated as existing are not guaranteed. Before beginning work, investigate and verify the existence and location of mechanical and electrical systems and other construction affecting the Work.
 - 1. Before construction, verify the location and points of connection of utility services.

SECTION 01 70 00
EXECUTION REQUIREMENTS

- B. Acceptance of Conditions: Examine substrates, areas, and conditions, with Installer or Applicator present where indicated, for compliance with requirements for installation tolerances and other conditions affecting performance. Record observations.
 - 1. Written Report: Where a written report listing conditions detrimental to performance of the Work is required by other Sections, include the following:
 - a. Description of the Work.
 - b. List of detrimental conditions, including substrates.
 - c. List of unacceptable installation tolerances.
 - d. Recommended corrections.
 - 2. Verify compatibility with and suitability of substrates, including compatibility with existing finishes or primers.
 - 3. Examine walls, floors, and roofs for suitable conditions where products and systems are to be installed.
 - 4. Proceed with installation only after unsatisfactory conditions have been corrected. Proceeding with the Work indicates acceptance of surfaces and conditions.

3.2 PREPARATION

- A. Existing Utility Information: Furnish information to Owner that is necessary to adjust, move, or relocate existing utility structures, utility poles, lines, services, or other utility appurtenances located in or affected by construction. Coordinate with authorities having jurisdiction.
- B. Field Measurements: Take field measurements as required to fit the Work properly. Recheck measurements before installing each product. Where portions of the Work are indicated to fit to other construction, verify dimensions of other construction by field measurements before fabrication. Coordinate fabrication schedule with construction progress to avoid delaying the Work.
- C. Space Requirements: Verify space requirements and dimensions of items shown diagrammatically on Drawings.
- D. Review of Contract Documents and Field Conditions: Immediately on discovery of the need for clarification of the Contract Documents, submit a request for information to Architect. Include a detailed description of problem encountered, together with recommendations for changing the Contract Documents. Submit requests on CSI Form 13.2A, "Request for Interpretation."

3.3 CONSTRUCTION LAYOUT

- A. Verification: Before proceeding to lay out the Work, verify layout information shown on Drawings, in relation to existing benchmarks. If discrepancies are discovered, notify Architect promptly.

3.4 INSTALLATION

- A. General: Locate the Work and components of the Work accurately, in correct alignment and elevation, as indicated.
 - 1. Make vertical work plumb and make horizontal work level.
 - 2. Where space is limited, install components to maximize space available for maintenance and ease of removal for replacement.
- B. Comply with manufacturer's written instructions and recommendations for installing products in applications indicated.

SECTION 01 70 00
EXECUTION REQUIREMENTS

- C. Install products at the time and under conditions that will ensure the best possible results. Maintain conditions required for product performance until Substantial Completion.
- D. Conduct construction operations so no part of the Work is subjected to damaging operations or loading in excess of that expected during normal conditions of occupancy.
- E. Tools and Equipment: Do not use tools or equipment that produces harmful noise levels.
- F. Templates: Obtain and distribute to the parties involved templates for work specified to be factory prepared and field installed. Check Shop Drawings of other work to confirm that adequate provisions are made for locating and installing products to comply with indicated requirements.
- G. Anchors and Fasteners: Provide anchors and fasteners as required to anchor each component securely in place, accurately located and aligned with other portions of the Work.
 - 1. Mounting Heights: Where mounting heights are not indicated, mount components at heights directed by Architect.
 - 2. Allow for building movement, including thermal expansion and contraction.
 - 3. Coordinate installation of anchorages. Furnish setting drawings, templates, and directions for installing anchorages, including sleeves, concrete inserts, anchor bolts, and items with integral anchors, that are to be embedded in concrete or masonry. Deliver such items to Project site in time for installation.
- H. Joints: Make joints of uniform width. Where joint locations in exposed work are not indicated, arrange joints for the best visual effect. Fit exposed connections together to form hairline joints.
- I. Hazardous Materials: Use products, cleaners, and installation materials that are not considered hazardous.

3.5 PROGRESS CLEANING

- A. Site: Maintain Project site free of waste materials and debris.
- B. Work Areas: Clean areas where work is in progress to the level of cleanliness necessary for proper execution of the Work.
 - 1. Remove liquid spills promptly.
- C. Installed Work: Keep installed work clean. Clean installed surfaces according to written instructions of manufacturer or fabricator of product installed, using only cleaning materials specifically recommended. If specific cleaning materials are not recommended, use cleaning materials that are not hazardous to health or property and that will not damage exposed surfaces.
- D. Waste Disposal: Burying or burning waste materials on-site will not be permitted. Washing waste materials down sewers or into waterways will not be permitted.
- E. During handling and installation, clean and protect construction in progress and adjoining materials already in place. Apply protective covering where required to ensure protection from damage or deterioration at Substantial Completion.
- F. Clean and provide maintenance on completed construction as frequently as necessary through the remainder of the construction period. Adjust and lubricate operable components to ensure operability without damaging effects.

SECTION 01 70 00
EXECUTION REQUIREMENTS

- G. Limiting Exposures: Supervise construction operations to assure that no part of the construction, completed or in progress, is subject to harmful, dangerous, damaging, or otherwise deleterious exposure during the construction period.

3.6 STARTING AND ADJUSTING

- A. Adjust operating components for proper operation without binding. Adjust equipment for proper operation.

3.7 PROTECTION OF INSTALLED CONSTRUCTION

- A. Provide final protection and maintain conditions that ensure installed Work is without damage or deterioration at time of Substantial Completion.

3.8 CORRECTION OF THE WORK

- A. Repair or remove and replace defective construction. Restore damaged substrates and finishes. Comply with requirements in Division 01 Section "Cutting and Patching."
 - 1. Repairing includes replacing defective parts, refinishing damaged surfaces, touching up with matching materials, and properly adjusting operating equipment.
- B. Restore permanent facilities used during construction to their specified condition.
- C. Remove and replace damaged surfaces that are exposed to view if surfaces cannot be repaired without visible evidence of repair.
- D. Repair components that do not operate properly. Remove and replace operating components that cannot be repaired.

END OF SECTION 01 70 00

**SECTION 01 73 10
CUTTING AND PATCHING**

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes procedural requirements for cutting and patching.
- B. Related Sections include the following:
 - 1. Division 01 Sections "Temporary Facilities" for temporary protection and construction aids.
 - 2. Division 01 Section "Selective Demolition" for debris removal (Alternates No. 1 and No. 2).
 - 3. Division 024400 "Shoring, Bracing and Support" for timber shoring posts throughout.
 - 4. Technical Sections for specific requirements and limitations applicable to cutting and patching individual parts of the Work.

1.3 DEFINITIONS

- A. Cutting: Removal of in-place construction necessary to permit installation or performance of other Work.
- B. Patching: Fitting and repair work required to restore surfaces to original conditions after installation of other Work.

1.4 SUBMITTALS

- A. Cutting and Patching Proposal: Submit a proposal describing procedures at least 10 days before the time cutting and patching will be performed, requesting approval to proceed. Include the following information:
 - 1. Extent: Describe cutting and patching, show how they will be performed, and indicate why they cannot be avoided.
 - 2. Structural Elements: Where cutting and patching involve adding reinforcement to structural elements, submit details and engineering calculations showing integration of reinforcement with original structure.
 - 3. Changes to In-Place Construction: Describe anticipated results. Include changes to structural elements and operating components as well as changes in building's appearance and other significant visual elements.
 - 4. Products: List products to be used and firms or entities that will perform the Work.
 - 5. Architect Approval: Obtain approval of cutting and patching proposal before cutting and patching. Approval does not waive right to later require removal and replacement of unsatisfactory work.

1.5 QUALITY ASSURANCE

- A. Structural Elements: Do not cut and patch structural elements in a manner that could change their load-carrying capacity or load-deflection ratio.

SECTION 01 73 10
CUTTING AND PATCHING

- B. Operational Elements: Do not cut and patch operating elements and related components in a manner that results in reducing their capacity to perform as intended or that results in increased maintenance or decreased operational life or safety.
- C. Miscellaneous Elements: Do not cut and patch miscellaneous elements or related components in a manner that could change their load-carrying capacity, that results in reducing their capacity to perform as intended, or that results in increased maintenance or decreased operational life or safety.

PART 2 - PRODUCTS

2.1 MATERIALS

- A. General: Comply with requirements specified in other Sections.
- B. In-Place Materials: Use materials identical to in-place materials. For exposed surfaces, use materials that visually match in-place adjacent surfaces to the fullest extent possible.
 - 1. If identical materials are unavailable or cannot be used, use materials that, when installed, will match the visual and functional performance of in-place materials.

PART 3 - EXECUTION

3.1 EXAMINATION

- A. Examine surfaces to be cut and patched and conditions under which cutting and patching are to be performed.
 - 1. Compatibility: Before patching, verify compatibility with and suitability of substrates, including compatibility with in-place finishes or primers.
 - 2. Proceed with installation only after unsafe or unsatisfactory conditions have been corrected.

3.2 PREPARATION

- A. Temporary Support: Provide temporary support of Work to be cut.
- B. Protection: Protect in-place construction during cutting and patching to prevent damage. Provide protection from adverse weather conditions for portions of Project that might be exposed during cutting and patching operations.

3.3 PERFORMANCE

- A. General: Employ skilled workers to perform cutting and patching. Proceed with cutting and patching at the earliest feasible time, and complete without delay.
 - 1. Cut in-place construction to provide for installation of other components or performance of other construction, and subsequently patch as required to restore surfaces to their original condition.

SECTION 01 73 10
CUTTING AND PATCHING

- B. Cutting: Cut in-place construction by sawing, drilling, breaking, chipping, grinding, and similar operations, including excavation, using methods least likely to damage elements retained or adjoining construction. If possible, review proposed procedures with original Installer; comply with original Installer's written recommendations.
1. In general, use hand or small power tools designed for sawing and grinding, not hammering and chopping. Cut holes and slots as small as possible, neatly to size required, and with minimum disturbance of adjacent surfaces. Temporarily cover openings when not in use.
 2. Finished Surfaces: Cut or drill from the exposed or finished side into concealed surfaces.
 3. Concrete Masonry: Cut using a cutting machine, such as an abrasive saw or a diamond-core drill.
 4. Excavating and Backfilling: Comply with requirements in applicable Division 31 Sections where required by cutting and patching operations.
 5. Proceed with patching after construction operations requiring cutting are complete.
- C. Patching: Patch construction by filling, repairing, refinishing, closing up, and similar operations following performance of other Work. Patch with durable seams that are as invisible as possible. Provide materials and comply with installation requirements specified in other Sections.
1. Inspection: Where feasible, test and inspect patched areas after completion to demonstrate integrity of installation.
 2. Exposed Finishes: Restore exposed finishes of patched areas and extend finish restoration into retained adjoining construction in a manner that will eliminate evidence of patching and refinishing.
 - a. Clean piping, conduit, and similar features before applying paint or other finishing materials.
 - b. Restore damaged pipe covering to its original condition.
 3. Functional Exterior Building Enclosure: Patch components in a manner that restores enclosure to a weathertight condition.
- D. Cleaning: Clean areas and spaces where cutting and patching are performed. Completely remove paint, mortar, oils, putty, and similar materials.

END OF SECTION 01 73 10

SECTION 01 73 20
SELECTIVE DEMOLITION

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes the following:
 - 1. In conjunction with stabilization of the masonry smokestack, removal of approximately 4 courses of brick from the top of the smokestack.
 - 2. Alternates No. 1 and No. 2: Removal of the collapsed roof structure and miscellaneous debris from the first floor deck and designated portions of the basement floor.
- B. Related Sections include the following:
 - 1. Abatement Work Plan for compliant abatement and removal of hazardous materials in areas designated for debris removal.
 - 2. Division 01 Section "Alternates" for delineation of selective demolition and debris-removal work.
 - 3. Division 01 Section "Summary" for use of premises and Owner-occupancy requirements.
 - 4. Division 01 Section "Photographic Documentation" for preconstruction photographs taken before selective demolition operations.
 - 5. Division 01 Section "Temporary Facilities and Controls" for temporary construction and environmental-protection measures for selective demolition operations.
 - 6. Division 02 Section "Shoring Bracing and Support" for support of the first floor and for stabilization of the top portion of the smokestack.
 - 7. Division 06 Section "Rough Carpentry."

1.3 SCOPE OF SELECTIVE DEMOLITION WORK

- A. Bid prices for selective demolition work shall be based on the following:
 - 1. Base Bid: Removal and salvage of approximately 4 courses of generally loose brick from the top of the smokestack.
 - 2. Alternate No. 1: An estimated volume of uncompacted collapsed roof structure and miscellaneous debris of approximately 4,800 cubic yards (covering a total floor area of approximately 7,200 square feet).
 - 3. Alternate No. 2: An estimated volume of uncompacted collapsed roof structure and miscellaneous debris of approximately 2,750 cubic yards (covering a total floor area of approximately 4,150 square feet).

1.4 DEFINITIONS

- A. Remove: Detach items from existing construction and legally dispose of them off-site, unless indicated to be removed and salvaged or removed and reinstalled.
- B. Remove and Salvage: Detach items from existing construction and deliver them to Owner.

SECTION 01 73 20
SELECTIVE DEMOLITION

- C. Existing to Remain: Existing items of construction that are not to be removed and that are not otherwise indicated to be removed, removed and salvaged, or removed and reinstalled.

1.5 MATERIALS OWNERSHIP

- A. Historic items, relics, and other items of interest or value to Owner that may be encountered during selective demolition remain Owner's property. Carefully remove and salvage each item or object in a manner to prevent damage and deliver promptly to Owner.
- B. Coordinate with Owner's consultant, who will establish special procedures for removal and salvage.

1.6 SUBMITTALS

- A. Qualification Data: For demolition firm.
- B. Schedule of Selective Demolition Activities: Indicate the following:
 - 1. Safety plan for the protection of workers working in the building.
 - 2. Detailed sequence of selective demolition and removal work, with starting and ending dates for each activity.
 - 3. Plan for proposed dust and noise-control.
 - 4. Means of protection for items to remain and items in path of waste removal from building.
- C. Predemolition Photographs: Show existing conditions of adjoining construction and site improvements, including finish surfaces, which might be misconstrued as damage caused by selective demolition operations. Comply with Division 01 Section "Photographic Documentation." Submit before Work begins.
- D. Landfill Records: Indicate receipt and acceptance of hazardous wastes by a landfill facility licensed to accept hazardous wastes.

1.7 QUALITY ASSURANCE

- A. Demolition Firm Qualifications: An experienced firm that has specialized in demolition work similar in material and extent to that indicated for this Project.
- B. Regulatory Requirements: Comply with governing EPA notification regulations before beginning selective demolition. Comply with hauling and disposal regulations of authorities having jurisdiction.
- C. Standards: Comply with ANSI A10.6 and NFPA 241.
- D. Predemolition Conference: Conduct conference at Project site to comply with requirements in Division 01 Section "Project Management and Coordination." Review methods and procedures related to selective demolition including, but not limited to, the following:
 - 1. Inspect and discuss condition of construction to be selectively demolished.
 - 2. Review structural load limitations of existing structure.
 - 3. Review and finalize selective demolition schedule and verify availability of materials, demolition personnel, equipment, and facilities needed to make progress and avoid delays.
 - 4. Review requirements of work performed by other trades that rely on substrates exposed by selective demolition operations.
 - 5. Review areas where existing construction is to remain and requires protection.

SECTION 01 73 20
SELECTIVE DEMOLITION

1.8 PROJECT CONDITIONS

- A. Owner will occupy portions of building immediately adjacent to selective demolition area. Conduct selective demolition so Owner's operations will not be disrupted.
 - 1. Comply with requirements specified in Division 01 Section "Summary."
- B. Conditions existing at time of inspection for bidding purpose will be maintained by Owner as far as practical.
- C. Notify Architect of discrepancies between existing conditions and Drawings before proceeding with selective demolition.
- D. Lead Hazard: Based on the age of the original building, assume that lead paint is present in construction to be selectively demolished.
- E. Asbestos Hazard: Based on the age of the original building, asbestos is present in certain building materials; refer to attached Abatement Work Plan. Suspected and verified asbestos-containing materials that must be disturbed as part of debris-removal operations shall be handled and/or disposed off site in full accordance with local, state and federal environmental and safety regulations.
- F. Storage or sale of removed items or materials on-site is not permitted.
- G. Utility Service: Maintain existing utilities indicated to remain in service and protect them against damage during selective demolition operations.

PART 2 - PRODUCTS (Not Used)

PART 3 - EXECUTION

3.1 EXAMINATION

- A. Survey existing conditions and correlate with requirements indicated to determine extent of selective demolition required.
- B. Inventory and record the condition of items to be removed and reinstalled and items to be removed and salvaged.
- C. When unanticipated mechanical, electrical, or structural elements that conflict with intended function or design are encountered, investigate and measure the nature and extent of conflict. Promptly submit a written report to Architect.
- D. Engage a professional engineer to survey condition of building to determine whether removing any element might result in structural deficiency or unplanned collapse of any portion of structure or adjacent structures during selective demolition operations.
- E. Survey of Existing Conditions: Record existing conditions by use of measured drawing sketches and/or preconstruction photographs.
 - 1. Comply with requirements specified in Division 01 Section "Photographic Documentation."

SECTION 01 73 20
SELECTIVE DEMOLITION

2. Before selective demolition or removal of existing building elements that will be reproduced or duplicated in final Work, make permanent record of measurements, materials, and construction details required to make exact reproduction.

- F. Perform surveys as the Work progresses to detect hazards resulting from selective demolition activities.

3.2 UTILITY SERVICES AND MECHANICAL/ELECTRICAL SYSTEMS

- A. Existing Services/Systems: Maintain services/systems indicated to remain and protect them against damage during selective demolition operations.

1. Comply with requirements for existing services/systems interruptions specified in Division 01 Section "Summary."

3.3 PREPARATION

- A. Site Access and Temporary Controls: Conduct selective demolition and debris-removal operations to ensure minimum interference with roads, streets, walks, walkways, and other adjacent occupied and used facilities.

1. Comply with requirements for access and protection specified in Division 01 Section "Temporary Facilities and Controls."

- B. Temporary Facilities: Provide temporary barricades and other protection required to prevent injury to people and damage to adjacent buildings and facilities to remain.

1. Provide protection to ensure safe passage of people around selective demolition area and to and from occupied portions of building.

2. Provide temporary weather protection, during interval between selective demolition of existing construction on exterior surfaces and new construction, to prevent water leakage and damage to structure and interior areas.

3. Comply with requirements for temporary enclosures, dust control, heating, and cooling specified in Division 01 Section "Temporary Facilities and Controls."

- C. Temporary Shoring: Provide and maintain shoring, bracing, and structural supports as required to preserve stability and prevent movement, settlement, or collapse of construction and finishes to remain, and to prevent unexpected or uncontrolled movement or collapse of construction being demolished.

1. Strengthen or add new supports when required during progress of selective demolition.

3.4 SELECTIVE DEMOLITION, GENERAL

- A. General: Demolish and remove existing construction only to the extent required by new construction and as indicated. Use methods required to complete the Work within limitations of governing regulations and as follows:

1. Proceed with selective demolition systematically, from higher to lower level. Complete selective demolition operations above each floor or tier before disturbing supporting members on the next lower level.

2. Neatly cut openings and holes plumb, square, and true to dimensions required. Use cutting methods least likely to damage construction to remain or adjoining construction. Use hand tools or small power tools

SECTION 01 73 20
SELECTIVE DEMOLITION

- designed for sawing or grinding, not hammering and chopping, to minimize disturbance of adjacent surfaces. Temporarily cover openings to remain.
3. Cut or drill from the exposed or finished side into concealed surfaces to avoid marring existing finished surfaces.
 4. Do not use cutting torches until work area is cleared of flammable materials. At concealed spaces, such as duct and pipe interiors, verify condition and contents of hidden space before starting flame-cutting operations. Maintain portable fire-suppression devices during flame-cutting operations.
 5. Maintain adequate ventilation when using cutting torches.
 6. Remove decayed, vermin-infested, or otherwise dangerous or unsuitable materials and promptly dispose of off-site.
 7. Remove structural framing members and lower to ground by method suitable to avoid free fall and to prevent ground impact or dust generation.
 8. Locate selective demolition equipment and remove debris and materials so as not to impose excessive loads on supporting walls, floors, or framing.
 9. Dispose of demolished items and materials promptly.
- B. Removed and Salvaged Items:
1. Remove excess dust and debris from salvaged items.
 2. Pack or crate items in one or more boxes or on pallets.
 3. Transport items to storage area on-site designated by Owner.
 4. Protect items from damage during transport and storage.
- C. Existing Items to Remain: Protect construction indicated to remain against damage and soiling during selective demolition.

3.5 DISPOSAL OF DEMOLISHED MATERIALS

- A. General: Except for items or materials indicated to be reused, salvaged, reinstalled, or otherwise indicated to remain Owner's property, remove demolished materials from Project site and legally dispose of them in an EPA-approved landfill.
1. Do not allow demolished materials to accumulate on-site.
 2. Remove and transport debris in a manner that will prevent spillage on adjacent surfaces and areas.
 3. Remove debris from elevated portions of building by chute, hoist, or other device that will convey debris to grade level in a controlled descent.
- B. Burning: Do not burn demolished materials.
- C. Disposal: Transport demolished materials off Owner's property and legally dispose of them.

3.6 CLEANING

- A. Clean adjacent structures and improvements of dust, dirt, and debris caused by selective demolition operations. Return adjacent areas to condition existing before selective demolition operations began.

SECTION 01 73 20
SELECTIVE DEMOLITION

3.7 SELECTIVE DEMOLITION SCHEDULE

A. Existing Construction to Be Removed:

1. Alternate No. 1: All construction materials and debris resting partially or completely on first floor of east wing of main mill block, and all collapsed sections of first floor resting on basement floor beneath. Refer to Drawings A101 and A102.
2. Alternate No. 2: All construction materials and debris resting partially or completely on first floor of west wing of main mill block, and all collapsed and collapsing sections of first floor resting on basement floor beneath and at south ell. Refer to Drawings A101 and A102.

B. Existing Items to Be Removed and Salvaged (Base Bid):

1. Top courses of brick at smokestack.
2. Window sash at masonry openings designated for window boarding.

END OF SECTION 01 73 20

SECTION 01 77 00
CLOSEOUT PROCEDURES

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes administrative and procedural requirements for contract closeout, including, but not limited to, the following:
1. Inspection procedures.
 2. Warranties.
 3. Instruction of Owner's Personnel.
 4. Final cleaning.
- B. Related Sections include the following:
1. Division 01 Section "Payment Procedures" for requirements for Applications for Payment for Substantial and Final Completion.
 2. Division 01 Section "Photographic Documentation" for submitting Final Completion construction photographs and digital files.
 3. Division 01 Section "Execution Requirements" for progress cleaning of Project site.
 4. Technical Sections for specific closeout requirements for the Work in those Sections.

1.3 SUBSTANTIAL COMPLETION

- A. Preliminary Procedures: Before requesting inspection for determining date of Substantial Completion, complete the following. List items below that are incomplete in request.
1. Prepare a list of items to be completed and corrected (punch list), the value of items on the list, and reasons why the Work is not complete.
 2. Advise Owner of pending insurance changeover requirements.
 3. Submit specific warranties, workmanship bonds, maintenance service agreements, final certifications and similar documents.
 4. Obtain and submit releases permitting Owner unrestricted use of the Work and access to services and utilities. Include occupancy permits, operating certificates, and similar releases.
 5. Prepare and submit Project Record Documents, operation and maintenance manuals, Final Completion construction photographs, and similar final record information.
 6. Deliver tools, spare parts, extra materials, and similar items to location designated by Owner. Label with manufacturer's name and model number where applicable.
 7. Terminate and remove temporary facilities from Project site, along with mockups, construction tools, and similar elements.
 8. Advise Owner of changeover in utilities.
 9. Complete final cleaning requirements.

**SECTION 01 77 00
CLOSEOUT PROCEDURES**

- B. Inspection: Submit a written request for inspection for Substantial Completion. On receipt of request, Architect will either proceed with inspection or notify Contractor of unfulfilled requirements. Architect will prepare the Certificate of Substantial Completion after inspection or will notify Contractor of items, either on Contractor's list or additional items identified by Architect, that must be completed or corrected before certificate will be issued.
 - 1. Reinspection: Request reinspection when the Work identified in previous inspections as incomplete is completed or corrected.
 - 2. Results of completed inspection will form the basis of requirements for Final Completion.

1.4 FINAL COMPLETION

- A. Preliminary Procedures: Before requesting final inspection for determining date of Final Completion, complete the following:
 - 1. Submit a final Application for Payment according to Division 01 Section "Payment Procedures."
 - 2. Submit certified copy of Architect's Substantial Completion inspection list of items to be completed or corrected (punch list), endorsed and dated by Architect. The certified copy of the list shall state that each item has been completed or otherwise resolved for acceptance.
 - 3. Submit evidence of final, continuing insurance coverage complying with insurance requirements.
- B. Inspection: Submit a written request for final inspection for acceptance. On receipt of request, Architect will either proceed with inspection or notify Contractor of unfulfilled requirements. Architect will prepare a final Certificate for Payment after inspection or will notify Contractor of construction that must be completed or corrected before certificate will be issued.
 - 1. Reinspection: Request reinspection when the Work identified in previous inspections as incomplete is completed or corrected.

1.5 LIST OF INCOMPLETE ITEMS (PUNCH LIST)

- A. Preparation: Submit **three** copies of list. Include name and identification of each space and area affected by construction operations for incomplete items and items needing correction including, if necessary, areas disturbed by Contractor that are outside the limits of construction.
 - 1. Include the following information at the top of each page:
 - a. Project name.
 - b. Date.
 - c. Name of Architect
 - d. Name of Contractor.
 - e. Page number.

1.6 WARRANTIES

- A. Submittal Time: Submit written warranties on request of Architect for designated portions of the Work where commencement of warranties other than date of Substantial Completion is indicated.

SECTION 01 77 00
CLOSEOUT PROCEDURES

PART 2 - PRODUCTS

2.1 MATERIALS

- A. Cleaning Agents: Use cleaning materials and agents recommended by manufacturer or fabricator of the surface to be cleaned. Do not use cleaning agents that are potentially hazardous to health or property or that might damage finished surfaces.

PART 3 - EXECUTION

3.1 FINAL CLEANING

- A. General: Provide final cleaning. Conduct cleaning and waste-removal operations to comply with local laws and ordinances and Federal and local environmental and antipollution regulations.
- B. Cleaning: Employ experienced workers or professional cleaners for final cleaning. Clean each surface or unit to condition expected in an average commercial building cleaning and maintenance program. Comply with manufacturer's written instructions.
 - 1. Complete the following cleaning operations before requesting inspection for certification of Substantial Completion for entire Project or for a portion of Project:
 - a. Clean Project site, yard, and grounds, in areas disturbed by construction activities, including landscape development areas, of rubbish, waste material, litter, and other foreign substances.
 - b. Sweep paved areas broom clean. Remove petrochemical spills, stains, and other foreign deposits.
 - c. Rake grounds that are neither planted nor paved to a smooth, even-textured surface.
 - d. Remove tools, construction equipment, machinery, and surplus material from Project site.
 - e. Sweep concrete floors broom clean in unoccupied spaces.
- C. Comply with safety standards for cleaning. Do not burn waste materials. Do not bury debris or excess materials on Owner's property. Do not discharge volatile, harmful, or dangerous materials into drainage systems. Remove waste materials from Project site and dispose of lawfully.

END OF SECTION 01 77 00

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and Division 1 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. The Work under this Section includes providing all labor, materials, tools and equipment necessary for clearing, grubbing, removing and disposing of all vegetation and debris (including earthen materials incidentally removed with vegetation and debris), and removing structures and obstructions located within the limits shown on the Drawings or designated by the Architect, except such objects as are designated to remain in place or are to be removed in accordance with other sections of these Specifications. The Work shall also include the preservation from injury or defacement of all vegetation and objects designated to remain.
- B. This Section includes the following:
 - 1. Protecting existing trees and vegetation to remain (as applicable).
 - 2. Removing trees and other vegetation.
 - 3. Clearing and grubbing.
- C. Related Sections include the following:
 - 1. Division 1 Section "Temporary Facilities and Controls" for temporary utilities, temporary construction and support facilities, temporary security and protection facilities, and environmental protection measures during site operations.
 - 2. Division 2 Section 01 73 20 "Alternates No. 1 and No. 2: Selective Demolition" for partial demolition of buildings or structures undergoing alterations.

1.3 DEFINITIONS

- A. Topsoil: Natural or cultivated surface-soil layer containing organic matter and sand, silt, and clay particles; friable, pervious, and black or a darker shade of brown, gray, or red than underlying subsoil; reasonably free of subsoil, clay lumps, gravel, and other objects more than 2 inches (50 mm) in diameter; and free of weeds, roots, and other deleterious materials.

1.4 MATERIALS OWNERSHIP

- A. Except for materials indicated to be stockpiled or to remain Owner's property, cleared materials shall become Contractor's property and shall be removed from the site.

1.5 SUBMITTALS

- A. Work plan for site clearing and grubbing.

1.6 PROJECT CONDITIONS

- A. Traffic: Minimize interference with adjoining roads, streets, walks, and other adjacent occupied or used facilities during site-clearing operations.
 - 1. Do not close or obstruct streets, walks, or other adjacent occupied or used facilities without permission from Owner and authorities having jurisdiction.
 - 2. Provide alternate routes around closed or obstructed traffic ways if required by authorities having jurisdiction.
- B. Improvements on Adjoining Property: Authority for performing indicated removal and alteration work on property adjoining Owner's property will be obtained by Owner before award of Contract.

PART 2 - PRODUCTS (Not Applicable)

PART 3 - EXECUTION

3.1 TREE PROTECTION

- A. Protect trees outside of limit of work and on adjacent properties.
 - 1. Do not store construction materials, debris, or excavated material within drip line of trees outside of limit of work. Do not permit vehicles, equipment, or foot traffic within drip line of these trees.
 - 2. Repair or replace all such trees damaged by construction operations, in a manner approved by Architect.

3.2 CLEARING AND GRUBBING

- A. Remove obstructions, trees, shrubs, grass, and other vegetation as indicated or required. Removal includes digging out stumps and obstructions and grubbing roots.
 - 1. Do not remove trees, shrubs, and other vegetation indicated to remain or to be relocated.
 - 2. Completely remove stumps, roots, obstructions, and debris extending to a depth of 18 inches below exposed subgrade.
- B. Fill depressions caused by clearing and grubbing operations with satisfactory soil material, unless further excavation or earthwork is indicated.
 - 1. Place fill material in horizontal layers not exceeding 8-inch loose depth, and compact each layer to a density equal to adjacent original ground.

3.5 GRUBBING

- A. All trees, stumps, roots and other objects not designated to remain shall be cleared and grubbed. If the area is not to be benched, the removal of undisturbed stumps and roots and nonperishable solid objects that will be a minimum of four feet below the embankment surface and that do not extend more than six inches above the original ground line, will not be required.

SECTION 02 23 30
SITE CLEARING

- B. In areas outside of the grading limits of cut and embankment areas and to the established limits of the WORK, all stumps and nonperishable solid objects permitted to remain in place shall be cut off not more than six inches above the ground line or low water level.
- C. Except in areas to be excavated, stump holes and other holes from which obstructions are removed shall be back-filled with suitable materials and compacted in accordance with the Contract Documents.

3.6 DISPOSAL

- A. Disposal: Remove surplus soil material, unsuitable topsoil, obstructions, demolished materials, and waste materials, including trash and debris, and legally dispose of them off Owner's property.

END OF SECTION 02 23 00

PART 1 - GENERAL

1.1 GENERAL PROVISIONS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and Division 1 Specifications Sections, apply to this Section.
- B. Attention is directed to the existing conditions at the site. The Contractor shall become thoroughly familiar with the existing conditions in order to assess the scope of work required.
- C. The Contractor shall monitor the condition and stability of the structure during the work and notify the Engineer, the inspectional services department and the fire department immediately if there are any indications of new movement or instability in the structure, stopping all work until it is deemed safe that the work be resumed.
- D. The contractor shall keep the Architect abreast of all conditions that are uncovered during the work that might affect it. The Architect and Structural Engineer of Record reserve the right to make modifications in the scope of work as may be needed to accommodate discovered conditions and the engineer will consider and review all suggested alternatives submitted by the contractor as may improve the safety, timeliness and effectiveness of the work.
- E. The Contractor shall make every reasonable attempt to complete the work absolutely as quickly and as safely as possible, keeping in mind the uncertainty and possibility of severe winter weather which may damage or even collapse the structure.

1.2 WORK INCLUDED

- A. Installation of all required temporary shoring, bracing and support as detailed on the Contract Drawings.

1.3 REFERENCES

- A. Comply with all applicable requirements of other sections and all OSHA and safety regulations.

1.4 QUALITY ASSURANCE

- A. Comply with all referenced standards for the products employed.
- B. Schedule all appropriate site visits and inspections with the Structural Engineer of Record for the shoring system.

PART 2 - PRODUCTS AND MATERIALS

2.1 MATERIALS AND PRODUCTS

- A. Products and materials shall be as described on the drawings and below.
- B. Timber Shoring and Dunnage Materials
 - 1. Dunnage, cribbing, shoring caps, shoring bases, and shoring posts that are denoted as "P/T" shall be No. 1 or No. 2 grade Southern Yellow Pine (SYP) pressure preservative treated with a minimum retention of 0.6 pcf of ACQ.
 - 2. Post timbers not designated "P/T" shall be No. 1 or No. 2 Spruce Pine Fir or Hem Fir, dressed or graded rough sawn.
 - 3. All timbers shall be dried to 19 percent maximum moisture content and shall be free of twists and bends.
- C. Wire Rope and Accessories
 - 1. The contractor shall install all wire rope wrapping as indicated, along w/ all necessary attachments, block, turnbuckles, and hardware, whether specifically indicates on these drawings or required as "incidentals" for the completion of the work.
 - 2. All cable synchs (wire rope) shall be non-galvanized, non-stainless steel, 6-wire (plus core) "iwrc", "xip" wire rope as manufactured by the "Wire Rope Corporation of America, Inc., available via the Philip A. Rand Corp., Newton, Massachusetts.
 - 3. Wire rope shall have the following minimum breaking capacities: 3/8" dia. @ 7.55 tons,
 - 4. All attachment hardware shall be sufficient to develop the full design capacity of the wire rope and shall be of not less than the nominal sizes indicated on the drawings. Eye and turnbuckle hardware shall be 1/2" nominal for 3/8" wire rope.

PART 3 - EXECUTION

3.1 TEMPORARY SHORING AND BRACING

- A. The contractor shall be solely responsible for all means and methods of installation employed on this project and the safe installation of all temporary bracing, support and protection of the existing Structure. Any sequences of work or methods indicated or implied in the contract documents are present only as assumptions on which the design of the permanent installations are based and are to be considered as a suggested option for review by the Contractor.

3.2 TIMBER CRIBBING INSTALLATION

- A. Locate cribbing positions according to plans and clean bearing surfaces from all piled and suspended debris.

SECTION 02 44 00
SHORING, BRACING AND SUPPORT

- B. Erect cribbing as shown on drawings in sufficient, solidly bearing stacks to reach just short of the level above, filling the top course of the stack with a solid row of timbers in order to provide a full and uninterrupted bearing area equal to the outer dimensions of the pile.
- C. Fill-in the remaining height between the cribbing stack and the underside of the decking above with solid blocking.

3.3 TIMBER SHORING POST INSTALLATION

- A. Locate post positions according to plans and clean bearing surfaces from all piled and suspended debris.
- B. Erect posts, bases and caps (where indicated) as shown on drawings, wedging them tightly into place and toe-nailing them into position. Do not attempt to lift existing timber beams more than 1/4" when positioning posts. Posts should be properly cut to length, which will vary by location, so that shimming thickness does not exceed 3/8".
- C. Where shimming is needed, utilize tapered cedar shingles or shakes driven from opposite directions in order to create flat contact surfaces. Balance the shimming around the post so as not to put bending stresses into the posts.

3.4 TIMBER DUNNAGE INSTALLATION

- A. Suspend dunnage timbers from top of stack after removing loose bricks from around rim. Suspension may consist of bent rods that hook over the top of the stack rim.
- B. Provide protruding lag screws to support the wire rope cable loops that will cinch the dunnage together.
- C. Align dunnage timbers vertically and evenly around the circumference of the stack. Position flatly against the brickwork for solid and even bearing.

3.5 WIRE ROPE CINCH INSTALLATION

- A. Loop wire rope cinches around vertical dunnage suspended from top of stack, resting them atop protruding lag screws.
- B. Terminate cinch cables by looping around pre-formed thimbles that are passed through closed 1/2" nominal eye-bolts threaded into 1/2" nominal turnbuckles. Clamp looped cables together with three Crosby clips per termination.
- C. Tighten wire rope cinches using the turnbuckles for a snug fit, removing all sag from between the dunnage timbers.
- D. Contractor and wire rope supplier shall review the design and verify the fit and clearance of all connected items and notify the Architect of any necessary modifications before proceeding with the work.
- E. No cables shall be bent at tighter than a 20-cable diameter radius, except where 3/8" cable passes through thimbles. Bends of greater than 5 degrees shall be made in pre-bent galvanized steel pipe and bends of less than 5 degrees shall be made with sufficient padding, curved blocking and/or taping as needed to protect the cable from kinking or chafing.
- F. Thimbles shall have an efficiency rating of not less than 80%.

END OF SECTION 02 44 00

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

- A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

- A. This Section includes the following:
 - 1. Framing with dimension lumber.
 - 2. Pressure-treated wood blocking, furring, cants and nailers.
 - 3. Boarding-up designated window and door openings.
 - 4. All other rough wood framing, backing and other concealed wood supports, and all other rough carpentry items incidental to the stabilization work.
 - 5. All rough hardware, inserts, hangers and anchors, and other related metal components, necessary to the installation of the rough carpentry.
 - 6. Alternate No. 3: Framing, plywood and associated hardware required to protect existing iron cresting and support plastic tarps atop bell tower.
- B. Related Sections include the following:
 - 1. Section 01 23 00 "Alternates."
 - 2. Section 02 44 00 "Shoring, Bracing and Support."

1.3 DEFINITIONS

- A. Dimension Lumber: Lumber of 2 inches nominal (38 mm actual) or greater but less than 5 inches nominal (114 mm actual) in least dimension.
- B. Lumber grading agencies, and the abbreviations used to reference them, include the following:
 - 1. NeLMA: Northeastern Lumber Manufacturers' Association.
 - 2. NLGA: National Lumber Grades Authority.
 - 3. RIS: Redwood Inspection Service.
 - 4. SPIB: The Southern Pine Inspection Bureau.
 - 5. WCLIB: West Coast Lumber Inspection Bureau.
 - 6. WWPA: Western Wood Products Association.

1.4 SUBMITTALS

- A. Product Data: For each type of process and factory-fabricated product. Indicate component materials and dimensions and include construction and application details.

SECTION 06 10 00
ROUGH CARPENTRY

1. Include data for wood-preservative treatment from chemical treatment manufacturer and certification by treating plant that treated materials comply with requirements. Indicate type of preservative used and net amount of preservative retained.
 2. Include copies of warranties from chemical treatment manufacturers for each type of treatment.
- B. Research/Evaluation Reports: For the following, showing compliance with building code in effect for Project:
1. Wood-Preservative-treated lumber.
 2. Power-driven fasteners.
 3. Powder-actuated fasteners.
 4. Metal framing anchors.

PART 2 - PRODUCTS

2.1 WOOD PRODUCTS, GENERAL

- A. Lumber: DOC PS 20 and applicable rules of grading agencies indicated. If no grading agency is indicated, provide lumber that complies with the applicable rules of any rules-writing agency certified by the ALSC Board of Review. Provide lumber graded by an agency certified by the ALSC Board of Review to inspect and grade lumber under the rules indicated.
1. Factory mark each piece of lumber with grade stamp of grading agency.
 2. Where nominal sizes are indicated, provide actual sizes required by DOC PS 20 for moisture content specified. Where actual sizes are indicated, they are minimum dressed sizes for dry lumber.
 3. Provide dressed lumber, S4S, unless otherwise indicated.

2.2 WOOD-PRESERVATIVE-TREATED LUMBER

- A. Preservative Treatment by Pressure Process: AWPA C2, except that lumber that is not in contact with the ground and is continuously protected from liquid water may be treated according to AWPA C31 with inorganic boron (SBX).
1. Preservative Chemicals: Acceptable to authorities having jurisdiction and containing no arsenic or chromium.
- B. Kiln-dry lumber after treatment to a maximum moisture content of 19 percent. Do not use material that is warped or does not comply with requirements for untreated material.
- C. Mark lumber with treatment quality mark of an inspection agency approved by the ALSC Board of Review.
- D. Application: Treat items indicated on Drawings, and the following:
1. Wood cants, nailers, curbs, equipment support bases, blocking, stripping, and similar members in connection with roofing, flashing, vapor barriers, and waterproofing.
 2. Wood blocking, furring, stripping, and similar concealed members in contact with masonry or concrete.

SECTION 06 10 00
ROUGH CARPENTRY

2.3 PLYWOOD FOR BOARDING MASONRY DOOR AND WINDOW OPENINGS

- A. CD Exterior-grade plywood, un-sanded.
- B. Provide plywood 5/8" minimum thickness for door and window openings.
- C. Drill or core array of ventilation holes, as indicated.
- D. Drill holes as needed to accommodate galvanized steel bolts and/or threaded rods; refer to detail for dimensional parameters.

2.4 MISCELLANEOUS LUMBER

- A. General: Provide miscellaneous lumber indicated and lumber for support or attachment of other construction, including the following:
 - 1. Blocking.
 - 2. Nailers.
- B. For items of dimension lumber size, provide Construction or No. 2 grade lumber with 19 percent maximum moisture content and any of the following species:
 - 1. Hem-fir (north); NLGA.
 - 2. Mixed southern pine; SPIB.
 - 3. Spruce-pine-fir; NLGA.
 - 4. Hem-fir; WCLIB, or WWPA.
 - 5. Spruce-pine-fir (south); NeLMA, WCLIB, or WWPA.
 - 6. Western woods; WCLIB or WWPA.
 - 7. Northern species; NLGA.
- C. For "Bridge" construction at the basement floor level, provide the following:
 - 1. Spanning timbers laid on the floor (designated as "P/T") shall be No. 1 or No. 2 grade Southern Yellow Pine (SYP) pressure preservative treated with a minimum retention of 0.6 pcf of ACQ.
 - 2. Decking planks shall be rough-sawn Hemlock or Pine.
 - 3. Dimensional lumber side rails shall be Spruce-Pine-Fir No. 2 grade or better.
 - 4. All timbers shall be dried to 19 percent maximum moisture content and shall be free of twists and bends.
- D. For concealed boards, provide lumber with 19 percent maximum moisture content and any of the following species and grades:
 - 1. Mixed southern pine, No.2 grade; SPIB.
 - 2. Hem-fir or hem-fir (north), Construction or 2 Common grade; NLGA, WCLIB, or WWPA.
 - 3. Spruce-pine-fir (south) or spruce-pine-fir, Construction or 2 Common grade; NeLMA, NLGA, WCLIB, or WWPA.
- E. For blocking and nailers used for attachment of other construction, select and cut lumber to eliminate knots and other defects that will interfere with attachment of other work.

SECTION 06 10 00
ROUGH CARPENTRY

2.5 FASTENERS

- A. General: Provide fasteners of size and type indicated that comply with requirements specified in this Article for material and manufacture.
 - 1. Where rough carpentry is exposed to weather, in ground contact, pressure-preservative treated, or in area of high relative humidity, provide fasteners of Type 304 stainless steel.
 - 2. Provide galvanized bolts and/or threaded rods for plywood door and window boarding assemblies.
- B. Nails, Brads, and Staples: ASTM F 1667.
- C. Power-Driven Fasteners: NES NER-272.
- D. Wood Screws: ASME B18.6.1.
- E. Lag Bolts: ASME B18.2.1 (ASME B18.2.3.8M).
- F. Bolts: Steel bolts complying with ASTM A 307, Grade A (ASTM F 568M, Property Class 4.6); with ASTM A 563 (ASTM A 563M) hex nuts and, where indicated, flat washers.

PART 3 - EXECUTION

3.1 DELIVERY, STORAGE, AND HANDLING

- A. Stack lumber flat with spacers between each bundle to provide air circulation. Provide for air circulation around stacks and under coverings.

3.2 BOARDING DOOR AND WINDOW MASONRY OPENINGS

- A. For masonry openings with extant window sash, carefully remove upper and lower sash and store on interior-side floor, adjacent to window opening.
- B. Cut rectangular plywood boards to fully cover face of door and window masonry opening as applicable, with overlap indicated on Drawings. Each plywood covering shall consist of a single, continuous panel.
- C. Pre-drill or drill-in-place holes for anchor bolts and/or threaded rods, in neat, workmanlike manner.
- D. Washers shall be of sufficient size to fully-accept, for carriage bolts, the square portion of bolt beneath head and, for threaded rods, the nuts and washers. Bolt and mating hardware may be galvanized or cadmium plated.
- E. 2"x4" lumber shall be graded and shall extend a minimum of 16" longer than the width of the plywood cover.

SECTION 06 10 00
ROUGH CARPENTRY

3.3 INSTALLATION, GENERAL

- A. Set rough carpentry to required levels and lines, with members plumb, true to line, cut, and fitted. Fit rough carpentry to other construction; scribe and cope as needed for accurate fit. Locate furring, nailers, blocking, and similar supports to comply with requirements for attaching other construction.
- B. Framing Standard: Comply with AF&PA's "Details for Conventional Wood Frame Construction," unless otherwise indicated.
- C. Do not use materials with defects that impair quality of installation or pieces that are too small to use with minimum number of joints or optimum joint arrangement.
- D. Cut panels at penetrations, edges, and other obstructions of work; fit tightly against abutting construction, unless otherwise indicated.
- E. Comply with AWWA M4 for applying field treatment to cut surfaces of preservative-treated lumber.
 - 1. Use inorganic boron for items that are continuously protected from liquid water.
 - 2. Use copper naphthenate for items not continuously protected from liquid water.
- F. Use common wire nails, unless otherwise indicated. Select fasteners of size that will not fully penetrate members where opposite side will be exposed to view or will receive finish materials. Make tight connections between members. Install fasteners without splitting wood; do not countersink nail heads, unless otherwise indicated.
- G. For exposed work, arrange fasteners in straight rows parallel with edges of members, with fasteners evenly spaced, and with adjacent rows staggered.

3.4 WOOD BLOCKING AND NAILER INSTALLATION

- A. Install where indicated and where required for attaching other work. Form to shapes indicated and cut as required for true line and level of attached work. Coordinate locations with other work involved.
- B. Attach items to substrates to support applied loading. Recess bolts and nuts flush with surfaces, unless otherwise indicated.

END OF SECTION 06 10 00

"ATTACHMENT A"
[Wage Rates]



**THE COMMONWEALTH OF MASSACHUSETTS
EXECUTIVE OFFICE OF LABOR AND WORKFORCE DEVELOPMENT
DEPARTMENT OF LABOR STANDARDS**

Prevailing Wage Rates

**As determined by the Director under the provisions of the
Massachusetts General Laws, Chapter 149, Sections 26 to 27H**

RONALD L. WALKER, II
Secretary

WILLIAM D MCKINNEY
Director

CHARLES D. BAKER
Governor

KARYN E. POLITO
Lt. Governor

Awarding Authority: Town of Westford
Contract Number: **City/Town:** WESTFORD
Description of Work: Phase 1 Stabilization of an historic mill building located at 12 North Main Street in Westford, MA. The project will include debris removal, hazardous material abatement, structural reinforcement
Job Location: 12 North Main Street

Information about Prevailing Wage Schedules for Awarding Authorities and Contractors

- This wage schedule applies only to the specific project referenced at the top of this page and uniquely identified by the “Wage Request Number” on all pages of this schedule.
- An Awarding Authority must request an updated wage schedule from the Department of Labor Standards (“DLS”) if it has not opened bids or selected a contractor within 90 days of the date of issuance of the wage schedule. For CM AT RISK projects (bid pursuant to G.L. c.149A), the earlier of: (a) the execution date of the GMP Amendment, or (b) the bid for the first construction scope of work must be within 90-days of the wage schedule issuance date.
- The wage schedule shall be incorporated in any advertisement or call for bids for the project as required by M.G.L. c. 149, § 27. The wage schedule shall be made a part of the contract awarded for the project. The wage schedule must be posted in a conspicuous place at the work site for the life of the project in accordance with M.G.L. c. 149 § 27. The wages listed on the wage schedule must be paid to employees performing construction work on the project whether they are employed by the prime contractor, a filed sub-bidder, or any sub-contractor.
- All apprentices working on the project are required to be registered with the Massachusetts Division of Apprentice Standards (DAS). Apprentice must keep his/her apprentice identification card on his/her person during all work hours on the project. An apprentice registered with DAS may be paid the lower apprentice wage rate at the applicable step as provided on the prevailing wage schedule. **If an apprentice rate is not listed on the prevailing wage schedule for the trade in which an apprentice is registered with the DAS, the apprentice must be paid the journeyworker's rate for the trade.**
- The wage rates will remain in effect for the duration of the project, except in the case of multi-year public construction projects. For construction projects lasting longer than one year, awarding authorities must request an updated wage schedule. Awarding authorities are required to request these updates no later than two weeks before the anniversary of the date the contract was executed by the awarding authority and the general contractor. For multi-year CM AT RISK projects, awarding authority must request an annual update no later than two weeks before the anniversary date, determined as the earlier of: (a) the execution date of the GMP Amendment, or (b) the execution date of the first amendment to permit procurement of construction services. Contractors are required to obtain the wage schedules from awarding authorities, and to pay no less than these rates to covered workers. The annual update requirement is not applicable to 27F “rental of equipment” contracts.
- Every contractor or subcontractor which performs construction work on the project is required to submit weekly payroll reports and a Statement of Compliance directly to the awarding authority by mail or email and keep them on file for three years. Each weekly payroll report must contain: the employee’s name, address, occupational classification, hours worked, and wages paid. Do not submit weekly payroll reports to DLS. A sample of a payroll reporting form may be obtained at <http://www.mass.gov/dols/pw>.
- Contractors with questions about the wage rates or classifications included on the wage schedule have an affirmative obligation to inquire with DLS at (617) 626-6953.
- Employees not receiving the prevailing wage rate set forth on the wage schedule may report the violation to the Fair Labor Division of the office of the Attorney General at (617) 727-3465.
- Failure of a contractor or subcontractor to pay the prevailing wage rates listed on the wage schedule to all employees who perform construction work on the project is a violation of the law and subjects the contractor or subcontractor to civil and criminal penalties.

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
Construction						
(2 AXLE) DRIVER - EQUIPMENT <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$31.65	\$10.41	\$9.33	\$0.00	\$51.39
	12/01/2015	\$31.65	\$10.41	\$10.08	\$0.00	\$52.14
	06/01/2016	\$32.15	\$10.41	\$10.08	\$0.00	\$52.64
	08/01/2016	\$32.15	\$10.91	\$10.08	\$0.00	\$53.14
	12/01/2016	\$32.15	\$10.91	\$10.89	\$0.00	\$53.95
(3 AXLE) DRIVER - EQUIPMENT <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$31.72	\$10.41	\$9.33	\$0.00	\$51.46
	12/01/2015	\$31.72	\$10.41	\$10.08	\$0.00	\$52.21
	06/01/2016	\$32.22	\$10.41	\$10.08	\$0.00	\$52.71
	08/01/2016	\$32.22	\$10.91	\$10.08	\$0.00	\$53.21
	12/01/2016	\$32.22	\$10.91	\$10.89	\$0.00	\$54.02
(4 & 5 AXLE) DRIVER - EQUIPMENT <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$31.84	\$10.41	\$9.33	\$0.00	\$51.58
	12/01/2015	\$31.84	\$10.41	\$10.08	\$0.00	\$52.33
	06/01/2016	\$32.34	\$10.41	\$10.08	\$0.00	\$52.83
	08/01/2016	\$32.34	\$10.91	\$10.08	\$0.00	\$53.33
	12/01/2016	\$32.34	\$10.91	\$10.89	\$0.00	\$54.14
ADS/SUBMERSIBLE PILOT <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$88.29	\$9.80	\$19.23	\$0.00	\$117.32
AIR TRACK OPERATOR <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	12/01/2015	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	06/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50
	12/01/2016	\$33.65	\$7.30	\$12.30	\$0.00	\$53.25
For apprentice rates see "Apprentice- LABORER"						
ASBESTOS REMOVER - PIPE / MECH. EQUIPT. <i>HEAT & FROST INSULATORS LOCAL 6 (BOSTON)</i>	06/01/2015	\$33.43	\$10.40	\$5.95	\$0.00	\$49.78
	12/01/2015	\$34.38	\$10.40	\$5.95	\$0.00	\$50.73
ASPHALT RAKER <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75
For apprentice rates see "Apprentice- LABORER"						
ASPHALT/CONCRETE/CRUSHER PLANT-ON SITE <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
BACKHOE/FRONT-END LOADER <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
BARCO-TYPE JUMPING TAMPER <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75
For apprentice rates see "Apprentice- LABORER"						
BLOCK PAVER, RAMMER / CURB SETTER <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	12/01/2015	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	06/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50
	12/01/2016	\$33.65	\$7.30	\$12.30	\$0.00	\$53.25
For apprentice rates see "Apprentice- LABORER"						
BOILER MAKER <i>BOILERMAKERS LOCAL 29</i>	01/01/2015	\$40.32	\$6.97	\$16.21	\$0.00	\$63.50
	01/01/2016	\$41.62	\$6.97	\$16.21	\$0.00	\$64.80
	01/01/2017	\$42.92	\$6.97	\$16.21	\$0.00	\$66.10

Apprentice - BOILERMAKER - Local 29

Effective Date - 01/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	65	\$26.21	\$6.97	\$10.54	\$0.00	\$43.72
2	65	\$26.21	\$6.97	\$10.54	\$0.00	\$43.72
3	70	\$28.22	\$6.97	\$11.35	\$0.00	\$46.54
4	75	\$30.24	\$6.97	\$12.16	\$0.00	\$49.37
5	80	\$32.26	\$6.97	\$12.97	\$0.00	\$52.20
6	85	\$34.27	\$6.97	\$13.78	\$0.00	\$55.02
7	90	\$36.29	\$6.97	\$14.59	\$0.00	\$57.85
8	95	\$38.30	\$6.97	\$15.40	\$0.00	\$60.67

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	65	\$27.05	\$6.97	\$10.54	\$0.00	\$44.56
2	65	\$27.05	\$6.97	\$10.54	\$0.00	\$44.56
3	70	\$29.13	\$6.97	\$11.35	\$0.00	\$47.45
4	75	\$31.22	\$6.97	\$12.16	\$0.00	\$50.35
5	80	\$33.30	\$6.97	\$12.97	\$0.00	\$53.24
6	85	\$35.38	\$6.97	\$13.78	\$0.00	\$56.13
7	90	\$37.46	\$6.97	\$14.59	\$0.00	\$59.02
8	95	\$39.54	\$6.97	\$15.40	\$0.00	\$61.91

Notes:

Apprentice to Journeyworker Ratio:1:5

BRICK/STONE/ARTIFICIAL MASONRY (INCL. MASONRY WATERPROOFING) <i>BRICKLAYERS LOCAL 3 (LOWELL)</i>	09/01/2015	\$47.76	\$10.18	\$17.97	\$0.00	\$75.91
	03/01/2016	\$48.33	\$10.18	\$17.97	\$0.00	\$76.48
	09/01/2016	\$49.23	\$10.18	\$18.05	\$0.00	\$77.46
	03/01/2017	\$49.80	\$10.18	\$18.05	\$0.00	\$78.03

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - BRICK/PLASTER/CEMENT MASON - Local 3 Lowell

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$23.88	\$10.18	\$17.97	\$0.00	\$52.03
2	60	\$28.66	\$10.18	\$17.97	\$0.00	\$56.81
3	70	\$33.43	\$10.18	\$17.97	\$0.00	\$61.58
4	80	\$38.21	\$10.18	\$17.97	\$0.00	\$66.36
5	90	\$42.98	\$10.18	\$17.97	\$0.00	\$71.13

Effective Date - 03/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.17	\$10.18	\$17.97	\$0.00	\$52.32
2	60	\$29.00	\$10.18	\$17.97	\$0.00	\$57.15
3	70	\$33.83	\$10.18	\$17.97	\$0.00	\$61.98
4	80	\$38.66	\$10.18	\$17.97	\$0.00	\$66.81
5	90	\$43.50	\$10.18	\$17.97	\$0.00	\$71.65

Notes:

Apprentice to Journeyworker Ratio:1:5

BULLDOZER/GRADER/SCRAPER	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
<i>OPERATING ENGINEERS LOCAL 4</i>	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

CAISSON & UNDERPINNING BOTTOM MAN	06/01/2015	\$36.20	\$7.30	\$13.40	\$0.00	\$56.90
<i>LABORERS - FOUNDATION AND MARINE</i>	12/01/2015	\$36.95	\$7.30	\$13.40	\$0.00	\$57.65
	06/01/2016	\$37.70	\$7.30	\$13.40	\$0.00	\$58.40
	12/01/2016	\$38.70	\$7.30	\$13.40	\$0.00	\$59.40

For apprentice rates see "Apprentice- LABORER"

CAISSON & UNDERPINNING LABORER	06/01/2015	\$35.05	\$7.30	\$13.40	\$0.00	\$55.75
<i>LABORERS - FOUNDATION AND MARINE</i>	12/01/2015	\$35.80	\$7.30	\$13.40	\$0.00	\$56.50
	06/01/2016	\$36.55	\$7.30	\$13.40	\$0.00	\$57.25
	12/01/2016	\$37.55	\$7.30	\$13.40	\$0.00	\$58.25

For apprentice rates see "Apprentice- LABORER"

CAISSON & UNDERPINNING TOP MAN	06/01/2015	\$35.05	\$7.30	\$13.40	\$0.00	\$55.75
<i>LABORERS - FOUNDATION AND MARINE</i>	12/01/2015	\$35.80	\$7.30	\$13.40	\$0.00	\$56.50
	06/01/2016	\$36.55	\$7.30	\$13.40	\$0.00	\$57.25
	12/01/2016	\$37.55	\$7.30	\$13.40	\$0.00	\$58.25

For apprentice rates see "Apprentice- LABORER"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
CARBIDE CORE DRILL OPERATOR <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75
For apprentice rates see "Apprentice- LABORER"						
CARPENTER <i>CARPENTERS -ZONE 2 (Eastern Massachusetts)</i>	03/01/2015	\$35.75	\$9.80	\$16.48	\$0.00	\$62.03

Apprentice - CARPENTER - Zone 2 Eastern MA

Effective Date - 03/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$17.88	\$9.80	\$1.63	\$0.00	\$29.31
2	60	\$21.45	\$9.80	\$1.63	\$0.00	\$32.88
3	70	\$25.03	\$9.80	\$11.59	\$0.00	\$46.42
4	75	\$26.81	\$9.80	\$11.59	\$0.00	\$48.20
5	80	\$28.60	\$9.80	\$13.22	\$0.00	\$51.62
6	80	\$28.60	\$9.80	\$13.22	\$0.00	\$51.62
7	90	\$32.18	\$9.80	\$14.85	\$0.00	\$56.83
8	90	\$32.18	\$9.80	\$14.85	\$0.00	\$56.83

Notes:

Apprentice to Journeyworker Ratio:1:5

CEMENT MASONRY/PLASTERING <i>BRICKLAYERS LOCAL 3 (LOWELL)</i>	07/01/2015	\$42.87	\$10.90	\$18.71	\$1.30	\$73.78
	01/01/2016	\$43.51	\$10.90	\$18.71	\$1.30	\$74.42

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - CEMENT MASONRY/PLASTERING - Lowell

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$21.44	\$10.90	\$12.21	\$0.00	\$44.55
2	60	\$25.72	\$10.90	\$13.71	\$1.30	\$51.63
3	65	\$27.87	\$10.90	\$14.71	\$1.30	\$54.78
4	70	\$30.01	\$10.90	\$15.71	\$1.30	\$57.92
5	75	\$32.15	\$10.90	\$16.71	\$1.30	\$61.06
6	80	\$34.30	\$10.90	\$17.71	\$1.30	\$64.21
7	90	\$38.58	\$10.90	\$18.71	\$1.30	\$69.49

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$21.76	\$10.90	\$12.21	\$0.00	\$44.87
2	60	\$26.11	\$10.90	\$13.71	\$1.30	\$52.02
3	65	\$28.28	\$10.90	\$14.71	\$1.30	\$55.19
4	70	\$30.46	\$10.90	\$15.71	\$1.30	\$58.37
5	75	\$32.63	\$10.90	\$16.71	\$1.30	\$61.54
6	80	\$34.81	\$10.90	\$17.71	\$1.30	\$64.72
7	90	\$39.16	\$10.90	\$18.71	\$1.30	\$70.07

Notes:

Steps 3,4 are 500 hrs. All other steps are 1,000 hrs.

Apprentice to Journeyworker Ratio:1:3

CHAIN SAW OPERATOR LABORERS - ZONE 2	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

CLAM SHELLS/SLURRY BUCKETS/HEADING MACHINES OPERATING ENGINEERS LOCAL 4	06/01/2015	\$43.83	\$10.00	\$14.55	\$0.00	\$68.38
	12/01/2015	\$45.08	\$10.00	\$14.55	\$0.00	\$69.63
	06/01/2016	\$45.83	\$10.00	\$14.55	\$0.00	\$70.38
	12/01/2016	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	06/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
	12/01/2017	\$49.08	\$10.00	\$14.55	\$0.00	\$73.63

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

COMPRESSOR OPERATOR OPERATING ENGINEERS LOCAL 4	06/01/2015	\$29.61	\$10.00	\$14.55	\$0.00	\$54.16
	12/01/2015	\$30.48	\$10.00	\$14.55	\$0.00	\$55.03
	06/01/2016	\$31.00	\$10.00	\$14.55	\$0.00	\$55.55
	12/01/2016	\$31.87	\$10.00	\$14.55	\$0.00	\$56.42
	06/01/2017	\$32.56	\$10.00	\$14.55	\$0.00	\$57.11
	12/01/2017	\$33.25	\$10.00	\$14.55	\$0.00	\$57.80

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
DELEADER (BRIDGE) PAINTERS LOCAL 35 - ZONE 2	07/01/2015	\$48.56	\$7.85	\$16.10	\$0.00	\$72.51
	01/01/2016	\$49.51	\$7.85	\$16.10	\$0.00	\$73.46
	07/01/2016	\$50.46	\$7.85	\$16.10	\$0.00	\$74.41
	01/01/2017	\$51.41	\$7.85	\$16.10	\$0.00	\$75.36

Apprentice - PAINTER Local 35 - BRIDGES/TANKS

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.28	\$7.85	\$0.00	\$0.00	\$32.13
2	55	\$26.71	\$7.85	\$3.66	\$0.00	\$38.22
3	60	\$29.14	\$7.85	\$3.99	\$0.00	\$40.98
4	65	\$31.56	\$7.85	\$4.32	\$0.00	\$43.73
5	70	\$33.99	\$7.85	\$14.11	\$0.00	\$55.95
6	75	\$36.42	\$7.85	\$14.44	\$0.00	\$58.71
7	80	\$38.85	\$7.85	\$14.77	\$0.00	\$61.47
8	90	\$43.70	\$7.85	\$15.44	\$0.00	\$66.99

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.76	\$7.85	\$0.00	\$0.00	\$32.61
2	55	\$27.23	\$7.85	\$3.66	\$0.00	\$38.74
3	60	\$29.71	\$7.85	\$3.99	\$0.00	\$41.55
4	65	\$32.18	\$7.85	\$4.32	\$0.00	\$44.35
5	70	\$34.66	\$7.85	\$14.11	\$0.00	\$56.62
6	75	\$37.13	\$7.85	\$14.44	\$0.00	\$59.42
7	80	\$39.61	\$7.85	\$14.77	\$0.00	\$62.23
8	90	\$44.56	\$7.85	\$15.44	\$0.00	\$67.85

Notes:
Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

DEMO: ADZEMAN LABORERS - ZONE 2	06/01/2015	\$35.25	\$7.30	\$13.20	\$0.00	\$55.75
	12/01/2015	\$36.00	\$7.30	\$13.20	\$0.00	\$56.50
For apprentice rates see "Apprentice- LABORER"						
DEMO: BACKHOE/LOADER/HAMMER OPERATOR LABORERS - ZONE 2	06/01/2015	\$36.25	\$7.30	\$13.20	\$0.00	\$56.75
	12/01/2015	\$37.00	\$7.30	\$13.20	\$0.00	\$57.50
For apprentice rates see "Apprentice- LABORER"						
DEMO: BURNERS LABORERS - ZONE 2	06/01/2015	\$36.00	\$7.30	\$13.20	\$0.00	\$56.50
	12/01/2015	\$36.75	\$7.30	\$13.20	\$0.00	\$57.25
For apprentice rates see "Apprentice- LABORER"						
DEMO: CONCRETE CUTTER/SAWYER LABORERS - ZONE 2	06/01/2015	\$36.25	\$7.30	\$13.20	\$0.00	\$56.75
	12/01/2015	\$37.00	\$7.30	\$13.20	\$0.00	\$57.50
For apprentice rates see "Apprentice- LABORER"						
DEMO: JACKHAMMER OPERATOR LABORERS - ZONE 2	06/01/2015	\$36.00	\$7.30	\$13.20	\$0.00	\$56.50
	12/01/2015	\$36.75	\$7.30	\$13.20	\$0.00	\$57.25

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
For apprentice rates see "Apprentice- LABORER"						
DEMO: WRECKING LABORER <i>LABORERS - ZONE 2</i>	06/01/2015	\$35.25	\$7.30	\$13.20	\$0.00	\$55.75
	12/01/2015	\$36.00	\$7.30	\$13.20	\$0.00	\$56.50
For apprentice rates see "Apprentice- LABORER"						
DIRECTIONAL DRILL MACHINE OPERATOR <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
DIVER <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$58.86	\$9.80	\$19.23	\$0.00	\$87.89
DIVER TENDER <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$42.04	\$9.80	\$19.23	\$0.00	\$71.07
DIVER TENDER (EFFLUENT) <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$63.06	\$9.80	\$19.23	\$0.00	\$92.09
DIVER/SLURRY (EFFLUENT) <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$88.23	\$9.80	\$19.23	\$0.00	\$117.26
DRAWBRIDGE OPERATOR (Construction) <i>ELECTRICIANS LOCAL 103</i>	09/01/2015	\$45.67	\$13.00	\$15.89	\$0.00	\$74.56
	03/01/2016	\$46.17	\$13.00	\$16.39	\$0.00	\$75.56
For apprentice rates see "Apprentice- ELECTRICIAN"						
ELECTRICIAN <i>ELECTRICIANS LOCAL 103</i>	09/01/2015	\$45.67	\$13.00	\$15.89	\$0.00	\$74.56
	03/01/2016	\$46.17	\$13.00	\$16.39	\$0.00	\$75.56

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - ELECTRICIAN - Local 103

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$18.27	\$13.00	\$0.55	\$0.00	\$31.82
2	40	\$18.27	\$13.00	\$0.55	\$0.00	\$31.82
3	45	\$20.55	\$13.00	\$11.86	\$0.00	\$45.41
4	45	\$20.55	\$13.00	\$11.86	\$0.00	\$45.41
5	50	\$22.84	\$13.00	\$12.23	\$0.00	\$48.07
6	55	\$25.12	\$13.00	\$12.58	\$0.00	\$50.70
7	60	\$27.40	\$13.00	\$12.95	\$0.00	\$53.35
8	65	\$29.69	\$13.00	\$13.32	\$0.00	\$56.01
9	70	\$31.97	\$13.00	\$13.69	\$0.00	\$58.66
10	75	\$34.25	\$13.00	\$14.06	\$0.00	\$61.31

Effective Date - 03/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$18.47	\$13.00	\$0.55	\$0.00	\$32.02
2	40	\$18.47	\$13.00	\$0.55	\$0.00	\$32.02
3	45	\$20.78	\$13.00	\$11.84	\$0.00	\$45.62
4	45	\$20.78	\$13.00	\$11.84	\$0.00	\$45.62
5	50	\$23.09	\$13.00	\$12.71	\$0.00	\$48.80
6	55	\$25.39	\$13.00	\$13.07	\$0.00	\$51.46
7	60	\$27.70	\$13.00	\$13.39	\$0.00	\$54.09
8	65	\$30.01	\$13.00	\$13.81	\$0.00	\$56.82
9	70	\$32.32	\$13.00	\$14.18	\$0.00	\$59.50
10	75	\$34.63	\$13.00	\$14.55	\$0.00	\$62.18

Notes :
App Prior 1/1/03; 30/35/40/45/50/55/65/70/75/80

Apprentice to Journeyworker Ratio:2:3***

ELEVATOR CONSTRUCTOR	01/01/2015	\$53.30	\$13.58	\$14.21	\$0.00	\$81.09
ELEVATOR CONSTRUCTORS LOCAL 4	01/01/2016	\$54.53	\$14.43	\$14.96	\$0.00	\$83.92
	01/01/2017	\$55.86	\$15.28	\$15.71	\$0.00	\$86.85

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - ELEVATOR CONSTRUCTOR - Local 4

Effective Date - 01/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$26.65	\$13.58	\$0.00	\$0.00	\$40.23
2	55	\$29.32	\$13.58	\$14.21	\$0.00	\$57.11
3	65	\$34.65	\$13.58	\$14.21	\$0.00	\$62.44
4	70	\$37.31	\$13.58	\$14.21	\$0.00	\$65.10
5	80	\$42.64	\$13.58	\$14.21	\$0.00	\$70.43

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$27.27	\$14.43	\$0.00	\$0.00	\$41.70
2	55	\$29.99	\$14.43	\$14.96	\$0.00	\$59.38
3	65	\$35.44	\$14.43	\$14.96	\$0.00	\$64.83
4	70	\$38.17	\$14.43	\$14.96	\$0.00	\$67.56
5	80	\$43.62	\$14.43	\$14.96	\$0.00	\$73.01

Notes:

Steps 1-2 are 6 mos.; Steps 3-5 are 1 year

Apprentice to Journeyworker Ratio:1:1

ELEVATOR CONSTRUCTOR HELPER <i>ELEVATOR CONSTRUCTORS LOCAL 4</i>	01/01/2015	\$37.31	\$13.58	\$14.21	\$0.00	\$65.10
	01/01/2016	\$38.17	\$14.43	\$14.96	\$0.00	\$67.56
	01/01/2017	\$39.10	\$15.28	\$15.71	\$0.00	\$70.09

For apprentice rates see "Apprentice - ELEVATOR CONSTRUCTOR"

FENCE & GUARD RAIL ERECTOR <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

FIELD ENG.INST.PERSON-BLDG,SITE,HVY/HWY <i>OPERATING ENGINEERS LOCAL 4</i>	05/01/2015	\$40.22	\$10.00	\$14.30	\$0.00	\$64.52
	11/01/2015	\$40.49	\$10.00	\$14.55	\$0.00	\$65.04
	05/01/2016	\$41.38	\$10.00	\$14.55	\$0.00	\$65.93
	11/01/2016	\$41.97	\$10.00	\$14.55	\$0.00	\$66.52
	05/01/2017	\$42.85	\$10.00	\$14.55	\$0.00	\$67.40
	11/01/2017	\$43.58	\$10.00	\$14.55	\$0.00	\$68.13
	05/01/2018	\$44.29	\$10.00	\$14.55	\$0.00	\$68.84

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

FIELD ENG.PARTY CHIEF-BLDG,SITE,HVY/HWY <i>OPERATING ENGINEERS LOCAL 4</i>	05/01/2015	\$41.65	\$10.00	\$14.30	\$0.00	\$65.95
	11/01/2015	\$41.93	\$10.00	\$14.55	\$0.00	\$66.48
	05/01/2016	\$42.82	\$10.00	\$14.55	\$0.00	\$67.37
	11/01/2016	\$43.42	\$10.00	\$14.55	\$0.00	\$67.97
	05/01/2017	\$44.31	\$10.00	\$14.55	\$0.00	\$68.86
	11/01/2017	\$45.04	\$10.00	\$14.55	\$0.00	\$69.59
	05/01/2018	\$45.76	\$10.00	\$14.55	\$0.00	\$70.31

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
FIELD ENG.ROD PERSON-BLDG,SITE,HVY/HWY <i>OPERATING ENGINEERS LOCAL 4</i>	05/01/2015	\$21.68	\$10.00	\$14.30	\$0.00	\$45.98
	11/01/2015	\$21.71	\$10.00	\$14.55	\$0.00	\$46.26
	05/01/2016	\$22.23	\$10.00	\$14.55	\$0.00	\$46.78
	11/01/2016	\$22.58	\$10.00	\$14.55	\$0.00	\$47.13
	05/01/2017	\$23.11	\$10.00	\$14.55	\$0.00	\$47.66
	11/01/2017	\$23.53	\$10.00	\$14.55	\$0.00	\$48.08
	05/01/2018	\$23.96	\$10.00	\$14.55	\$0.00	\$48.51
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
FIRE ALARM INSTALLER <i>ELECTRICIANS LOCAL 103</i>	09/01/2015	\$45.67	\$13.00	\$15.89	\$0.00	\$74.56
	03/01/2016	\$46.17	\$13.00	\$16.39	\$0.00	\$75.56
For apprentice rates see "Apprentice- ELECTRICIAN"						
FIRE ALARM REPAIR / MAINTENANCE <i>LOCAL 103</i> / COMMISSIONING <i>ELECTRICIANS</i>	09/01/2015	\$34.25	\$13.00	\$14.06	\$0.00	\$61.31
	03/01/2016	\$34.63	\$13.00	\$14.55	\$0.00	\$62.18
For apprentice rates see "Apprentice- TELECOMMUNICATIONS TECHNICIAN"						
FIREMAN (ASST. ENGINEER) <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$35.64	\$10.00	\$14.55	\$0.00	\$60.19
	12/01/2015	\$36.69	\$10.00	\$14.55	\$0.00	\$61.24
	06/01/2016	\$37.31	\$10.00	\$14.55	\$0.00	\$61.86
	12/01/2016	\$38.35	\$10.00	\$14.55	\$0.00	\$62.90
	06/01/2017	\$39.19	\$10.00	\$14.55	\$0.00	\$63.74
	12/01/2017	\$40.02	\$10.00	\$14.55	\$0.00	\$64.57
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
FLAGGER & SIGNALER <i>LABORERS - ZONE 2</i>	06/01/2015	\$20.50	\$7.30	\$12.30	\$0.00	\$40.10
	12/01/2015	\$20.50	\$7.30	\$12.30	\$0.00	\$40.10
	06/01/2016	\$20.50	\$7.30	\$12.30	\$0.00	\$40.10
	12/01/2016	\$20.50	\$7.30	\$12.30	\$0.00	\$40.10
For apprentice rates see "Apprentice- LABORER"						
FLOORCOVERER <i>FLOORCOVERERS LOCAL 2168 ZONE 1</i>	09/01/2015	\$41.59	\$9.80	\$17.53	\$0.00	\$68.92

Apprentice - FLOORCOVERER - Local 2168 Zone 1

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$20.80	\$9.80	\$1.79	\$0.00	\$32.39
2	55	\$22.87	\$9.80	\$1.79	\$0.00	\$34.46
3	60	\$24.95	\$9.80	\$12.16	\$0.00	\$46.91
4	65	\$27.03	\$9.80	\$12.16	\$0.00	\$48.99
5	70	\$29.11	\$9.80	\$13.95	\$0.00	\$52.86
6	75	\$31.19	\$9.80	\$13.95	\$0.00	\$54.94
7	80	\$33.27	\$9.80	\$15.74	\$0.00	\$58.81
8	85	\$35.35	\$9.80	\$15.74	\$0.00	\$60.89

Notes:

Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
FORK LIFT/CHERRY PICKER <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
GENERATOR/LIGHTING PLANT/HEATERS <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$29.61	\$10.00	\$14.55	\$0.00	\$54.16
	12/01/2015	\$30.48	\$10.00	\$14.55	\$0.00	\$55.03
	06/01/2016	\$31.00	\$10.00	\$14.55	\$0.00	\$55.55
	12/01/2016	\$31.87	\$10.00	\$14.55	\$0.00	\$56.42
	06/01/2017	\$32.56	\$10.00	\$14.55	\$0.00	\$57.11
	12/01/2017	\$33.25	\$10.00	\$14.55	\$0.00	\$57.80
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
GLAZIER (GLASS PLANK/AIR BARRIER/INTERIOR SYSTEMS) <i>GLAZIERS LOCAL 35 (ZONE 2)</i>	07/01/2015	\$38.06	\$7.85	\$16.10	\$0.00	\$62.01
	01/01/2016	\$39.01	\$7.85	\$16.10	\$0.00	\$62.96
	07/01/2016	\$39.96	\$7.85	\$16.10	\$0.00	\$63.91
	01/01/2017	\$40.91	\$7.85	\$16.10	\$0.00	\$64.86

Apprentice - GLAZIER - Local 35 Zone 2

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.03	\$7.85	\$0.00	\$0.00	\$26.88
2	55	\$20.93	\$7.85	\$3.66	\$0.00	\$32.44
3	60	\$22.84	\$7.85	\$3.99	\$0.00	\$34.68
4	65	\$24.74	\$7.85	\$4.32	\$0.00	\$36.91
5	70	\$26.64	\$7.85	\$14.11	\$0.00	\$48.60
6	75	\$28.55	\$7.85	\$14.44	\$0.00	\$50.84
7	80	\$30.45	\$7.85	\$14.77	\$0.00	\$53.07
8	90	\$34.25	\$7.85	\$15.44	\$0.00	\$57.54

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.51	\$7.85	\$0.00	\$0.00	\$27.36
2	55	\$21.46	\$7.85	\$3.66	\$0.00	\$32.97
3	60	\$23.41	\$7.85	\$3.99	\$0.00	\$35.25
4	65	\$25.36	\$7.85	\$4.32	\$0.00	\$37.53
5	70	\$27.31	\$7.85	\$14.11	\$0.00	\$49.27
6	75	\$29.26	\$7.85	\$14.44	\$0.00	\$51.55
7	80	\$31.21	\$7.85	\$14.77	\$0.00	\$53.83
8	90	\$35.11	\$7.85	\$15.44	\$0.00	\$58.40

Notes:

Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
HOISTING ENGINEER/CRANES/GRADALLS <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63

Apprentice - OPERATING ENGINEERS - Local 4

Effective Date - 06/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	55	\$23.56	\$10.00	\$0.00	\$0.00	\$33.56
2	60	\$25.70	\$10.00	\$14.55	\$0.00	\$50.25
3	65	\$27.84	\$10.00	\$14.55	\$0.00	\$52.39
4	70	\$29.98	\$10.00	\$14.55	\$0.00	\$54.53
5	75	\$32.12	\$10.00	\$14.55	\$0.00	\$56.67
6	80	\$34.26	\$10.00	\$14.55	\$0.00	\$58.81
7	85	\$36.41	\$10.00	\$14.55	\$0.00	\$60.96
8	90	\$38.55	\$10.00	\$14.55	\$0.00	\$63.10

Effective Date - 12/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	55	\$24.24	\$10.00	\$0.00	\$0.00	\$34.24
2	60	\$26.45	\$10.00	\$14.55	\$0.00	\$51.00
3	65	\$28.65	\$10.00	\$14.55	\$0.00	\$53.20
4	70	\$30.86	\$10.00	\$14.55	\$0.00	\$55.41
5	75	\$33.06	\$10.00	\$14.55	\$0.00	\$57.61
6	80	\$35.26	\$10.00	\$14.55	\$0.00	\$59.81
7	85	\$37.47	\$10.00	\$14.55	\$0.00	\$62.02
8	90	\$39.67	\$10.00	\$14.55	\$0.00	\$64.22

Notes:

Apprentice to Journeyworker Ratio:1:6

HVAC (DUCTWORK) <i>SHEETMETAL WORKERS LOCAL 17 - A</i>	08/01/2015	\$43.31	\$10.20	\$21.48	\$2.25	\$77.24
	02/01/2016	\$44.31	\$10.20	\$21.48	\$2.25	\$78.24
	08/01/2016	\$45.46	\$10.20	\$21.48	\$2.25	\$79.39
	02/01/2017	\$46.56	\$10.20	\$21.48	\$2.25	\$80.49
	08/01/2017	\$47.66	\$10.20	\$21.48	\$2.25	\$81.59
	02/01/2018	\$48.81	\$10.20	\$21.48	\$2.25	\$82.74

For apprentice rates see "Apprentice- SHEET METAL WORKER"

HVAC (ELECTRICAL CONTROLS) <i>ELECTRICIANS LOCAL 103</i>	09/01/2015	\$45.67	\$13.00	\$15.89	\$0.00	\$74.56
	03/01/2016	\$46.17	\$13.00	\$16.39	\$0.00	\$75.56

For apprentice rates see "Apprentice- ELECTRICIAN"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
HVAC (TESTING AND BALANCING - AIR) <i>SHEETMETAL WORKERS LOCAL 17 - A</i>	08/01/2015	\$43.31	\$10.20	\$21.48	\$2.25	\$77.24
	02/01/2016	\$44.31	\$10.20	\$21.48	\$2.25	\$78.24
	08/01/2016	\$45.46	\$10.20	\$21.48	\$2.25	\$79.39
	02/01/2017	\$46.56	\$10.20	\$21.48	\$2.25	\$80.49
	08/01/2017	\$47.66	\$10.20	\$21.48	\$2.25	\$81.59
	02/01/2018	\$48.81	\$10.20	\$21.48	\$2.25	\$82.74
For apprentice rates see "Apprentice- SHEET METAL WORKER"						
HVAC (TESTING AND BALANCING -WATER) <i>PIPEFITTERS LOCAL 537</i>	09/01/2015	\$49.69	\$9.70	\$16.89	\$0.00	\$76.28
	03/01/2016	\$50.69	\$9.70	\$16.89	\$0.00	\$77.28
	09/01/2016	\$51.69	\$9.70	\$16.89	\$0.00	\$78.28
	03/01/2017	\$52.69	\$9.70	\$16.89	\$0.00	\$79.28
For apprentice rates see "Apprentice- PIPEFITTER" or "PLUMBER/PIPEFITTER"						
HVAC MECHANIC <i>PIPEFITTERS LOCAL 537</i>	09/01/2015	\$49.69	\$9.70	\$16.89	\$0.00	\$76.28
	03/01/2016	\$50.69	\$9.70	\$16.89	\$0.00	\$77.28
	09/01/2016	\$51.69	\$9.70	\$16.89	\$0.00	\$78.28
	03/01/2017	\$52.69	\$9.70	\$16.89	\$0.00	\$79.28
For apprentice rates see "Apprentice- PIPEFITTER" or "PLUMBER/PIPEFITTER"						
HYDRAULIC DRILLS <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	12/01/2015	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	06/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50
	12/01/2016	\$33.65	\$7.30	\$12.30	\$0.00	\$53.25
For apprentice rates see "Apprentice- LABORER"						
INSULATOR (PIPES & TANKS) <i>HEAT & FROST INSULATORS LOCAL 6 (BOSTON)</i>	09/01/2015	\$43.81	\$11.50	\$13.80	\$0.00	\$69.11
	09/01/2016	\$45.81	\$11.50	\$13.80	\$0.00	\$71.11
	09/01/2017	\$47.81	\$11.50	\$13.80	\$0.00	\$73.11
	09/01/2018	\$50.06	\$11.50	\$13.80	\$0.00	\$75.36
	09/01/2019	\$52.56	\$11.50	\$13.80	\$0.00	\$77.86

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - ASBESTOS INSULATOR (Pipes & Tanks) - Local 6 Boston

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$21.91	\$11.50	\$10.05	\$0.00	\$43.46
2	60	\$26.29	\$11.50	\$10.80	\$0.00	\$48.59
3	70	\$30.67	\$11.50	\$11.55	\$0.00	\$53.72
4	80	\$35.05	\$11.50	\$12.30	\$0.00	\$58.85

Effective Date - 09/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$22.91	\$11.50	\$10.05	\$0.00	\$44.46
2	60	\$27.49	\$11.50	\$10.80	\$0.00	\$49.79
3	70	\$32.07	\$11.50	\$11.55	\$0.00	\$55.12
4	80	\$36.65	\$11.50	\$12.30	\$0.00	\$60.45

Notes:

Steps are 1 year

Apprentice to Journeyworker Ratio:1:4

IRONWORKER/WELDER	09/16/2015	\$37.99	\$7.80	\$20.85	\$0.00	\$66.64
IRONWORKERS LOCAL 7 (LAWRENCE AREA)	03/16/2016	\$38.99	\$7.80	\$20.85	\$0.00	\$67.64
	09/16/2016	\$39.64	\$7.80	\$20.85	\$0.00	\$68.29
	03/16/2017	\$40.24	\$7.80	\$20.85	\$0.00	\$68.89

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - IRONWORKER - Local 7 Lawrence

Effective Date - 09/16/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	60	\$22.79	\$7.80	\$20.85	\$0.00	\$51.44
2	70	\$26.59	\$7.80	\$20.85	\$0.00	\$55.24
3	75	\$28.49	\$7.80	\$20.85	\$0.00	\$57.14
4	80	\$30.39	\$7.80	\$20.85	\$0.00	\$59.04
5	85	\$32.29	\$7.80	\$20.85	\$0.00	\$60.94
6	90	\$34.19	\$7.80	\$20.85	\$0.00	\$62.84

Effective Date - 03/16/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	60	\$23.39	\$7.80	\$20.85	\$0.00	\$52.04
2	70	\$27.29	\$7.80	\$20.85	\$0.00	\$55.94
3	75	\$29.24	\$7.80	\$20.85	\$0.00	\$57.89
4	80	\$31.19	\$7.80	\$20.85	\$0.00	\$59.84
5	85	\$33.14	\$7.80	\$20.85	\$0.00	\$61.79
6	90	\$35.09	\$7.80	\$20.85	\$0.00	\$63.74

Notes:

Structural 1:6; Ornamental 1:4

Apprentice to Journeyworker Ratio:

JACKHAMMER & PAVING BREAKER OPERATOR LABORERS - ZONE 2	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

LABORER LABORERS - ZONE 2	06/01/2015	\$31.15	\$7.30	\$12.30	\$0.00	\$50.75
	12/01/2015	\$31.65	\$7.30	\$12.30	\$0.00	\$51.25
	06/01/2016	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - LABORER - Zone 2

Effective Date - 06/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	60	\$18.69	\$7.30	\$12.30	\$0.00	\$38.29
2	70	\$21.81	\$7.30	\$12.30	\$0.00	\$41.41
3	80	\$24.92	\$7.30	\$12.30	\$0.00	\$44.52
4	90	\$28.04	\$7.30	\$12.30	\$0.00	\$47.64

Effective Date - 12/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	60	\$18.99	\$7.30	\$12.30	\$0.00	\$38.59
2	70	\$22.16	\$7.30	\$12.30	\$0.00	\$41.76
3	80	\$25.32	\$7.30	\$12.30	\$0.00	\$44.92
4	90	\$28.49	\$7.30	\$12.30	\$0.00	\$48.09

Notes:

Apprentice to Journeyworker Ratio:1:5

LABORER: CARPENTER TENDER LABORERS - ZONE 2	06/01/2015	\$31.15	\$7.30	\$12.30	\$0.00	\$50.75
	12/01/2015	\$31.65	\$7.30	\$12.30	\$0.00	\$51.25
	06/01/2016	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50

For apprentice rates see "Apprentice- LABORER"

LABORER: CEMENT FINISHER TENDER LABORERS - ZONE 2	06/01/2015	\$31.15	\$7.30	\$12.30	\$0.00	\$50.75
	12/01/2015	\$31.65	\$7.30	\$12.30	\$0.00	\$51.25
	06/01/2016	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50

For apprentice rates see "Apprentice- LABORER"

LABORER: HAZARDOUS WASTE/ASBESTOS REMOVER LABORERS - ZONE 2	06/01/2015	\$31.35	\$7.30	\$12.25	\$0.00	\$50.90
	12/01/2015	\$31.85	\$7.30	\$12.25	\$0.00	\$51.40

For apprentice rates see "Apprentice- LABORER"

LABORER: MASON TENDER LABORERS - ZONE 2	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

LABORER: MULTI-TRADE TENDER LABORERS - ZONE 2	06/01/2015	\$31.15	\$7.30	\$12.30	\$0.00	\$50.75
	12/01/2015	\$31.65	\$7.30	\$12.30	\$0.00	\$51.25
	06/01/2016	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50

For apprentice rates see "Apprentice- LABORER"

LABORER: TREE REMOVER LABORERS - ZONE 2	06/01/2015	\$31.15	\$7.30	\$12.30	\$0.00	\$50.75
	12/01/2015	\$31.65	\$7.30	\$12.30	\$0.00	\$51.25
	06/01/2016	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50

Classification Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate
 This classification applies to all tree work associated with the removal of standing trees, and trimming and removal of branches and limbs when the work is not done for a utility company for the purpose of operation, maintenance or repair of utility company equipment. For apprentice rates see "Apprentice- LABORER"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
LASER BEAM OPERATOR LABORERS - ZONE 2	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
MARBLE & TILE FINISHERS BRICKLAYERS LOCAL 3 - MARBLE & TILE	08/01/2015	\$38.08	\$10.18	\$17.25	\$0.00	\$65.51
	02/01/2016	\$38.53	\$10.18	\$17.25	\$0.00	\$65.96
	08/01/2016	\$39.23	\$10.18	\$17.33	\$0.00	\$66.74
	02/01/2017	\$39.69	\$10.18	\$17.33	\$0.00	\$67.20

Apprentice - MARBLE & TILE FINISHER - Local 3 Marble & Tile

Effective Date - 08/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.04	\$10.18	\$17.25	\$0.00	\$46.47
2	60	\$22.85	\$10.18	\$17.25	\$0.00	\$50.28
3	70	\$26.66	\$10.18	\$17.25	\$0.00	\$54.09
4	80	\$30.46	\$10.18	\$17.25	\$0.00	\$57.89
5	90	\$34.27	\$10.18	\$17.25	\$0.00	\$61.70

Effective Date - 02/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.27	\$10.18	\$17.25	\$0.00	\$46.70
2	60	\$23.12	\$10.18	\$17.25	\$0.00	\$50.55
3	70	\$26.97	\$10.18	\$17.25	\$0.00	\$54.40
4	80	\$30.82	\$10.18	\$17.25	\$0.00	\$58.25
5	90	\$34.68	\$10.18	\$17.25	\$0.00	\$62.11

Notes:

Apprentice to Journeyworker Ratio:1:3

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
MARBLE MASONS, TILELAYERS & TERRAZZO MECH BRICKLAYERS LOCAL 3 - MARBLE & TILE	08/01/2015	\$49.90	\$10.18	\$18.57	\$0.00	\$78.65
	02/01/2016	\$50.47	\$10.18	\$18.57	\$0.00	\$79.22
	08/01/2016	\$51.37	\$10.18	\$18.65	\$0.00	\$80.20
	02/01/2017	\$51.94	\$10.18	\$18.65	\$0.00	\$80.77

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - MARBLE-TILE-TERRAZZO MECHANIC - Local 3 Marble & Tile

Effective Date - 08/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.95	\$10.18	\$18.57	\$0.00	\$53.70
2	60	\$29.94	\$10.18	\$18.57	\$0.00	\$58.69
3	70	\$34.93	\$10.18	\$18.57	\$0.00	\$63.68
4	80	\$39.92	\$10.18	\$18.57	\$0.00	\$68.67
5	90	\$44.91	\$10.18	\$18.57	\$0.00	\$73.66

Effective Date - 02/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$25.24	\$10.18	\$18.57	\$0.00	\$53.99
2	60	\$30.28	\$10.18	\$18.57	\$0.00	\$59.03
3	70	\$35.33	\$10.18	\$18.57	\$0.00	\$64.08
4	80	\$40.38	\$10.18	\$18.57	\$0.00	\$69.13
5	90	\$45.42	\$10.18	\$18.57	\$0.00	\$74.17

Notes:

Apprentice to Journeyworker Ratio:1:5

MECH. SWEEPER OPERATOR (ON CONST. SITES) <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
MECHANICS MAINTENANCE <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
MILLWRIGHT (Zone 2) <i>MILLWRIGHTS LOCAL 1121 - Zone 2</i>	04/01/2015	\$34.69	\$9.80	\$16.21	\$0.00	\$60.70

Apprentice - MILLWRIGHT - Local 1121 Zone 2

Effective Date - 04/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	55	\$19.08	\$9.80	\$4.48	\$0.00	\$33.36
2	65	\$22.55	\$9.80	\$13.36	\$0.00	\$45.71
3	75	\$26.02	\$9.80	\$14.18	\$0.00	\$50.00
4	85	\$29.49	\$9.80	\$14.99	\$0.00	\$54.28

Notes:

Steps are 2,000 hours

Apprentice to Journeyworker Ratio:1:5

MORTAR MIXER LABORERS - ZONE 2	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

OILER (OTHER THAN TRUCK CRANES,GRADALLS) OPERATING ENGINEERS LOCAL 4	06/01/2015	\$21.97	\$10.00	\$14.55	\$0.00	\$46.52
	12/01/2015	\$22.62	\$10.00	\$14.55	\$0.00	\$47.17
	06/01/2016	\$23.01	\$10.00	\$14.55	\$0.00	\$47.56
	12/01/2016	\$23.66	\$10.00	\$14.55	\$0.00	\$48.21
	06/01/2017	\$24.17	\$10.00	\$14.55	\$0.00	\$48.72
	12/01/2017	\$24.69	\$10.00	\$14.55	\$0.00	\$49.24

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

OILER (TRUCK CRANES, GRADALLS) OPERATING ENGINEERS LOCAL 4	06/01/2015	\$25.68	\$10.00	\$14.55	\$0.00	\$50.23
	12/01/2015	\$26.43	\$10.00	\$14.55	\$0.00	\$50.98
	06/01/2016	\$26.89	\$10.00	\$14.55	\$0.00	\$51.44
	12/01/2016	\$27.64	\$10.00	\$14.55	\$0.00	\$52.19
	06/01/2017	\$28.24	\$10.00	\$14.55	\$0.00	\$52.79
	12/01/2017	\$28.85	\$10.00	\$14.55	\$0.00	\$53.40

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

OTHER POWER DRIVEN EQUIPMENT - CLASS II OPERATING ENGINEERS LOCAL 4	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

PAINTER (BRIDGES/TANKS) PAINTERS LOCAL 35 - ZONE 2	07/01/2015	\$48.56	\$7.85	\$16.10	\$0.00	\$72.51
	01/01/2016	\$49.51	\$7.85	\$16.10	\$0.00	\$73.46
	07/01/2016	\$50.46	\$7.85	\$16.10	\$0.00	\$74.41
	01/01/2017	\$51.41	\$7.85	\$16.10	\$0.00	\$75.36

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - PAINTER Local 35 - BRIDGES/TANKS

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.28	\$7.85	\$0.00	\$0.00	\$32.13
2	55	\$26.71	\$7.85	\$3.66	\$0.00	\$38.22
3	60	\$29.14	\$7.85	\$3.99	\$0.00	\$40.98
4	65	\$31.56	\$7.85	\$4.32	\$0.00	\$43.73
5	70	\$33.99	\$7.85	\$14.11	\$0.00	\$55.95
6	75	\$36.42	\$7.85	\$14.44	\$0.00	\$58.71
7	80	\$38.85	\$7.85	\$14.77	\$0.00	\$61.47
8	90	\$43.70	\$7.85	\$15.44	\$0.00	\$66.99

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.76	\$7.85	\$0.00	\$0.00	\$32.61
2	55	\$27.23	\$7.85	\$3.66	\$0.00	\$38.74
3	60	\$29.71	\$7.85	\$3.99	\$0.00	\$41.55
4	65	\$32.18	\$7.85	\$4.32	\$0.00	\$44.35
5	70	\$34.66	\$7.85	\$14.11	\$0.00	\$56.62
6	75	\$37.13	\$7.85	\$14.44	\$0.00	\$59.42
7	80	\$39.61	\$7.85	\$14.77	\$0.00	\$62.23
8	90	\$44.56	\$7.85	\$15.44	\$0.00	\$67.85

Notes:
Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

PAINTER (SPRAY OR SANDBLAST, NEW) *	07/01/2015	\$39.46	\$7.85	\$16.10	\$0.00	\$63.41
* If 30% or more of surfaces to be painted are new construction, NEW paint rate shall be used. PAINTERS LOCAL 35 - ZONE 2	01/01/2016	\$40.41	\$7.85	\$16.10	\$0.00	\$64.36
	07/01/2016	\$41.36	\$7.85	\$16.10	\$0.00	\$65.31
	01/01/2017	\$42.31	\$7.85	\$16.10	\$0.00	\$66.26

Apprentice - PAINTER Local 35 Zone 2 - Spray/Sandblast - New

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.73	\$7.85	\$0.00	\$0.00	\$27.58
2	55	\$21.70	\$7.85	\$3.66	\$0.00	\$33.21
3	60	\$23.68	\$7.85	\$3.99	\$0.00	\$35.52
4	65	\$25.65	\$7.85	\$4.32	\$0.00	\$37.82
5	70	\$27.62	\$7.85	\$14.11	\$0.00	\$49.58
6	75	\$29.60	\$7.85	\$14.44	\$0.00	\$51.89
7	80	\$31.57	\$7.85	\$14.77	\$0.00	\$54.19
8	90	\$35.51	\$7.85	\$15.44	\$0.00	\$58.80

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$20.21	\$7.85	\$0.00	\$0.00	\$28.06
2	55	\$22.23	\$7.85	\$3.66	\$0.00	\$33.74
3	60	\$24.25	\$7.85	\$3.99	\$0.00	\$36.09
4	65	\$26.27	\$7.85	\$4.32	\$0.00	\$38.44
5	70	\$28.29	\$7.85	\$14.11	\$0.00	\$50.25
6	75	\$30.31	\$7.85	\$14.44	\$0.00	\$52.60
7	80	\$32.33	\$7.85	\$14.77	\$0.00	\$54.95
8	90	\$36.37	\$7.85	\$15.44	\$0.00	\$59.66

Notes:
Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

PAINTER (SPRAY OR SANDBLAST, REPAINT)	07/01/2015	\$37.52	\$7.85	\$16.10	\$0.00	\$61.47
PAINTERS LOCAL 35 - ZONE 2	01/01/2016	\$38.47	\$7.85	\$16.10	\$0.00	\$62.42
	07/01/2016	\$39.42	\$7.85	\$16.10	\$0.00	\$63.37
	01/01/2017	\$40.37	\$7.85	\$16.10	\$0.00	\$64.32

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - PAINTER Local 35 Zone 2 - Spray/Sandblast - Repaint

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$18.76	\$7.85	\$0.00	\$0.00	\$26.61
2	55	\$20.64	\$7.85	\$3.66	\$0.00	\$32.15
3	60	\$22.51	\$7.85	\$3.99	\$0.00	\$34.35
4	65	\$24.39	\$7.85	\$4.32	\$0.00	\$36.56
5	70	\$26.26	\$7.85	\$14.11	\$0.00	\$48.22
6	75	\$28.14	\$7.85	\$14.44	\$0.00	\$50.43
7	80	\$30.02	\$7.85	\$14.77	\$0.00	\$52.64
8	90	\$33.77	\$7.85	\$15.44	\$0.00	\$57.06

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.24	\$7.85	\$0.00	\$0.00	\$27.09
2	55	\$21.16	\$7.85	\$3.66	\$0.00	\$32.67
3	60	\$23.08	\$7.85	\$3.99	\$0.00	\$34.92
4	65	\$25.01	\$7.85	\$4.32	\$0.00	\$37.18
5	70	\$26.93	\$7.85	\$14.11	\$0.00	\$48.89
6	75	\$28.85	\$7.85	\$14.44	\$0.00	\$51.14
7	80	\$30.78	\$7.85	\$14.77	\$0.00	\$53.40
8	90	\$34.62	\$7.85	\$15.44	\$0.00	\$57.91

Notes:
Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

PAINTER (TRAFFIC MARKINGS) LABORERS - ZONE 2	06/01/2015	\$31.15	\$7.30	\$12.30	\$0.00	\$50.75
	12/01/2015	\$31.65	\$7.30	\$12.30	\$0.00	\$51.25
	06/01/2016	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2016	\$32.90	\$7.30	\$12.30	\$0.00	\$52.50

For Apprentice rates see "Apprentice- LABORER"

PAINTER / TAPER (BRUSH, NEW) *	07/01/2015	\$38.06	\$7.85	\$16.10	\$0.00	\$62.01
* If 30% or more of surfaces to be painted are new construction, NEW paint rate shall be used. PAINTERS LOCAL 35 - ZONE 2	01/01/2016	\$39.01	\$7.85	\$16.10	\$0.00	\$62.96
	07/01/2016	\$39.96	\$7.85	\$16.10	\$0.00	\$63.91
	01/01/2017	\$40.91	\$7.85	\$16.10	\$0.00	\$64.86

Apprentice - PAINTER - Local 35 Zone 2 - BRUSH NEW

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.03	\$7.85	\$0.00	\$0.00	\$26.88
2	55	\$20.93	\$7.85	\$3.66	\$0.00	\$32.44
3	60	\$22.84	\$7.85	\$3.99	\$0.00	\$34.68
4	65	\$24.74	\$7.85	\$4.32	\$0.00	\$36.91
5	70	\$26.64	\$7.85	\$14.11	\$0.00	\$48.60
6	75	\$28.55	\$7.85	\$14.44	\$0.00	\$50.84
7	80	\$30.45	\$7.85	\$14.77	\$0.00	\$53.07
8	90	\$34.25	\$7.85	\$15.44	\$0.00	\$57.54

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$19.51	\$7.85	\$0.00	\$0.00	\$27.36
2	55	\$21.46	\$7.85	\$3.66	\$0.00	\$32.97
3	60	\$23.41	\$7.85	\$3.99	\$0.00	\$35.25
4	65	\$25.36	\$7.85	\$4.32	\$0.00	\$37.53
5	70	\$27.31	\$7.85	\$14.11	\$0.00	\$49.27
6	75	\$29.26	\$7.85	\$14.44	\$0.00	\$51.55
7	80	\$31.21	\$7.85	\$14.77	\$0.00	\$53.83
8	90	\$35.11	\$7.85	\$15.44	\$0.00	\$58.40

Notes:
Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

PAINTER / TAPER (BRUSH, REPAINT)	07/01/2015	\$36.12	\$7.85	\$16.10	\$0.00	\$60.07
PAINTERS LOCAL 35 - ZONE 2	01/01/2016	\$37.07	\$7.85	\$16.10	\$0.00	\$61.02
	07/01/2016	\$38.02	\$7.85	\$16.10	\$0.00	\$61.97
	01/01/2017	\$38.97	\$7.85	\$16.10	\$0.00	\$62.92

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - PAINTER Local 35 Zone 2 - BRUSH REPAINT

Effective Date - 07/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$18.06	\$7.85	\$0.00	\$0.00	\$25.91
2	55	\$19.87	\$7.85	\$3.66	\$0.00	\$31.38
3	60	\$21.67	\$7.85	\$3.99	\$0.00	\$33.51
4	65	\$23.48	\$7.85	\$4.32	\$0.00	\$35.65
5	70	\$25.28	\$7.85	\$14.11	\$0.00	\$47.24
6	75	\$27.09	\$7.85	\$14.44	\$0.00	\$49.38
7	80	\$28.90	\$7.85	\$14.77	\$0.00	\$51.52
8	90	\$32.51	\$7.85	\$15.44	\$0.00	\$55.80

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$18.54	\$7.85	\$0.00	\$0.00	\$26.39
2	55	\$20.39	\$7.85	\$3.66	\$0.00	\$31.90
3	60	\$22.24	\$7.85	\$3.99	\$0.00	\$34.08
4	65	\$24.10	\$7.85	\$4.32	\$0.00	\$36.27
5	70	\$25.95	\$7.85	\$14.11	\$0.00	\$47.91
6	75	\$27.80	\$7.85	\$14.44	\$0.00	\$50.09
7	80	\$29.66	\$7.85	\$14.77	\$0.00	\$52.28
8	90	\$33.36	\$7.85	\$15.44	\$0.00	\$56.65

Notes:

Steps are 750 hrs.

Apprentice to Journeyworker Ratio:1:1

PANEL & PICKUP TRUCKS DRIVER <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	12/01/2012	\$30.28	\$9.07	\$8.00	\$0.00	\$47.35
PIER AND DOCK CONSTRUCTOR (UNDERPINNING AND DECK) <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$42.04	\$9.80	\$19.23	\$0.00	\$71.07
PILE DRIVER <i>PILE DRIVER LOCAL 56 (ZONE 1)</i>	08/01/2015	\$42.04	\$9.80	\$19.23	\$0.00	\$71.07

Apprentice - PILE DRIVER - Local 56 Zone 1

Effective Date - 08/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$21.02	\$9.80	\$19.23	\$0.00	\$50.05
2	60	\$25.22	\$9.80	\$19.23	\$0.00	\$54.25
3	70	\$29.43	\$9.80	\$19.23	\$0.00	\$58.46
4	75	\$31.53	\$9.80	\$19.23	\$0.00	\$60.56
5	80	\$33.63	\$9.80	\$19.23	\$0.00	\$62.66
6	80	\$33.63	\$9.80	\$19.23	\$0.00	\$62.66
7	90	\$37.84	\$9.80	\$19.23	\$0.00	\$66.87
8	90	\$37.84	\$9.80	\$19.23	\$0.00	\$66.87

Notes:

Apprentice to Journeyworker Ratio:1:3

PIPEFITTER & STEAMFITTER	09/01/2015	\$49.69	\$9.70	\$16.89	\$0.00	\$76.28
PIPEFITTERS LOCAL 537	03/01/2016	\$50.69	\$9.70	\$16.89	\$0.00	\$77.28
	09/01/2016	\$51.69	\$9.70	\$16.89	\$0.00	\$78.28
	03/01/2017	\$52.69	\$9.70	\$16.89	\$0.00	\$79.28

Apprentice - PIPEFITTER - Local 537

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$19.88	\$9.70	\$7.50	\$0.00	\$37.08
2	45	\$22.36	\$9.70	\$16.89	\$0.00	\$48.95
3	60	\$29.81	\$9.70	\$16.89	\$0.00	\$56.40
4	70	\$34.78	\$9.70	\$16.89	\$0.00	\$61.37
5	80	\$39.75	\$9.70	\$16.89	\$0.00	\$66.34

Effective Date - 03/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$20.28	\$9.70	\$7.50	\$0.00	\$37.48
2	45	\$22.81	\$9.70	\$16.89	\$0.00	\$49.40
3	60	\$30.41	\$9.70	\$16.89	\$0.00	\$57.00
4	70	\$35.48	\$9.70	\$16.89	\$0.00	\$62.07
5	80	\$40.55	\$9.70	\$16.89	\$0.00	\$67.14

Notes:

** 1:3; 3:15; 1:10 thereafter / Steps are 1 yr.
Refrig/AC Mechanic **1:1;1:2;2:4;3:6;4:8;5:10;6:12;7:14;8:17;9:20;10:23(Max)

Apprentice to Journeyworker Ratio:**

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
PIPELAYER <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

PLUMBERS & GASFITTERS <i>PLUMBERS & GASFITTERS LOCAL 12</i>	09/01/2015	\$50.46	\$10.82	\$15.14	\$0.00	\$76.42
	03/01/2016	\$51.61	\$10.82	\$15.14	\$0.00	\$77.57
	09/01/2016	\$52.66	\$10.82	\$15.14	\$0.00	\$78.62
	03/01/2017	\$53.66	\$10.82	\$15.14	\$0.00	\$79.62

Apprentice - PLUMBER/GASFITTER - Local 12

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	35	\$17.66	\$10.82	\$5.63	\$0.00	\$34.11
2	40	\$20.18	\$10.82	\$6.37	\$0.00	\$37.37
3	55	\$27.75	\$10.82	\$8.56	\$0.00	\$47.13
4	65	\$32.80	\$10.82	\$10.03	\$0.00	\$53.65
5	75	\$37.85	\$10.82	\$11.48	\$0.00	\$60.15

Effective Date - 03/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	35	\$18.06	\$10.82	\$5.61	\$0.00	\$34.49
2	40	\$20.64	\$10.82	\$6.36	\$0.00	\$37.82
3	55	\$28.39	\$10.82	\$8.56	\$0.00	\$47.77
4	65	\$33.55	\$10.82	\$10.02	\$0.00	\$54.39
5	75	\$38.71	\$10.82	\$11.48	\$0.00	\$61.01

Notes:

** 1:2; 2:6; 3:10; 4:14; 5:19/Steps are 1 yr
Step4 with lic\$56.90 Step5 with lic\$63.40

Apprentice to Journeyworker Ratio:**

PNEUMATIC CONTROLS (TEMP.) <i>PIPEFITTERS LOCAL 537</i>	09/01/2015	\$49.69	\$9.70	\$16.89	\$0.00	\$76.28
	03/01/2016	\$50.69	\$9.70	\$16.89	\$0.00	\$77.28
	09/01/2016	\$51.69	\$9.70	\$16.89	\$0.00	\$78.28
	03/01/2017	\$52.69	\$9.70	\$16.89	\$0.00	\$79.28

For apprentice rates see "Apprentice- PIPEFITTER" or "PLUMBER/PIPEFITTER"

PNEUMATIC DRILL/TOOL OPERATOR <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

POWDERMAN & BLASTER <i>LABORERS - ZONE 2</i>	06/01/2015	\$32.15	\$7.30	\$12.30	\$0.00	\$51.75
	12/01/2015	\$32.65	\$7.30	\$12.30	\$0.00	\$52.25
	06/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75
	12/01/2016	\$33.90	\$7.30	\$12.30	\$0.00	\$53.50

For apprentice rates see "Apprentice- LABORER"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
POWER SHOVEL/DERRICK/TRENCHING MACHINE <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
PUMP OPERATOR (CONCRETE) <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
PUMP OPERATOR (DEWATERING, OTHER) <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$29.61	\$10.00	\$14.55	\$0.00	\$54.16
	12/01/2015	\$30.48	\$10.00	\$14.55	\$0.00	\$55.03
	06/01/2016	\$31.00	\$10.00	\$14.55	\$0.00	\$55.55
	12/01/2016	\$31.87	\$10.00	\$14.55	\$0.00	\$56.42
	06/01/2017	\$32.56	\$10.00	\$14.55	\$0.00	\$57.11
	12/01/2017	\$33.25	\$10.00	\$14.55	\$0.00	\$57.80
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
READY-MIX CONCRETE DRIVER <i>TEAMSTERS LOCAL 49</i>	05/01/2010	\$22.88	\$6.97	\$3.94	\$0.00	\$33.79
RECLAIMERS <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
RESIDENTIAL WOOD FRAME (All Other Work) <i>CARPENTERS -ZONE 2 (Residential Wood)</i>	04/01/2011	\$24.24	\$8.67	\$15.51	\$0.00	\$48.42
RESIDENTIAL WOOD FRAME CARPENTER **	05/01/2011	\$24.24	\$6.34	\$6.23	\$0.00	\$36.81

** The Residential Wood Frame Carpenter classification applies only to the construction of new, wood frame residences that do not exceed four stories including the basement. *CARPENTERS -ZONE 2 (Residential Wood)*

As of 9/1/09 Carpentry work on wood-frame residential WEATHERIZATION projects shall be paid the RESIDENTIAL WOOD FRAME CARPENTER rate.

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - CARPENTER (Residential Wood Frame) - Zone 2

Effective Date - 05/01/2011

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	60	\$14.54	\$6.34	\$0.00	\$0.00	\$20.88
2	60	\$14.54	\$6.34	\$6.23	\$0.00	\$27.11
3	65	\$15.76	\$6.34	\$6.23	\$0.00	\$28.33
4	70	\$16.97	\$6.34	\$6.23	\$0.00	\$29.54
5	75	\$18.18	\$6.34	\$6.23	\$0.00	\$30.75
6	80	\$19.39	\$6.34	\$6.23	\$0.00	\$31.96
7	85	\$20.60	\$6.34	\$6.23	\$0.00	\$33.17
8	90	\$21.82	\$6.34	\$6.23	\$0.00	\$34.39

Notes:

Apprentice to Journeyworker Ratio:1:5

RIDE-ON MOTORIZED BUGGY OPERATOR <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75

For apprentice rates see "Apprentice- LABORER"

ROLLER/SPREADER/MULCHING MACHINE <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

ROOFER (Inc.Roofer Waterproofng &Roofer Damproofg) <i>ROOFERS LOCAL 33</i>	08/01/2015	\$40.11	\$11.00	\$12.00	\$0.00	\$63.11
	02/01/2016	\$41.01	\$11.00	\$12.00	\$0.00	\$64.01

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - ROOFER - Local 33

Effective Date - 08/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$20.06	\$11.00	\$3.38	\$0.00	\$34.44
2	60	\$24.07	\$11.00	\$12.00	\$0.00	\$47.07
3	65	\$26.07	\$11.00	\$12.00	\$0.00	\$49.07
4	75	\$30.08	\$11.00	\$12.00	\$0.00	\$53.08
5	85	\$34.09	\$11.00	\$12.00	\$0.00	\$57.09

Effective Date - 02/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$20.51	\$11.00	\$3.38	\$0.00	\$34.89
2	60	\$24.61	\$11.00	\$12.00	\$0.00	\$47.61
3	65	\$26.66	\$11.00	\$12.00	\$0.00	\$49.66
4	75	\$30.76	\$11.00	\$12.00	\$0.00	\$53.76
5	85	\$34.86	\$11.00	\$12.00	\$0.00	\$57.86

Notes: ** 1:5, 2:6-10, the 1:10; Reroofing: 1:4, then 1:1
 Step 1 is 2000 hrs.; Steps 2-5 are 1000 hrs.

Apprentice to Journeyworker Ratio:**

ROOFER SLATE / TILE / PRECAST CONCRETE	08/01/2015	\$40.36	\$11.00	\$12.00	\$0.00	\$63.36
ROOFERS LOCAL 33	02/01/2016	\$41.26	\$11.00	\$12.00	\$0.00	\$64.26
For apprentice rates see "Apprentice- ROOFER"						
SHEETMETAL WORKER	08/01/2015	\$43.31	\$10.20	\$21.48	\$2.25	\$77.24
SHEETMETAL WORKERS LOCAL 17 - A	02/01/2016	\$44.31	\$10.20	\$21.48	\$2.25	\$78.24
	08/01/2016	\$45.46	\$10.20	\$21.48	\$2.25	\$79.39
	02/01/2017	\$46.56	\$10.20	\$21.48	\$2.25	\$80.49
	08/01/2017	\$47.66	\$10.20	\$21.48	\$2.25	\$81.59
	02/01/2018	\$48.81	\$10.20	\$21.48	\$2.25	\$82.74

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - SHEET METAL WORKER - Local 17-A

Effective Date - 08/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$17.32	\$10.20	\$4.90	\$0.00	\$32.42
2	40	\$17.32	\$10.20	\$4.90	\$0.00	\$32.42
3	45	\$19.49	\$10.20	\$9.59	\$1.18	\$40.46
4	45	\$19.49	\$10.20	\$9.59	\$1.18	\$40.46
5	50	\$21.66	\$10.20	\$10.45	\$1.27	\$43.58
6	50	\$21.66	\$10.20	\$10.70	\$1.28	\$43.84
7	60	\$25.99	\$10.20	\$12.17	\$1.45	\$49.81
8	65	\$28.15	\$10.20	\$13.04	\$1.54	\$52.93
9	75	\$32.48	\$10.20	\$14.76	\$1.72	\$59.16
10	85	\$36.81	\$10.20	\$15.98	\$1.89	\$64.88

Effective Date - 02/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$17.72	\$10.20	\$4.90	\$0.00	\$32.82
2	40	\$17.72	\$10.20	\$4.90	\$0.00	\$32.82
3	45	\$19.94	\$10.20	\$9.59	\$1.19	\$40.92
4	45	\$19.94	\$10.20	\$9.59	\$1.19	\$40.92
5	50	\$22.16	\$10.20	\$10.45	\$1.28	\$44.09
6	50	\$22.16	\$10.20	\$10.70	\$1.29	\$44.35
7	60	\$26.59	\$10.20	\$12.17	\$1.47	\$50.43
8	65	\$28.80	\$10.20	\$13.04	\$1.56	\$53.60
9	75	\$33.23	\$10.20	\$14.76	\$1.75	\$59.94
10	85	\$37.66	\$10.20	\$15.98	\$1.92	\$65.76

Notes:
Steps are 6 mos.

Apprentice to Journeyworker Ratio:1:4

SIGN ERECTOR PAINTERS LOCAL 35 - ZONE 2	06/01/2013	\$25.81	\$7.07	\$7.05	\$0.00	\$39.93
--	------------	---------	--------	--------	--------	---------

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - SIGN ERECTOR - Local 35 Zone 2

Effective Date - 06/01/2013

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$12.91	\$7.07	\$0.00	\$0.00	\$19.98
2	55	\$14.20	\$7.07	\$2.45	\$0.00	\$23.72
3	60	\$15.49	\$7.07	\$2.45	\$0.00	\$25.01
4	65	\$16.78	\$7.07	\$2.45	\$0.00	\$26.30
5	70	\$18.07	\$7.07	\$7.05	\$0.00	\$32.19
6	75	\$19.36	\$7.07	\$7.05	\$0.00	\$33.48
7	80	\$20.65	\$7.07	\$7.05	\$0.00	\$34.77
8	85	\$21.94	\$7.07	\$7.05	\$0.00	\$36.06
9	90	\$23.23	\$7.07	\$7.05	\$0.00	\$37.35

Notes:
Steps are 4 mos.

Apprentice to Journeyworker Ratio:1:1

SPECIALIZED EARTH MOVING EQUIP < 35 TONS <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$31.94	\$10.41	\$9.33	\$0.00	\$51.68
	12/01/2015	\$31.94	\$10.41	\$10.08	\$0.00	\$52.43
	06/01/2016	\$32.44	\$10.41	\$10.08	\$0.00	\$52.93
	08/01/2016	\$32.44	\$10.91	\$10.08	\$0.00	\$53.43
	12/01/2016	\$32.44	\$10.91	\$10.89	\$0.00	\$54.24
SPECIALIZED EARTH MOVING EQUIP > 35 TONS <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$32.23	\$10.41	\$9.33	\$0.00	\$51.97
	12/01/2015	\$32.23	\$10.41	\$10.08	\$0.00	\$52.72
	06/01/2016	\$32.73	\$10.41	\$10.08	\$0.00	\$53.22
	08/01/2016	\$32.73	\$10.91	\$10.08	\$0.00	\$53.72
	12/01/2016	\$32.73	\$10.91	\$10.89	\$0.00	\$54.53
SPRINKLER FITTER <i>SPRINKLER FITTERS LOCAL 550 - (Section A) Zone 1</i>	10/01/2015	\$54.83	\$8.42	\$15.65	\$0.00	\$78.90
	01/01/2016	\$54.43	\$8.67	\$15.80	\$0.00	\$78.90
	03/01/2016	\$55.43	\$8.67	\$15.80	\$0.00	\$79.90
	10/01/2016	\$56.58	\$8.67	\$15.80	\$0.00	\$81.05
	03/01/2017	\$57.58	\$8.67	\$15.80	\$0.00	\$82.05

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - SPRINKLER FITTER - Local 550 (Section A) Zone 1

Effective Date - 10/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	35	\$19.19	\$8.42	\$8.40	\$0.00	\$36.01
2	40	\$21.93	\$8.42	\$8.40	\$0.00	\$38.75
3	45	\$24.67	\$8.42	\$8.40	\$0.00	\$41.49
4	50	\$27.42	\$8.42	\$8.40	\$0.00	\$44.24
5	55	\$30.16	\$8.42	\$8.40	\$0.00	\$46.98
6	60	\$32.90	\$8.42	\$8.40	\$0.00	\$49.72
7	65	\$35.64	\$8.42	\$8.40	\$0.00	\$52.46
8	70	\$38.38	\$8.42	\$8.40	\$0.00	\$55.20
9	75	\$41.12	\$8.42	\$8.40	\$0.00	\$57.94
10	80	\$43.86	\$8.42	\$8.40	\$0.00	\$60.68

Effective Date - 01/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	35	\$19.05	\$8.67	\$8.55	\$0.00	\$36.27
2	40	\$21.77	\$8.67	\$8.55	\$0.00	\$38.99
3	45	\$24.49	\$8.67	\$8.55	\$0.00	\$41.71
4	50	\$27.22	\$8.67	\$8.55	\$0.00	\$44.44
5	55	\$29.94	\$8.67	\$8.55	\$0.00	\$47.16
6	60	\$32.66	\$8.67	\$8.55	\$0.00	\$49.88
7	65	\$35.38	\$8.67	\$8.55	\$0.00	\$52.60
8	70	\$38.10	\$8.67	\$8.55	\$0.00	\$55.32
9	75	\$40.82	\$8.67	\$8.55	\$0.00	\$58.04
10	80	\$43.54	\$8.67	\$8.55	\$0.00	\$60.76

Notes: Apprentice entered prior 9/30/10:
40/45/50/55/60/65/70/75/80/85
Steps are 850 hours

Apprentice to Journeyworker Ratio:1:3

STEAM BOILER OPERATOR <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

TAMPERS, SELF-PROPELLED OR TRACTOR DRAWN <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
TELECOMMUNICATION TECHNICIAN <i>ELECTRICIANS LOCAL 103</i>	09/01/2015	\$34.25	\$13.00	\$14.06	\$0.00	\$61.31
	03/01/2016	\$34.63	\$13.00	\$14.55	\$0.00	\$62.18

Apprentice - TELECOMMUNICATION TECHNICIAN - Local 103

Effective Date - 09/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$13.70	\$13.00	\$0.41	\$0.00	\$27.11
2	40	\$13.70	\$13.00	\$0.41	\$0.00	\$27.11
3	45	\$15.41	\$13.00	\$11.03	\$0.00	\$39.44
4	45	\$15.41	\$13.00	\$11.03	\$0.00	\$39.44
5	50	\$17.13	\$13.00	\$11.30	\$0.00	\$41.43
6	55	\$18.84	\$13.00	\$11.58	\$0.00	\$43.42
7	60	\$20.55	\$13.00	\$11.86	\$0.00	\$45.41
8	65	\$22.26	\$13.00	\$12.13	\$0.00	\$47.39
9	70	\$23.98	\$13.00	\$12.41	\$0.00	\$49.39
10	75	\$25.69	\$13.00	\$12.68	\$0.00	\$51.37

Effective Date - 03/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	40	\$13.85	\$13.00	\$0.42	\$0.00	\$27.27
2	40	\$13.85	\$13.00	\$0.42	\$0.00	\$27.27
3	45	\$15.58	\$13.00	\$11.52	\$0.00	\$40.10
4	45	\$15.58	\$13.00	\$11.52	\$0.00	\$40.10
5	50	\$17.32	\$13.00	\$11.79	\$0.00	\$42.11
6	55	\$19.05	\$13.00	\$12.06	\$0.00	\$44.11
7	60	\$20.78	\$13.00	\$12.34	\$0.00	\$46.12
8	65	\$22.51	\$13.00	\$12.62	\$0.00	\$48.13
9	70	\$24.24	\$13.00	\$12.90	\$0.00	\$50.14
10	75	\$25.97	\$13.00	\$13.17	\$0.00	\$52.14

Notes:

Apprentice to Journeyworker Ratio:1:1

TERRAZZO FINISHERS <i>BRICKLAYERS LOCAL 3 - MARBLE & TILE</i>	08/01/2015	\$48.80	\$10.18	\$18.57	\$0.00	\$77.55
	02/01/2016	\$49.37	\$10.18	\$18.57	\$0.00	\$78.12
	08/01/2016	\$50.27	\$10.18	\$18.65	\$0.00	\$79.10
	02/01/2017	\$50.84	\$10.18	\$18.65	\$0.00	\$79.67

Classification

Effective Date Base Wage Health Pension Supplemental Unemployment Total Rate

Apprentice - TERRAZZO FINISHER - Local 3 Marble & Tile

Effective Date - 08/01/2015

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.40	\$10.18	\$18.57	\$0.00	\$53.15
2	60	\$29.28	\$10.18	\$18.57	\$0.00	\$58.03
3	70	\$34.16	\$10.18	\$18.57	\$0.00	\$62.91
4	80	\$39.04	\$10.18	\$18.57	\$0.00	\$67.79
5	90	\$43.92	\$10.18	\$18.57	\$0.00	\$72.67

Effective Date - 02/01/2016

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	50	\$24.69	\$10.18	\$18.57	\$0.00	\$53.44
2	60	\$29.62	\$10.18	\$18.57	\$0.00	\$58.37
3	70	\$34.56	\$10.18	\$18.57	\$0.00	\$63.31
4	80	\$39.50	\$10.18	\$18.57	\$0.00	\$68.25
5	90	\$44.43	\$10.18	\$18.57	\$0.00	\$73.18

Notes:

Apprentice to Journeyworker Ratio:1:3

TEST BORING DRILLER <i>LABORERS - FOUNDATION AND MARINE</i>	06/01/2015	\$36.45	\$7.30	\$13.40	\$0.00	\$57.15
	12/01/2015	\$37.20	\$7.30	\$13.40	\$0.00	\$57.90
	06/01/2016	\$37.95	\$7.30	\$13.40	\$0.00	\$58.65
	12/01/2016	\$38.95	\$7.30	\$13.40	\$0.00	\$59.65

For apprentice rates see "Apprentice- LABORER"

TEST BORING DRILLER HELPER <i>LABORERS - FOUNDATION AND MARINE</i>	06/01/2015	\$35.17	\$7.30	\$13.40	\$0.00	\$55.87
	12/01/2015	\$35.92	\$7.30	\$13.40	\$0.00	\$56.62
	06/01/2016	\$36.67	\$7.30	\$13.40	\$0.00	\$57.37
	12/01/2016	\$37.67	\$7.30	\$13.40	\$0.00	\$58.37

For apprentice rates see "Apprentice- LABORER"

TEST BORING LABORER <i>LABORERS - FOUNDATION AND MARINE</i>	06/01/2015	\$35.05	\$7.30	\$13.40	\$0.00	\$55.75
	12/01/2015	\$35.80	\$7.30	\$13.40	\$0.00	\$56.50
	06/01/2016	\$36.55	\$7.30	\$13.40	\$0.00	\$57.25
	12/01/2016	\$37.55	\$7.30	\$13.40	\$0.00	\$58.25

For apprentice rates see "Apprentice- LABORER"

TRACTORS/PORTABLE STEAM GENERATORS <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.42	\$10.00	\$14.55	\$0.00	\$66.97
	12/01/2015	\$43.66	\$10.00	\$14.55	\$0.00	\$68.21
	06/01/2016	\$44.41	\$10.00	\$14.55	\$0.00	\$68.96
	12/01/2016	\$45.64	\$10.00	\$14.55	\$0.00	\$70.19
	06/01/2017	\$46.63	\$10.00	\$14.55	\$0.00	\$71.18
	12/01/2017	\$47.62	\$10.00	\$14.55	\$0.00	\$72.17

For apprentice rates see "Apprentice- OPERATING ENGINEERS"

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
TRAILERS FOR EARTH MOVING EQUIPMENT <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$32.52	\$10.41	\$9.33	\$0.00	\$52.26
	12/01/2015	\$32.52	\$10.41	\$10.08	\$0.00	\$53.01
	06/01/2016	\$33.02	\$10.41	\$10.08	\$0.00	\$53.51
	08/01/2016	\$33.02	\$10.91	\$10.08	\$0.00	\$54.01
	12/01/2016	\$33.02	\$10.91	\$10.89	\$0.00	\$54.82
TUNNEL WORK - COMPRESSED AIR <i>LABORERS (COMPRESSED AIR)</i>	06/01/2015	\$47.33	\$7.30	\$13.80	\$0.00	\$68.43
	12/01/2015	\$48.08	\$7.30	\$13.80	\$0.00	\$69.18
	06/01/2016	\$48.83	\$7.30	\$13.80	\$0.00	\$69.93
	12/01/2016	\$49.83	\$7.30	\$13.80	\$0.00	\$70.93
For apprentice rates see "Apprentice- LABORER"						
TUNNEL WORK - COMPRESSED AIR (HAZ. WASTE) <i>LABORERS (COMPRESSED AIR)</i>	06/01/2015	\$49.33	\$7.30	\$13.80	\$0.00	\$70.43
	12/01/2015	\$50.08	\$7.30	\$13.80	\$0.00	\$71.18
	06/01/2016	\$50.83	\$7.30	\$13.80	\$0.00	\$71.93
	12/01/2016	\$51.83	\$7.30	\$13.80	\$0.00	\$72.93
For apprentice rates see "Apprentice- LABORER"						
TUNNEL WORK - FREE AIR <i>LABORERS (FREE AIR TUNNEL)</i>	06/01/2015	\$39.40	\$7.30	\$13.80	\$0.00	\$60.50
	12/01/2015	\$40.15	\$7.30	\$13.80	\$0.00	\$61.25
	06/01/2016	\$40.90	\$7.30	\$13.80	\$0.00	\$62.00
	12/01/2016	\$41.90	\$7.30	\$13.80	\$0.00	\$63.00
For apprentice rates see "Apprentice- LABORER"						
TUNNEL WORK - FREE AIR (HAZ. WASTE) <i>LABORERS (FREE AIR TUNNEL)</i>	06/01/2015	\$41.40	\$7.30	\$13.80	\$0.00	\$62.50
	12/01/2015	\$42.15	\$7.30	\$13.80	\$0.00	\$63.25
	06/01/2016	\$42.90	\$7.30	\$13.80	\$0.00	\$64.00
	12/01/2016	\$43.90	\$7.30	\$13.80	\$0.00	\$65.00
For apprentice rates see "Apprentice- LABORER"						
VAC-HAUL <i>TEAMSTERS JOINT COUNCIL NO. 10 ZONE B</i>	08/01/2015	\$31.94	\$10.41	\$9.33	\$0.00	\$51.68
	12/01/2015	\$31.94	\$10.41	\$10.08	\$0.00	\$52.43
	06/01/2016	\$32.44	\$10.41	\$10.08	\$0.00	\$52.93
	08/01/2016	\$32.44	\$10.91	\$10.08	\$0.00	\$53.43
	12/01/2016	\$32.44	\$10.91	\$10.89	\$0.00	\$54.24
WAGON DRILL OPERATOR <i>LABORERS - ZONE 2</i>	06/01/2015	\$31.40	\$7.30	\$12.30	\$0.00	\$51.00
	12/01/2015	\$31.90	\$7.30	\$12.30	\$0.00	\$51.50
	06/01/2016	\$32.40	\$7.30	\$12.30	\$0.00	\$52.00
	12/01/2016	\$33.15	\$7.30	\$12.30	\$0.00	\$52.75
For apprentice rates see "Apprentice- LABORER"						
WASTE WATER PUMP OPERATOR <i>OPERATING ENGINEERS LOCAL 4</i>	06/01/2015	\$42.83	\$10.00	\$14.55	\$0.00	\$67.38
	12/01/2015	\$44.08	\$10.00	\$14.55	\$0.00	\$68.63
	06/01/2016	\$44.83	\$10.00	\$14.55	\$0.00	\$69.38
	12/01/2016	\$46.08	\$10.00	\$14.55	\$0.00	\$70.63
	06/01/2017	\$47.08	\$10.00	\$14.55	\$0.00	\$71.63
	12/01/2017	\$48.08	\$10.00	\$14.55	\$0.00	\$72.63
For apprentice rates see "Apprentice- OPERATING ENGINEERS"						
WATER METER INSTALLER <i>PLUMBERS & GASFITTERS LOCAL 12</i>	09/01/2015	\$50.46	\$10.82	\$15.14	\$0.00	\$76.42
	03/01/2016	\$51.61	\$10.82	\$15.14	\$0.00	\$77.57
	09/01/2016	\$52.66	\$10.82	\$15.14	\$0.00	\$78.62
	03/01/2017	\$53.66	\$10.82	\$15.14	\$0.00	\$79.62
For apprentice rates see "Apprentice- PLUMBER/PIPEFITTER" or "PLUMBER/GASFITTER"						

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
Outside Electrical - East						
CABLE TECHNICIAN (Power Zone) <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$25.66	\$8.70	\$4.48	\$0.00	\$38.84
For apprentice rates see "Apprentice- LINEMAN"						
CABLEMAN (Underground Ducts & Cables) <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$36.55	\$8.70	\$6.58	\$0.00	\$51.83
For apprentice rates see "Apprentice- LINEMAN"						
DRIVER / GROUNDMAN CDL <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$29.94	\$8.70	\$6.05	\$0.00	\$44.69
For apprentice rates see "Apprentice- LINEMAN"						
DRIVER / GROUNDMAN -Inexperienced (<2000 Hrs) <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$23.52	\$8.70	\$5.24	\$0.00	\$37.46
For apprentice rates see "Apprentice- LINEMAN"						
EQUIPMENT OPERATOR (Class A CDL) <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$36.35	\$8.70	\$9.43	\$0.00	\$54.48
For apprentice rates see "Apprentice- LINEMAN"						
EQUIPMENT OPERATOR (Class B CDL) <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$32.08	\$8.70	\$6.59	\$0.00	\$47.37
For apprentice rates see "Apprentice- LINEMAN"						
GROUNDMAN <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$23.52	\$8.70	\$3.72	\$0.00	\$35.94
For apprentice rates see "Apprentice- LINEMAN"						
GROUNDMAN -Inexperienced (<2000 Hrs.) <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$19.25	\$8.70	\$2.85	\$0.00	\$30.80
For apprentice rates see "Apprentice- LINEMAN"						
JOURNEYMAN LINEMAN <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	09/01/2013	\$42.77	\$8.70	\$11.78	\$0.00	\$63.25

Apprentice - LINEMAN (Outside Electrical) - East Local 104

Effective Date - 09/01/2013

Step	percent	Apprentice Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
1	60	\$25.66	\$8.70	\$4.24	\$0.00	\$38.60
2	65	\$27.80	\$8.70	\$4.71	\$0.00	\$41.21
3	70	\$29.94	\$8.70	\$5.43	\$0.00	\$44.07
4	75	\$32.08	\$8.70	\$6.16	\$0.00	\$46.94
5	80	\$34.22	\$8.70	\$6.88	\$0.00	\$49.80
6	85	\$36.35	\$8.70	\$7.62	\$0.00	\$52.67
7	90	\$38.49	\$8.70	\$8.83	\$0.00	\$56.02

Notes:

Apprentice to Journeyworker Ratio:1:2

TELEDATA CABLE SPLICER <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	01/01/2015	\$28.12	\$4.25	\$3.09	\$0.00	\$35.46
	01/01/2016	\$28.98	\$4.25	\$3.12	\$0.00	\$36.35
TELEDATA LINEMAN/EQUIPMENT OPERATOR <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	01/01/2015	\$26.49	\$4.25	\$3.04	\$0.00	\$33.78
	01/01/2016	\$27.31	\$4.25	\$3.07	\$0.00	\$34.63
TELEDATA WIREMAN/INSTALLER/TECHNICIAN <i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	01/01/2015	\$26.49	\$4.25	\$3.04	\$0.00	\$33.78
	01/01/2016	\$27.31	\$4.25	\$3.07	\$0.00	\$34.63

Classification	Effective Date	Base Wage	Health	Pension	Supplemental Unemployment	Total Rate
TREE TRIMMER	02/01/2015	\$18.05	\$3.55	\$0.00	\$0.00	\$21.60
<i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	01/31/2016	\$18.51	\$3.55	\$0.00	\$0.00	\$22.06
This classification applies only to tree work done: (a) for a utility company, R.E.A. cooperative, or railroad or coal mining company, and (b) for the purpose of operating, maintaining, or repairing the utility company's equipment, and (c) by a person who is using hand or mechanical cutting methods and is not on the ground. This classification does not apply to wholesale tree removal.						
TREE TRIMMER GROUNDMAN	02/01/2015	\$15.92	\$3.55	\$0.00	\$0.00	\$19.47
<i>OUTSIDE ELECTRICAL WORKERS - EAST LOCAL 104</i>	01/31/2016	\$16.32	\$3.55	\$0.00	\$0.00	\$19.87
This classification applies only to tree work done: (a) for a utility company, R.E.A. cooperative, or railroad or coal mining company, and (b) for the purpose of operating, maintaining, or repairing the utility company's equipment, and (c) by a person who is using hand or mechanical cutting methods and is on the ground. This classification does not apply to wholesale tree removal.						

Additional Apprentice Information:

Minimum wage rates for apprentices employed on public works projects are listed above as a percentage of the pre-determined hourly wage rate established by the Commissioner under the provisions of the M.G.L. c. 149, ss. 26-27D. Apprentice ratios are established by the Division of Apprenticeship Training pursuant to M.G.L. c. 23, ss. 11E-11L.

All apprentices must be registered with the Division of Apprenticeship Training in accordance with M.G.L. c. 23, ss. 11E-11L.

All steps are six months (1000 hours.)

Ratios are expressed in allowable number of apprentices to journeymen or fraction thereof, unless otherwise specified.

** Multiple ratios are listed in the comment field.

*** APP to JM; 1:1, 2:2, 2:3, 3:4, 4:4, 4:5, 4:6, 5:7, 6:7, 6:8, 6:9, 7:10, 8:10, 8:11, 8:12, 9:13, 10:13, 10:14, etc.

**** APP to JM; 1:1, 1:2, 2:3, 2:4, 3:5, 4:6, 4:7, 5:8, 6:9, 6:10, 7:11, 8:12, 8:13, 9:14, 10:15, 10:16, etc.

"ATTACHMENT B"
[DRAFT Abatement Work Plan]

**Abatement Work Plan (AWP)
For The
Roofing Abatement Project
12 North Main Street
Westford, Massachusetts**

BACKGROUND:

The roof at 12 North Main Street has collapsed and roofing materials has fallen into the building. Refer to the attached photos. The Town of Westford would like to have the collapsed roofs removed to ease the weight on the building until the building is either renovated or demolished. As part of this phase, roofing flashing, pipe sealant and flooring materials (might be disturbed) would need to be removed. Not all suspect materials are intended to be removed during this phase of the project due to a very limited funding.

SAMPLING:

Bulk samples were previously collected from various materials suspected to contain asbestos. The following materials were found to contain asbestos:

Roofing materials flashing (90 LF);
Red poured flooring and adhesive (200 SF);
Brown flooring sheeting (800 SF);
Dark brown flooring sheeting (1,500 SF);
Roofing vents pipe sealant (20 LF).

Refer to the attached bulk sampling results.

SCOPE OF WORK AND ALTERNATIVE PROCEDURES:

The scope of work will include the removal and disposal of unknown quantities of the asbestos containing materials (ACM) roofing materials that might got intermixed with other building materials to be performed by bulk loading.

The following requirement listed in 310 CMR 7.15 could not be established or followed: 310 CMR 7.15, 7(C, D & E) for the following reasons:

- Containment could not be erected as the contaminated structure require the use of large equipments to demolish and dispose;
- A ventilation system could not be used as there is no possibility of erecting containment on top of the structure.

The Contractor will use sufficient amount of water to reduce any possibility of a fiber release or significant risk to public health. Continues on-site project monitoring will be performed at all points of each work area. Refer to Project Monitoring below.

PROJECT APPROACH:

Upon receipt of the MA DEP Waiver, the Contractor will mobilize materials, equipment and supplies to the site. All activities will be performed in accordance with all applicable local, state, and federal regulations governing asbestos abatement.

SCHEDULE:

Upon receipt of the MA DEP Waiver, the Contractor will mobilize materials, equipment, and supplies to the site. It is anticipated that removal will take approximately 3 weeks to complete.

PROJECT MONITORING:

During all abatement activities full time project monitoring including visual inspection and continuous air sampling will be performed at the perimeter of the work area by a Massachusetts licensed project monitor in accordance with the Environmental Protection Agency AHERA regulations. A minimum of six (6) monitoring stations will be performed. Refer to the attached plan for anticipated locations of air monitoring stations.

Air Monitoring will be performed by a Massachusetts licensed asbestos project monitor (Universal Environmental Consultants) and samples will be analyzed by Phase Contrast Microscopy (PCM) on site. Air monitoring stations (6) will be established around the perimeter of the regulated work area. Ambient air monitoring around the circumference of the work area will be performed on a continuous basis during all activities. Two (2) sets of air monitoring will be performed daily and results emailed or faxed to the DEP daily once the IH has access to a computer or a fax machine.

Analyses of the perimeter air samples will be performed immediately upon collection and results reported by the project monitor to the asbestos supervisor and facility owner within one (1) hour of collection, so that corrections in the work practices can be made immediately. If the air monitoring results exceed the Massachusetts Division of Occupational Safety's (DOS) clean air criteria of 0.010 f/cc, then all work will stop. The work methods will be evaluated by the project monitor, the Asbestos Site Supervisor and the demolition site supervisor prior to continuing any further work. DEP will be notified by telephone on that same day of the air monitoring exceedance and the updated emission control procedures. If the airborne fiber concentrations reach or exceed fifteen thousandths fibers per cubic centimeter (0.015-f/cc) of air, then work will stop and DEP will be notified of the exceedance by telephone within two (2) hours. All sample analyses will be performed by analysts, who are properly trained by holding a NIOSH Course 582 or 582 Equivalent Certification. The analyst will also be a successful participant in the American Industrial Hygiene Association's Asbestos Analytical Registry (AIHA's AAR), deemed "proficient" in the current round of the Proficiency Analytical Testing ("PAT") program or alternatively, be an employee of a laboratory, which holds a current and valid license issued by the DLS to perform such analysis, and said laboratory will also be accredited with either the AIHA or National Voluntary Laboratory Accreditation Program ("NVLAP").

All perimeter air samples will be collected in the general breathing zone, which for the purpose of this AWP, is located at a minimum of forty-eight inches (48") and a maximum of seventy-two inches (72") above the ground level. All samples will be collected utilizing high flow pumps and will be collected at a flow rate (8-12) LPM, with a minimum volume of 1,100 liters per sample.

No work pursuant to this AWP will commence unless the project monitor is at the Site and all air monitoring stations, both perimeter and employee monitoring, are in full operation.

Each of the contractors performing asbestos handling at the Site will perform employee air monitoring. This is not to be confused with OSHA personal monitoring requirements. Employee air monitoring will be performed by each contractor and subcontractor performing asbestos related work at the Site. At least one

in four workers, for each assigned job duty, will wear a personal air monitor. This includes supervisors, ground crew in the asbestos work area, and ground crew outside the asbestos work area, asbestos removers, and equipment operators. The employee air monitoring will be performed on a continuous basis during all phases of the work.

All employee air monitoring samples will be collected in the breathing zone, which for the purpose of this AWP, is located at a maximum of twelve inches (12") from the nose and mouth of each individual. Each sampling pump will be calibrated to operate at a flow rate of two and one-half (2.5) liters of air per minute. The device used to measure the flow rates for the employee monitoring samples will have been calibrated by a primary calibration device within six (6) months of utilization at the Site. A record of the calibration record for each of the measurement devices used at the Site will be kept at the Site by each contractor for the duration of the project and a copy of each calibration record will be submitted to DEP prior to commencing any work pursuant to this AWP, and will accompany the air monitoring data required below. Air filter cassettes will be changed periodically during each day's employee monitoring to prevent particulate overloading. Each air filter cassette will have the start and stop time and associated start and stop flow rates recorded in each contractor's Site logbook for review by DEP. Sample results of each filter cassette will be calculated and reported individually. Air monitoring series which repeatedly reveal samples that are overloaded with particulate and cannot be analyzed will be considered to be in noncompliance with the AWP, and potentially subject the facility, and their contractors and consultants, to enforcement action by DEP.

Analyses of the employee air samples will be performed daily by analysts who are properly trained by holding a NIOSH Course 582 or 582 Equivalent Certification. The analyst performing the analysis of the employee monitoring samples will also be a successful participant in the American Industrial Hygiene Association's Asbestos Analytical Registry (AIHA's AAR), deemed "proficient" in the current round of the Proficiency Analytical Testing ("PAT") program or alternatively, be an employee of a laboratory, which holds a current and valid license issued by the DLS to perform such analysis, and said laboratory will also be accredited with either the AIHA or National Voluntary Laboratory Accreditation Program ("NVLAP").

All employee air sampling analyses results will be reported, in writing, to the project monitor and property owner, on the morning following the date they were collected and before any work will be allowed to commence on every day other than the first day of operations. If the employee air monitoring results exceed the DLS clean air criterion of one - one hundredth fiber per cubic centimeter (0.010 f/cc) of air, then all activity at the Site will halt and DEP will be notified by telephone within one (1) hour of receipt of the results showing the exceedance in order to evaluate the work and to institute necessary changes in the work procedures.

Project monitoring reports will be emailed daily to the DEP.

The following work area activities will be performed to complete the abatement project. Refer to the attached site plans.

1. A wash area will be established within the vicinity of the work area. The wash area will consist of the installation of two layers of rubber flooring with the edges folded to eliminate the overflow of water and debris beyond the area. Collect water and debris for proper disposal. Wash and remove the

- rubber flooring upon completion of work. Location of the wash areas will be determined depending on access. Refer to site plan for anticipated location.
2. One regulated area will be established utilizing asbestos barrier tape and asbestos warning signs. A remote three stage decontamination chamber will be erected contiguous to the regulated area. The decontamination chamber will consist of three separate, adjacent rooms separated by curtained entrances, constructed in accordance with applicable regulations.
 3. Lined trucks with two layers of 10-mil poly liners sized to fit the vehicle and placarded on all four (4) sides (2212) will be used to load out debris from each regulated work area. The lined trucks will be placed on top of the wash area. The lined truck will be leak-tight sealable container in accordance with 310 CMR 7.15 (15).
 4. Trucks will be washed in the wash area along with tires of vehicle and water will be collected for proper disposal. Collection, handling and disposal of the water will be in accordance with 310 CMR 7.15(7) (f) for off-site disposal.
 5. All Laborers within the regulated work area will have the proper asbestos training & licensing and done the proper personal protective equipment (PPE.). Employees working inside the regulated areas will have current asbestos training certificates, medical clearance records, respiratory fit tests, and current Massachusetts asbestos licenses. Operators within the machinery will have Asbestos Awareness Training and will not leave the enclosed cab of the excavator within the regulated area.
 6. Personal OSHA Air Monitoring will be conducted during this operation, as required.
 7. Roofing/intermixed materials will be removed by heavy equipment with grapples and live loaded as ACM waste into the lined trucks. The lined trucks will be leak-tight sealable container in accordance with 310 CMR 7.15 (15). Once the trucks are loaded, the liners will be individually sealed utilizing duct tape and spray glue and labeled with proper asbestos warning labels and generator labels. The exterior of the trailers will be labeled on all sides with placards to properly identify the waste when transporting the material to an EPA certified landfill.
 8. While removing the ACM the contractor will utilize water as to wash each load hopefully to remove all ACM prior to loading into the lined trucks.
 9. The licensed asbestos supervisor and project monitor will perform a visual inspection of the work area.
 10. At the end of each work day, the project monitor along with the asbestos supervisor will perform a visual inspection for ACM debris that might be found during loading around the vicinity of each work area on the outside of the building. Should ACM was found the ACM will be placed into lined asbestos bags for proper disposal. The bags will comply with EPA NESHAP requirements related to thickness and also in accordance with 310 CMR 7.15 (15) and will be leak-tight with proper warning labels.
 11. Upon completion of the work a UEC licensed project monitor will perform a final visual inspection.
 12. All equipments will be decontaminated upon completion of entire project in the wash area. Collection, handling and disposal of the water will be in accordance with 310 CMR 7.15(7) (f) for off-site disposal.
 13. No stock piling >100 CY will be allowed. Any material stockpiled will be placed on poly and covered with poly with signs posted.
 14. DEP will be notified prior to start of work for pre-abatement inspection and for post-abatement inspection. The DEP will be given 24-48 hours prior to the beginning and ending of the project.
 15. Asbestos contaminated debris will be shipped to an approved landfill for disposal. Asbestos materials will be hauled by Red Technologies of Bloomfield, CT and disposed of at the Minerva Landfill in OH.

Tuesday, October 13, 2015


FORM AQ36:

Attached is a copy of the completed Form AQ36.




Ammar M. Dieb
Asbestos Designer
AD900326

12 North Main Street Westford

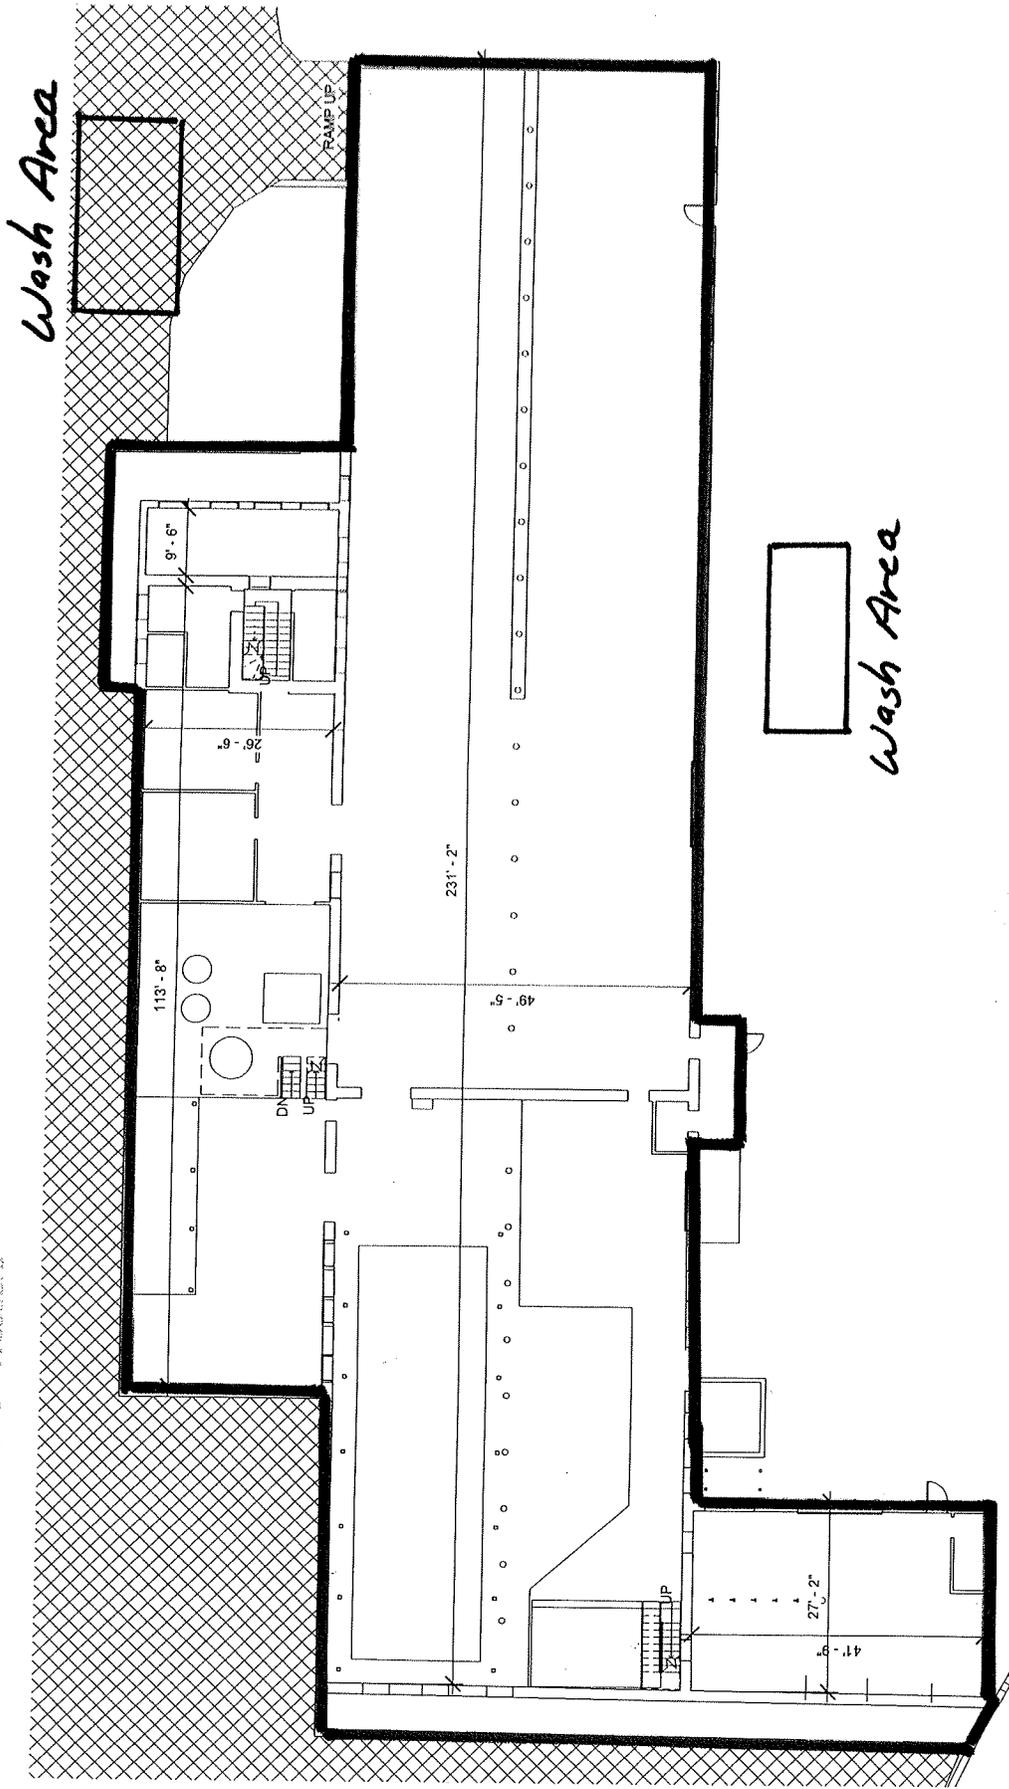

bhfa

12 North Main Street Westford

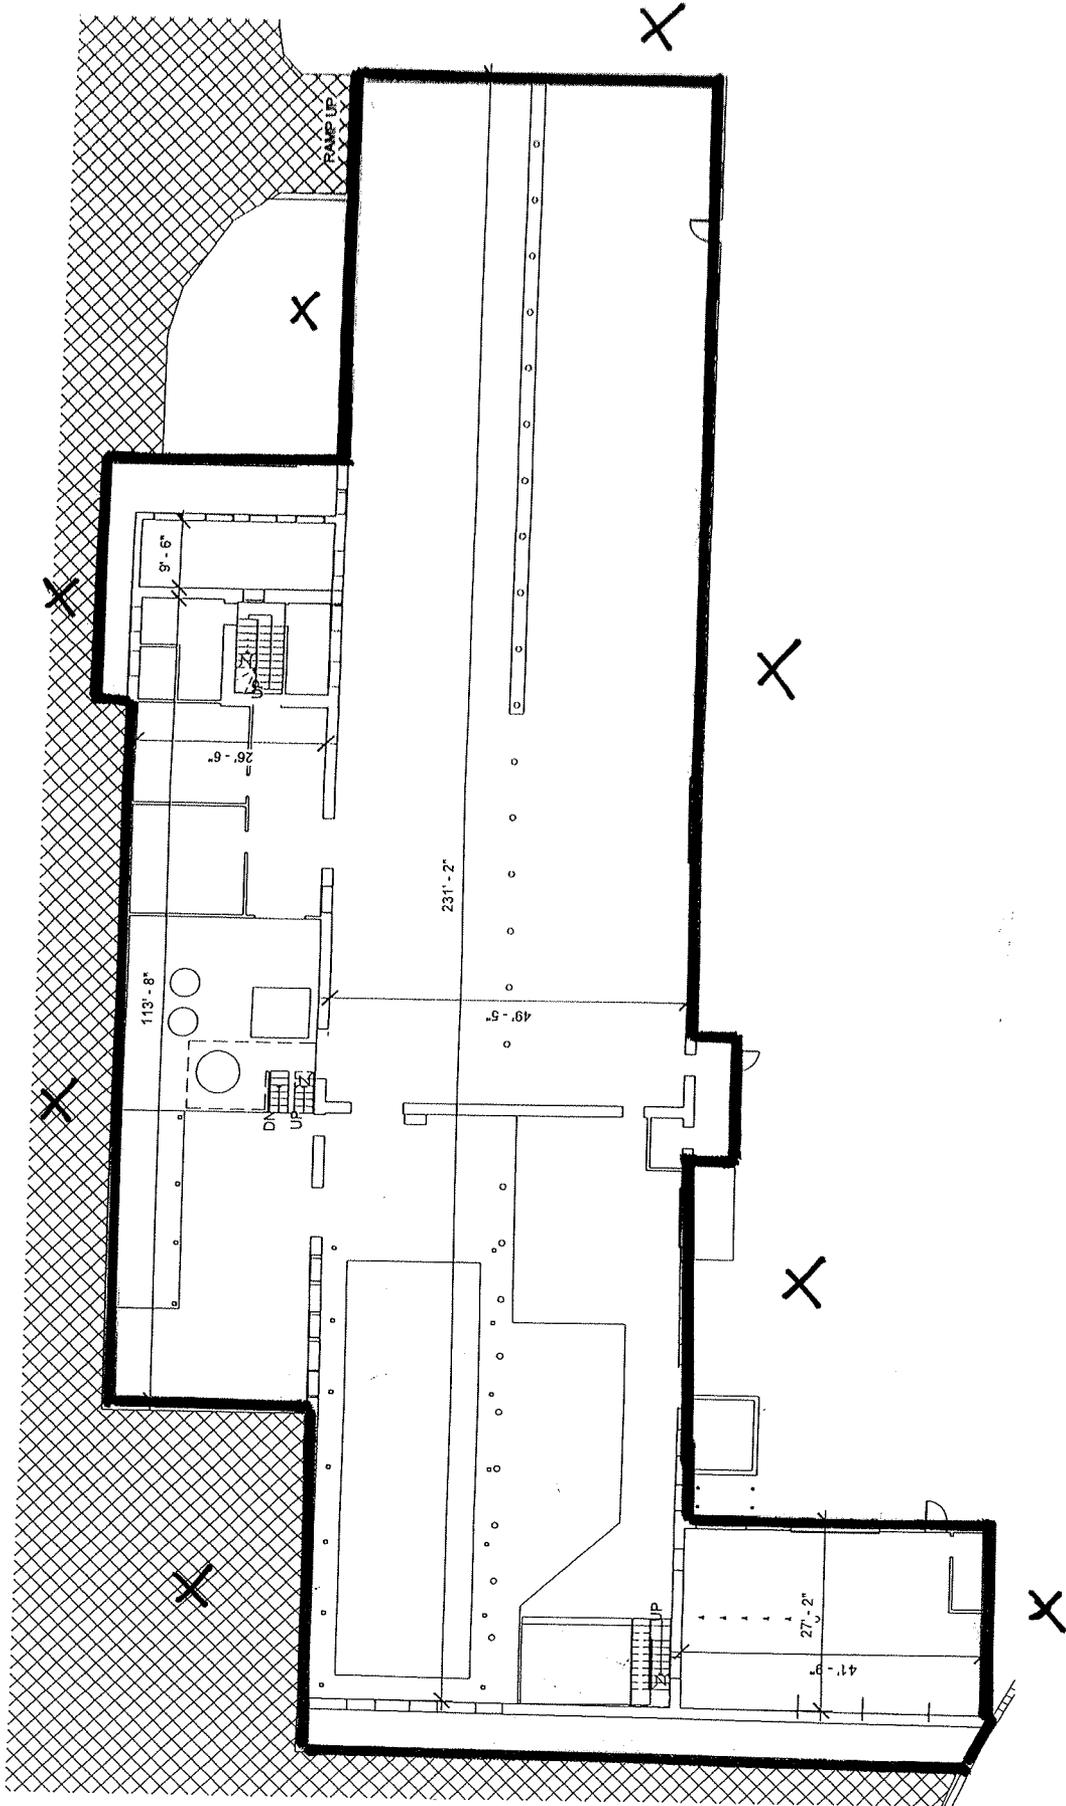

X: Air Sampling Stations

bhta



Massachusetts Department of Environmental Protection Bureau of Waste Prevention

BWP AQ 36 Application for Non-Traditional Asbestos Abatement Work Practice Approval

A. Work Site Information

Important:
When completing forms on a computer, use only the tab key to move your cursor - do not use the return key.



Facility

Vacant Industrial Building
Facility Name or Site Description

12 North Main Street
Facility Address

Westford
City/Town

MA
State

01886
ZIP Code

Owner

Town of Westford
Owner Name

55 Main Street
Owner Address

Westford
City/Town

MA
State

01886
ZIP Code

978-692-5501
Telephone Number

jmangiaratti@westfordma.gov
Email Address

Applicant - Check here if same as Owner and skip to next section. Otherwise, complete fields below.

Universal Environmental Consultants

Applicant Name

12 Brewster Road
Applicant Address

Framingham
City/Town

MA
State

01702
ZIP Code

508-628-5486
Telephone Number

adieb@uec-env.com
Email Address

B. Project Information

Asbestos Abatement Project Designer

Ammar M Dieb
Name

AD-900326

Department of Labor Standards (DLS) Contractor License Number

12 Brewster Road
Address

Framingham
City/Town

MA
State

01702
ZIP Code

508-628-5486
Telephone Number

adieb@uec-env.com
Email Address

Asbestos Abatement Contractor

Unknown

Contractor Name

Department of Labor Standards (DLS) Contractor License Number

Address

City/Town

State

ZIP Code

Telephone Number

Email Address



Massachusetts Department of Environmental Protection Bureau of Waste Prevention

BWP AQ 36 Application for Non-Traditional Asbestos Abatement Work Practice Approval

B. Project Information (continued)

Demolition Contractor (If Applicable)

Unknown

Address

City/Town

State

ZIP Code

Telephone Number

Email Address

Circumstances – Check the appropriate box(es) to indicate why a Non-Traditional Asbestos Abatement Work Practice Approval is needed.

- Facility is being demolished under a state or local government order because it is structurally unsound and in danger of imminent collapse. (Please attach a copy of the order to your work plan proposal.)
- Asbestos Containing Material (ACM) or Asbestos Containing Waste Material (ACWM) was not accessible for testing, therefore not discovered until after demolition began and, as a result, cannot be safely removed.
- Abatement activity is being conducted as part of an emergency renovation operation.
- Asbestos abatement activity is being conducted to clean up and decontaminate a facility or portion of a facility where:
 - Previous asbestos abatement activities were not conducted in compliance with 310 CMR 7.15.
 - ACM deterioration, if not immediately attended to, would present a safety or public health hazard.
- Wetting during a facility renovation would unavoidably damage equipment or present a safety hazard.
- The project requires bulk loading of ACM and/or ACWM.

List the requirements of 310 CMR 7.15 that you are unable to comply with and explain why:

Roofing and other building materials were found to contain asbestos. The roof has collapsed and requires removal. Not all suspect materials will be removed during this phase of the project as funding is very limited.

Other Project Details

Types & Amounts of ACM Requiring Non-Traditional Work Practice(s):

<input type="checkbox"/> Friable	_____	<input checked="" type="checkbox"/> Non-Friable	<u>50 CY</u>
	Quantity in Cubic Meters (Cubic Yards)		Quantity in Cubic Meters (Cubic Yards)

Location(s) of ACM in the Facility:

Roof and interior of building.



Massachusetts Department of Environmental Protection Bureau of Waste Prevention

BWP AQ 36 Application for Non-Traditional Asbestos Abatement Work Practice Approval

C. Certification

"I certify that I have personally examined the foregoing and am familiar with the information contained in this document and all attachments and that, based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including possible fines and imprisonment. I am aware that this permit application or notification shall not be deemed valid unless payment of the applicable fee is made."

Signature

Ammar Dieb

Printed Name

Project Designer

Title

10/13/2015

Date (MM/DD/YYYY)

D. Submission of Application

Note:
MassDEP review will begin only after your submissions have been received at both locations.

STEP 1: Submit Fee Payment

Send the materials below to the P.O. box address below to:

MassDEP
P.O. Box 4062
Boston, MA 02211

- A copy of this completed and signed form.
- Fee payment of \$600 (check or money order payable to "Commonwealth of Massachusetts").

The following entities are exempt from this fee:

- Cities, towns, counties or districts of the Commonwealth
- Federally recognized Indian tribe housing authorities
- Municipal housing authorities
- The Massachusetts Bay Transportation Authority (MBTA)

Entities that are exempt from the fee must still submit a copy of this completed and signed form, without payment, to the P.O. box above.

STEP 2: Submit Application

Send the following materials to the appropriate MassDEP Regional Office*, Attention: Asbestos Section:

- This original completed and signed form.
- A copy of the check or money order from Step 1.
- Your proposed work plan, describing work practices, duration and schedule. The proposal must:
 - Include signature of the Asbestos Project Designer who prepared it.
 - Demonstrate that the deviations from 310 CMR 7.15 and alternatives proposed will not cause any visible emissions to the outside air or pose significant risk to public health, safety or the environment.
- All supporting documentation.

*Find the MassDEP Regional Office for the community where this work will be done:

<http://www.mass.gov/eea/agencies/massdep/about/contacts/>



"ATTACHMENT C"
[Existing Conditions]

**TOWN OF WESTFORD,
MASSACHUSETTS**

**Phase 1 Building
Stabilization Project
12 North Main Street**

**EXISTING CONDITIONS OF
THE FORMER ABBOT
WORSTED MILL BUILDING
LOCATED AT 12 NORTH
MAIN STREET**

October 16, 2015

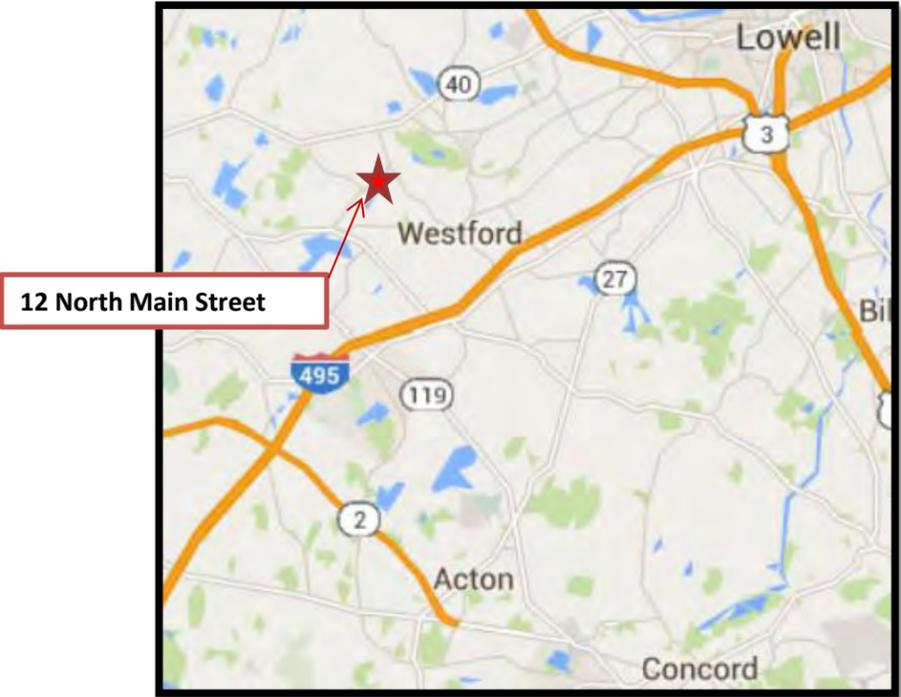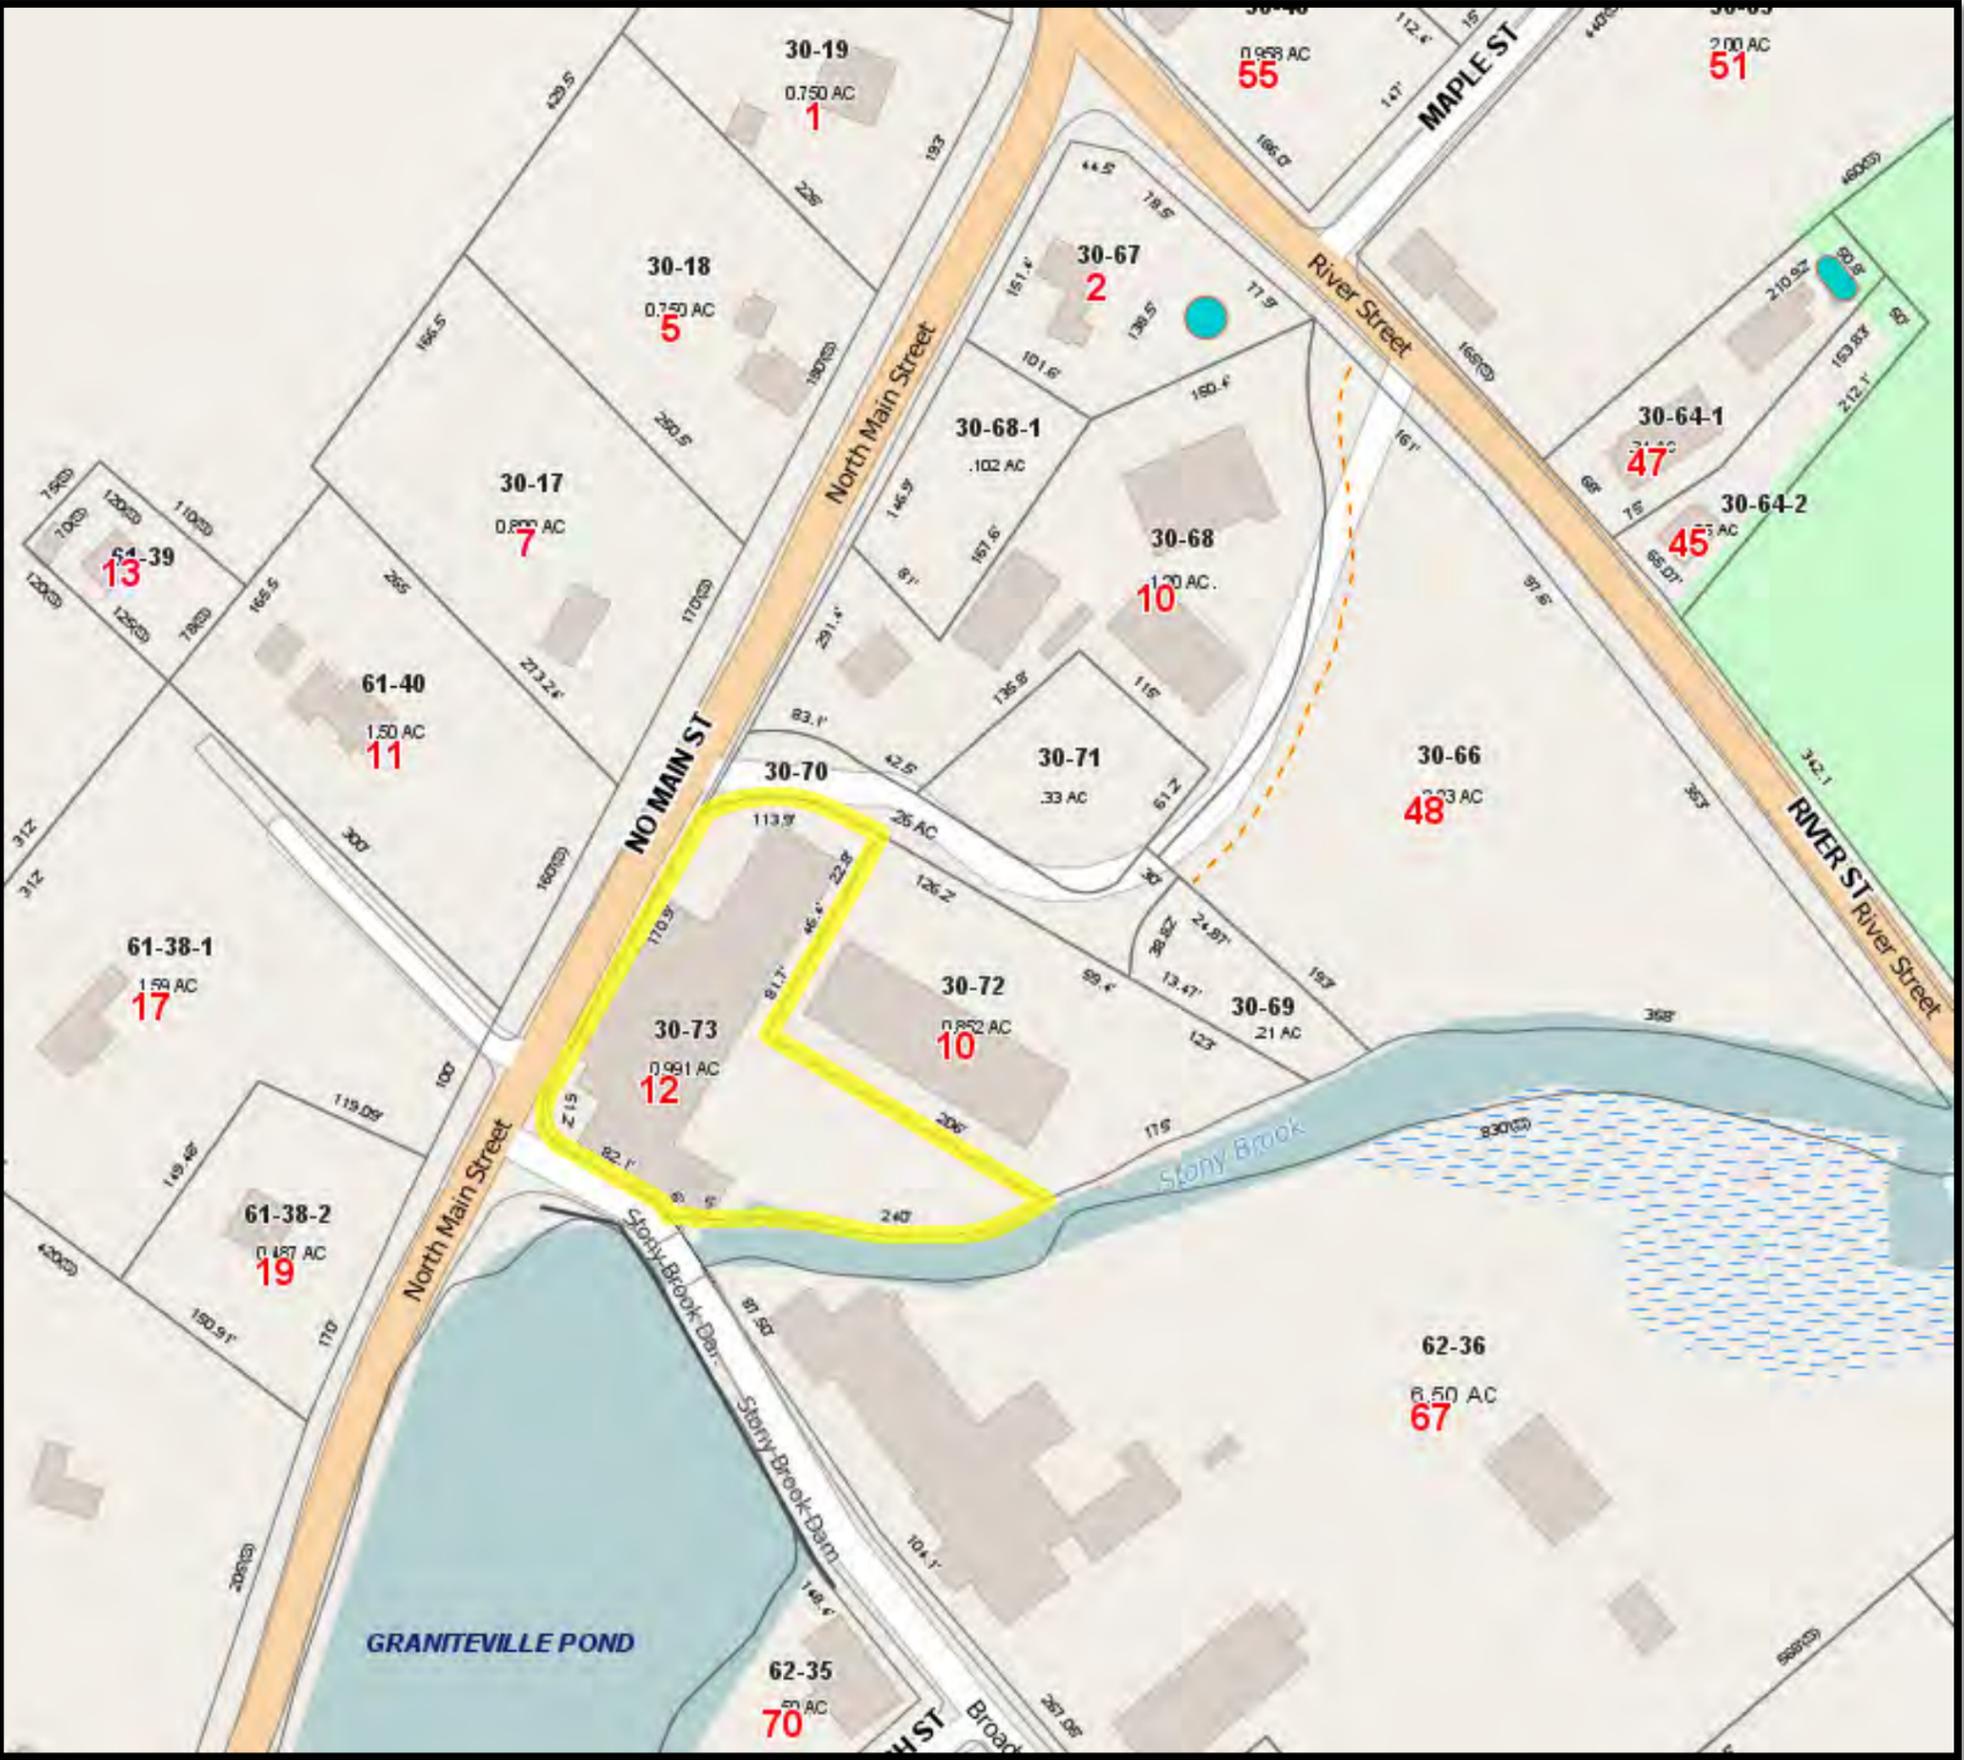

Westford GIS Map – 12 North Main Street Parcel Highlighted in Yellow




May 2015 Photograph




© 2014 Pictometry


April 2014 Photograph

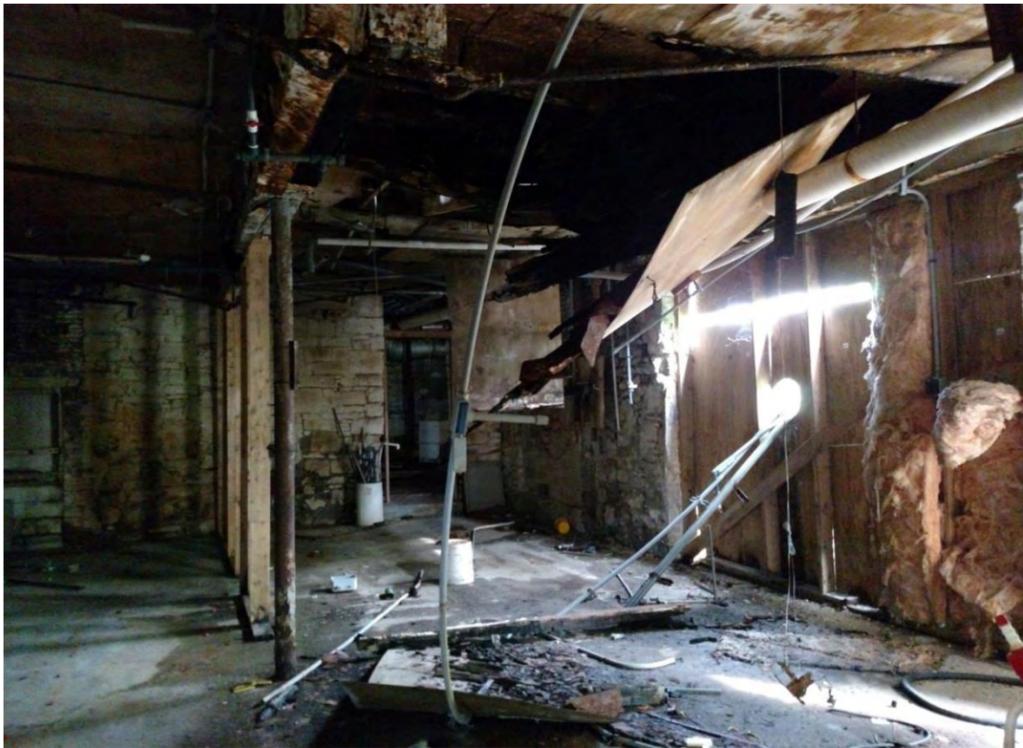

A (lower level)

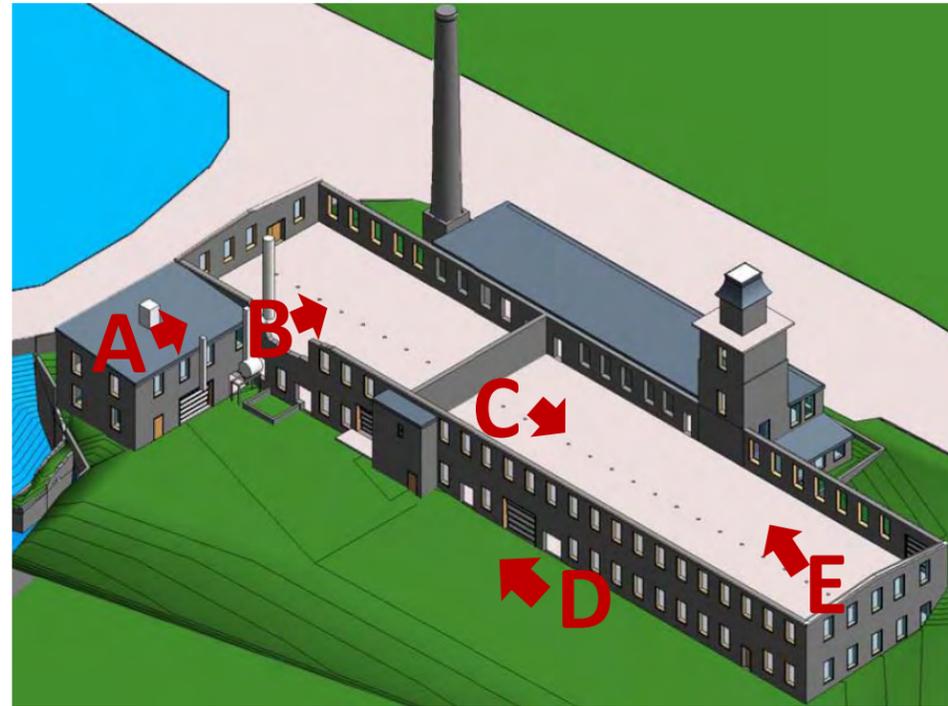

Index to Photographs (arrow indicates approximate direction of the photograph)

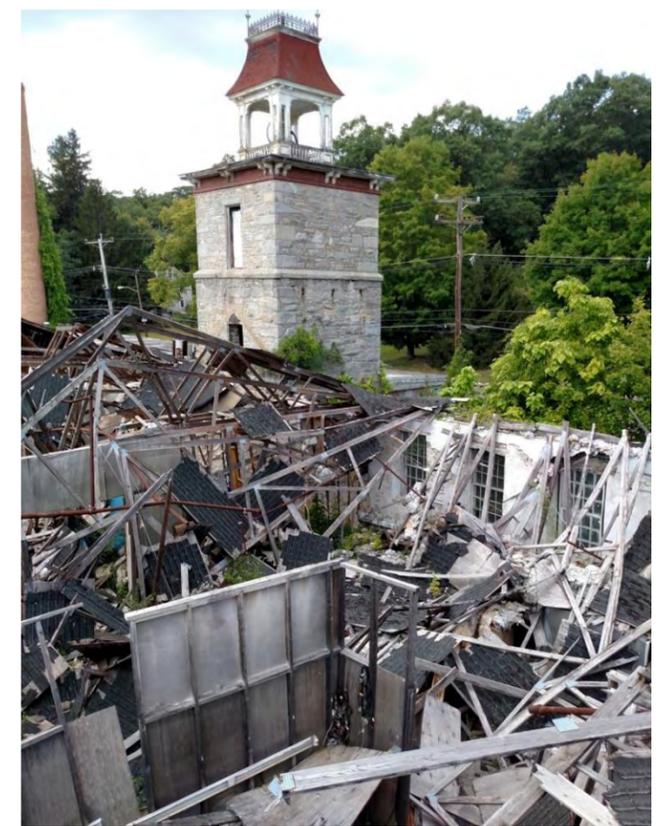


E (upper level)



B (lower level)




C (lower level)

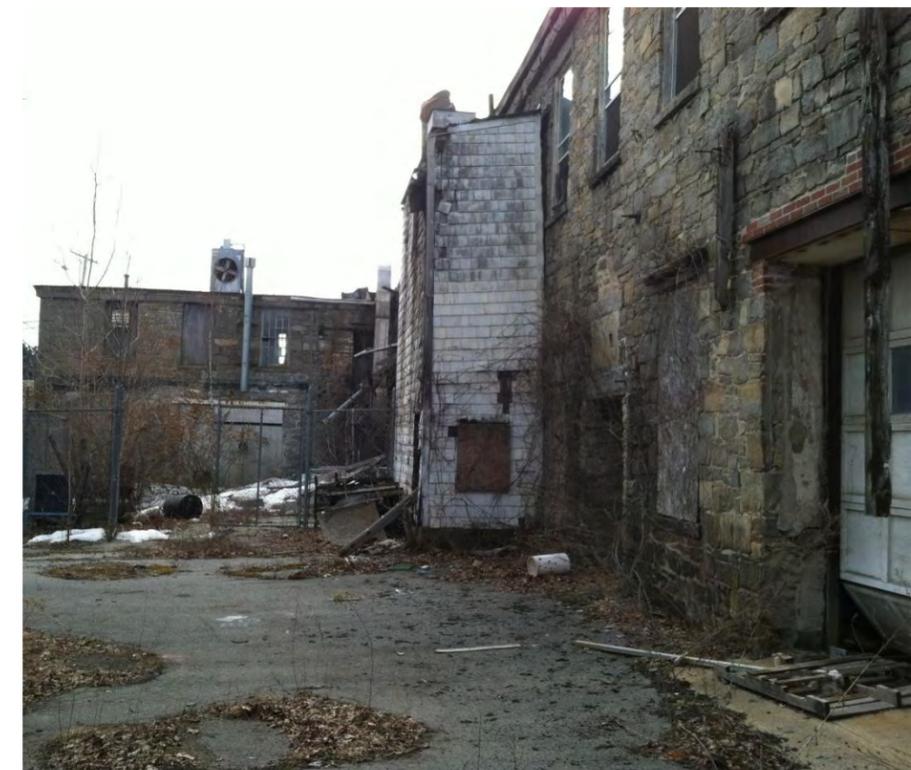

D (exterior)

DRAFT FLOOR PLAN OF LOWER LEVEL (BASEMENT)


12 North Main Street Westford

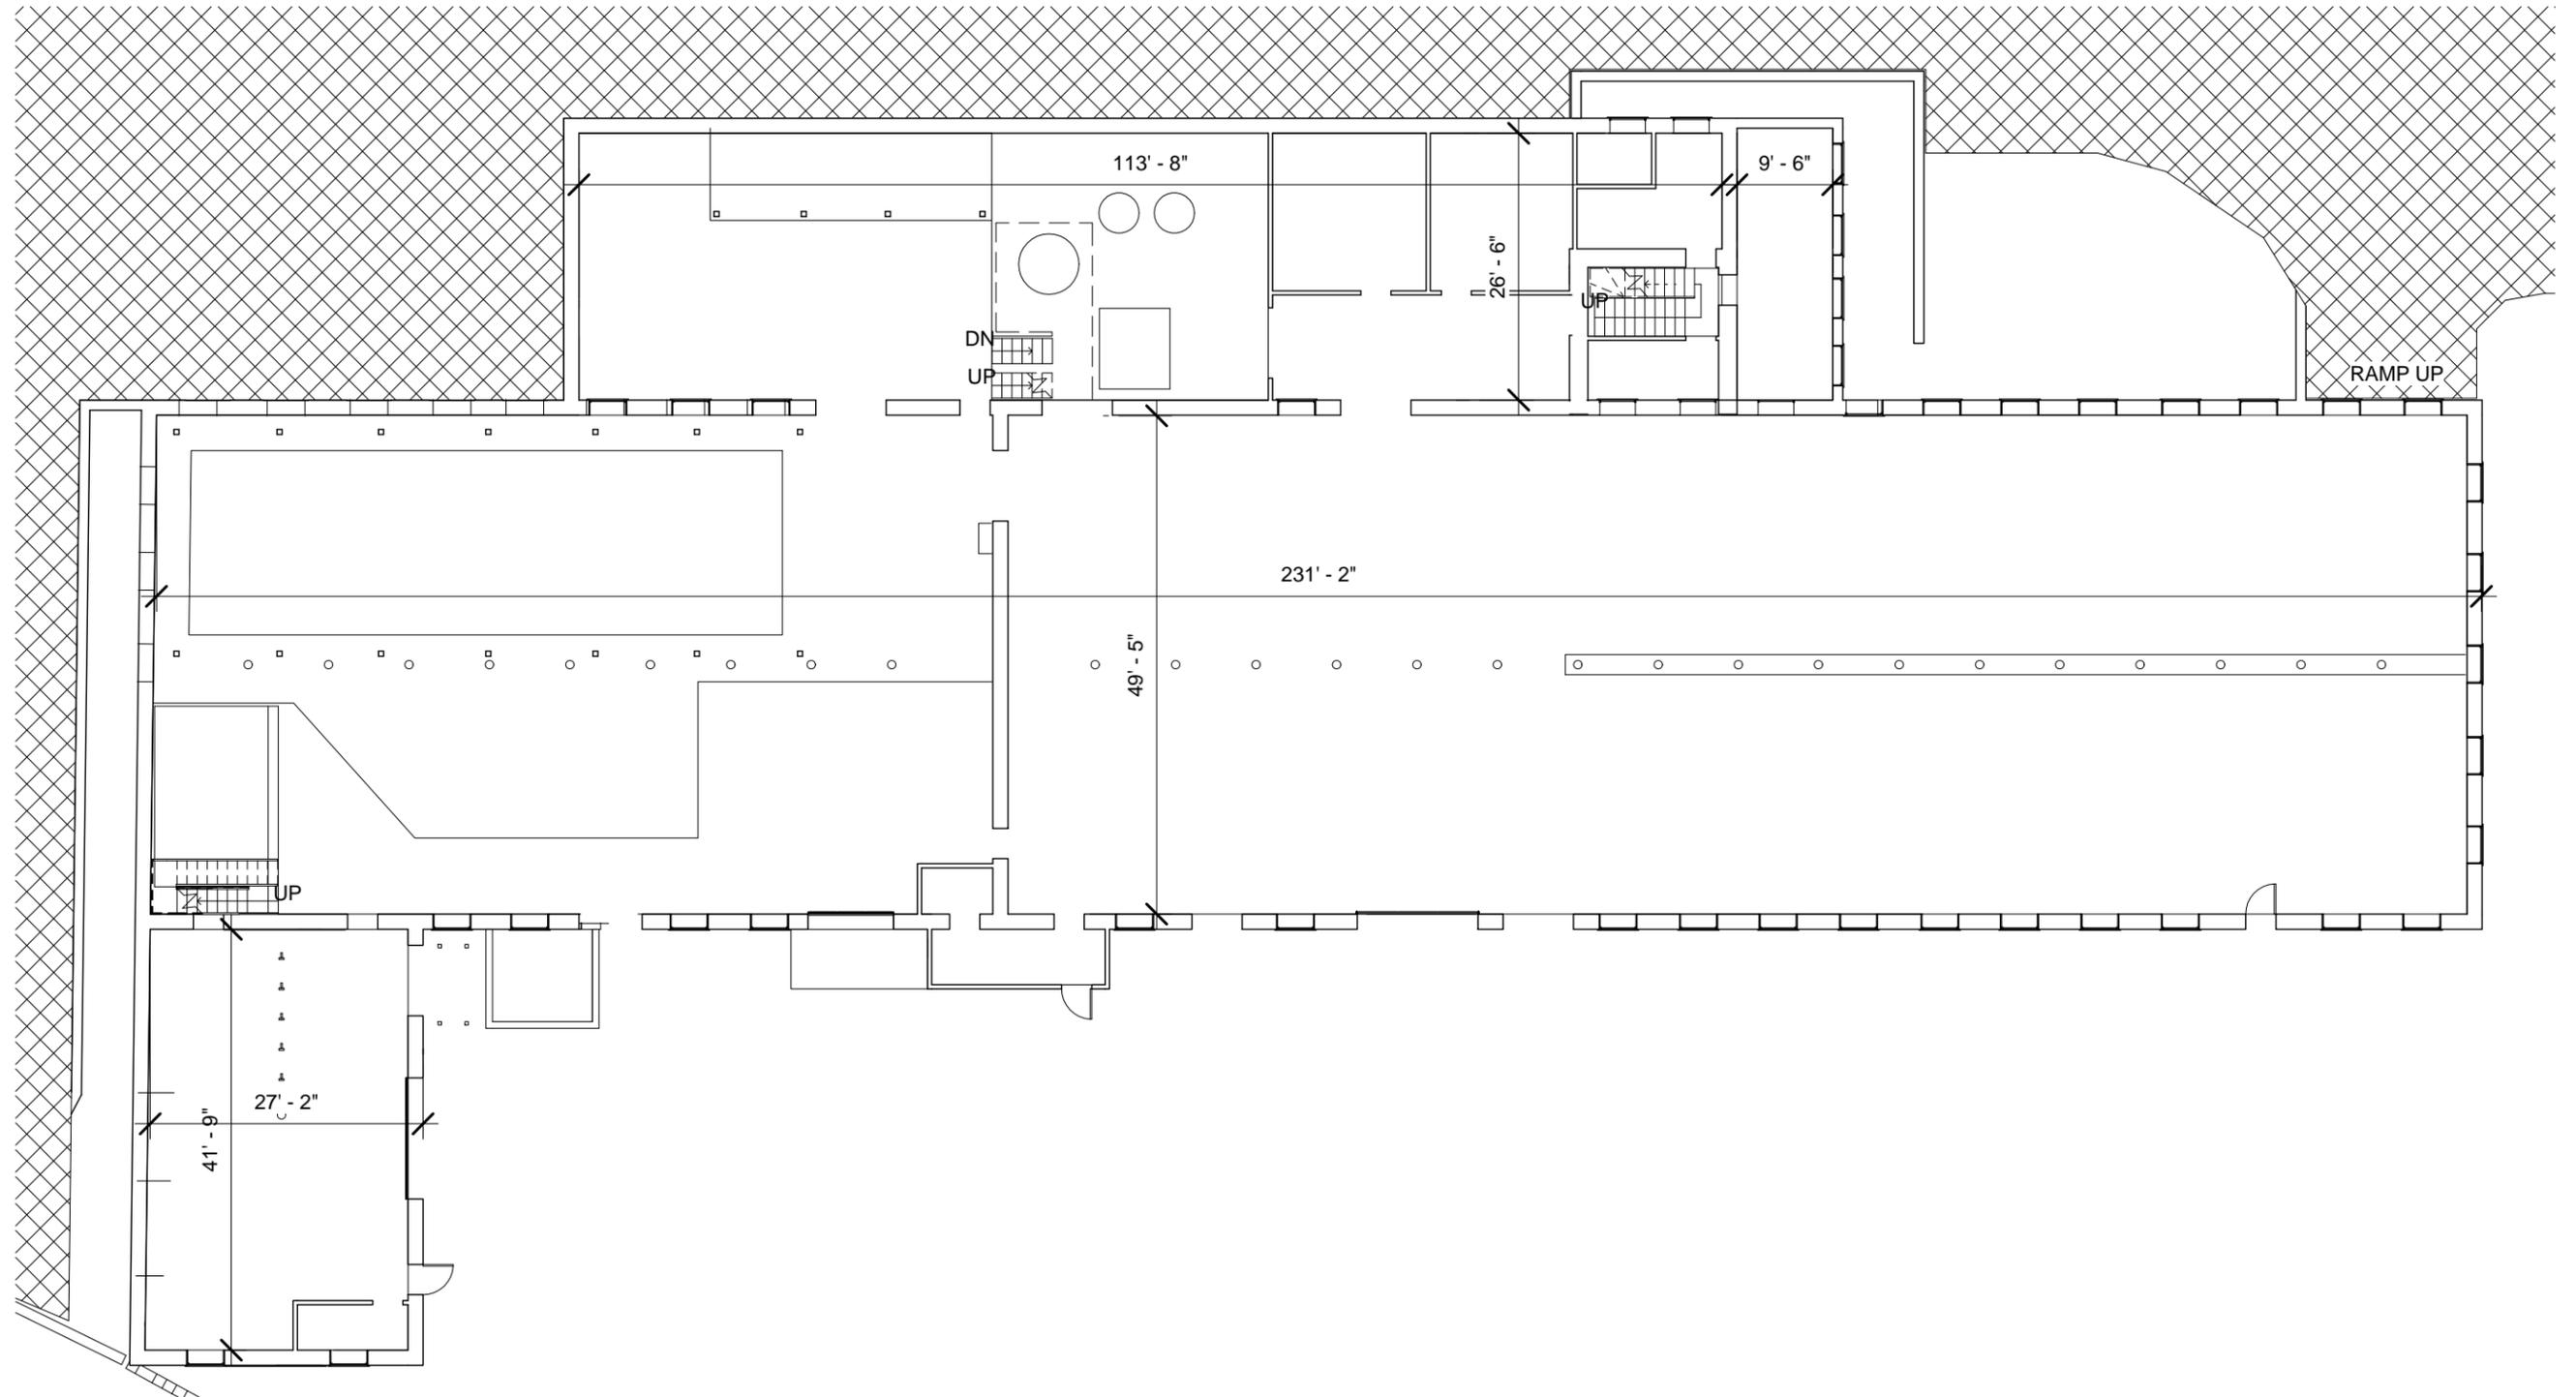

❖ STRUCTURAL ASSESSMENT (presented 9/24/2015)



❖ STRUCTURAL ASSESSMENT: NORTH WING

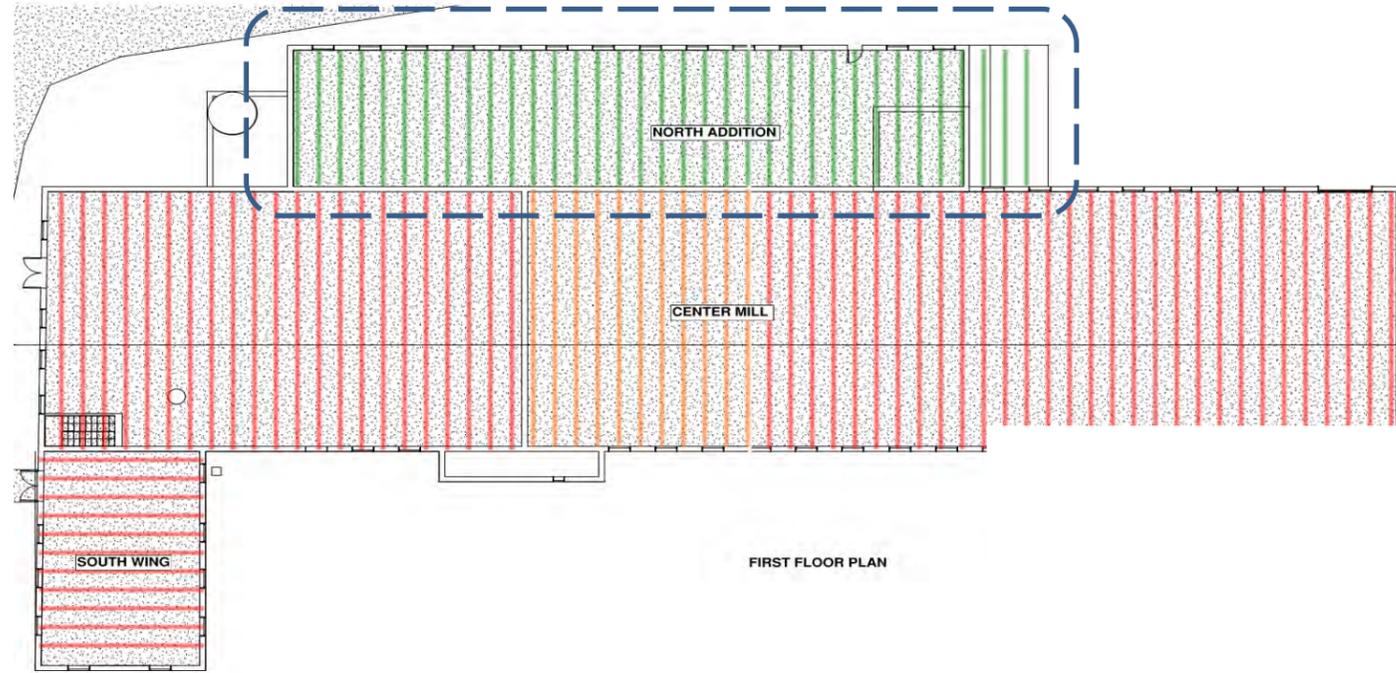


FIRST FLOOR




BASEMENT

❖ STRUCTURAL ASSESSMENT: MILLS #1 & #2

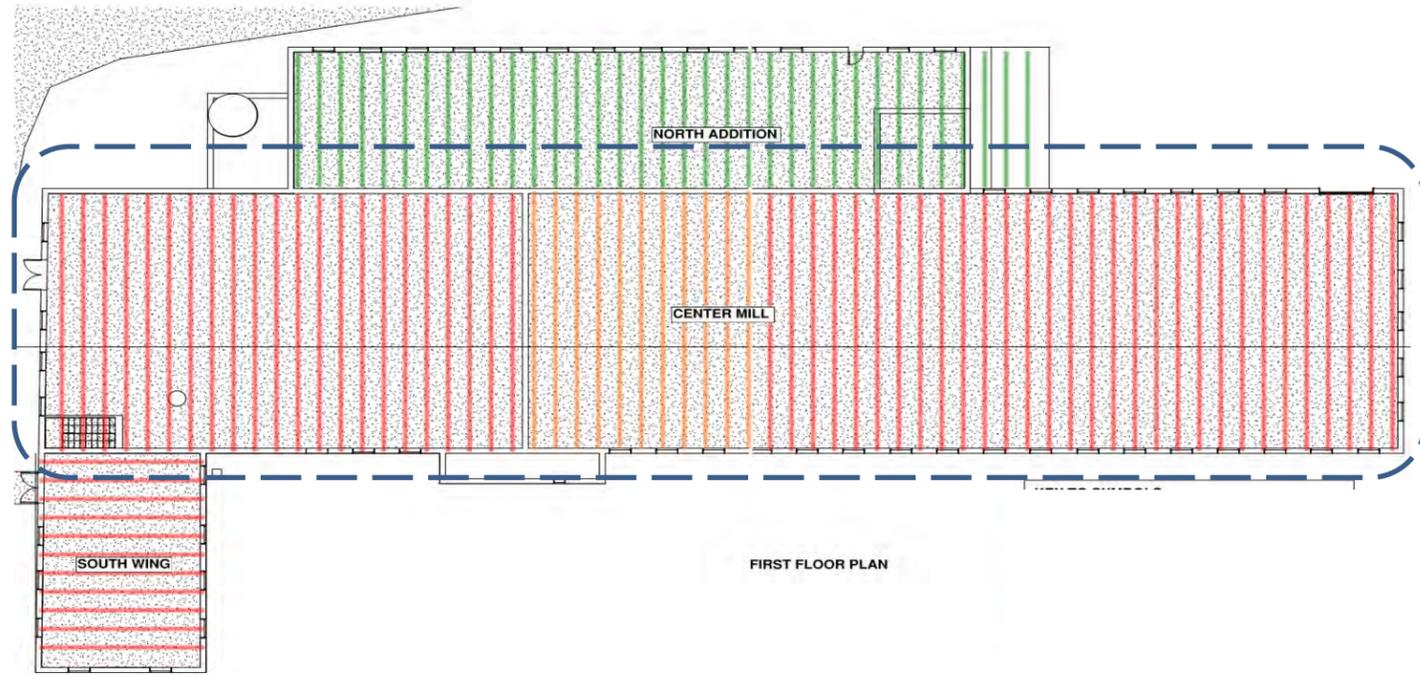

❖ STRUCTURAL ASSESSMENT: #3 (SOUTH ELL)

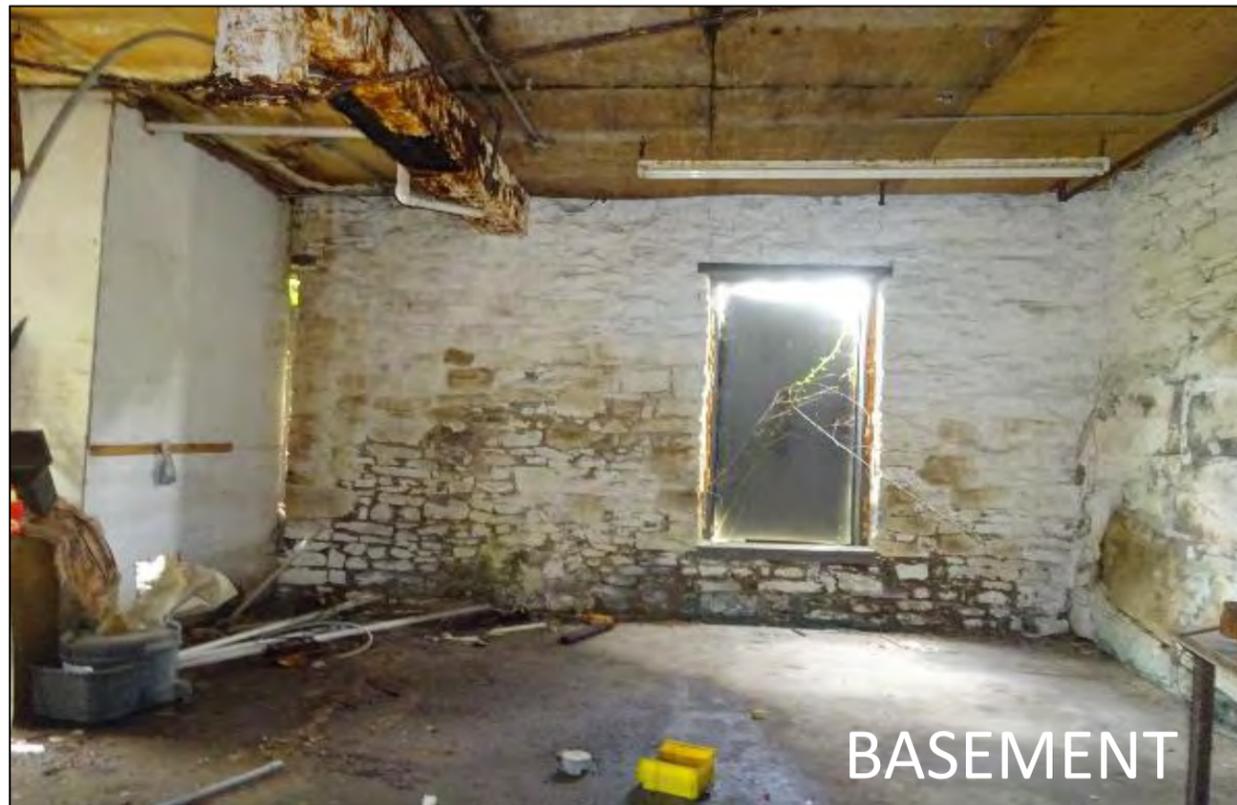

❖ STRUCTURAL ASSESSMENT: STACK

